



Appendix A


Contractor Certification Forms

Appendix B

Site Location/Drainage Area/Drainage Pattern Maps



SITE LOCATION MAP



CASELLA HAULING FACILITY SITE PLAN TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK



PROJ. NO: 1049.00
SCALE: NTS
DATE: 4/10/2026


CIVIL - TRANSPORTATION - ENVIRONMENTAL - LAND SURVEYING

FH1 - FALLING HEAD TEST 1 4' BELOW GRADE IN MEDIUM SAND	60 IN/HR
FH2 - FALLING HEAD TEST 2 4.5' BELOW GRADE IN TILL LAYER	5.75 IN/HR
FH3 - FALLING HEAD TEST 3 4' BELOW GRADE IN MEDIUM SAND	60 IN/HR

SOIL APPRAISAL							
DEEP HOLE OBSERVATIONS & PERCOLATION TESTING PERFORMED ON 9/23/2026 BY LANSING ENGINEERING							
MOREAU CASELLA TRUCK SHOP	TRIAL 1	TRIAL 2	TRIAL 3	TRIAL 4	TRIAL 5	TRIAL 6	TRIAL 7
PT1 - PERCOLATION TEST NO. 1	0:49 MIN./IN.	0:53 MIN./IN.	0:58 MIN./IN.	0:59 MIN./IN.	1:02 MIN./IN.		
PT2 - PERCOLATION TEST NO. 2	0:43 MIN./IN.	0:48 MIN./IN.	0:54 MIN./IN.	0:58 MIN./IN.	0:59 MIN./IN.	0:59 MIN./IN.	1:02 MIN./IN.
PT3 - PERCOLATION TEST NO. 3	0:46 MIN./IN.	0:51 MIN./IN.	0:57 MIN./IN.	1:03 MIN./IN.	1:07 MIN./IN.	1:10 MIN./IN.	
TP1 - TEST PIT NO. 1	0'-2" 2'-10.5' TOPSOIL MEDIUM BROWN SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP2 - TEST PIT NO. 2	0'-4" 4'-10.5' TOPSOIL MEDIUM/COARSE GRAY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP3 - TEST PIT NO. 3	0'-12" 12'-11' TOPSOIL MEDIUM/COARSE GRAY SAND		MOTTLING @ 132" NO GROUNDWATER OBSERVED				
TP4 - TEST PIT NO. 4	0'-12" 12'-4" TOPSOIL MEDIUM ORANGE SAND MED/COARSE GRAY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP5 - TEST PIT NO. 5	0'-1.5' 1.5'-7' TOPSOIL MEDIUM GRAY SAND SILTY HARD PACKED TILL		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP6 - TEST PIT NO. 6	0'-12" 12'-5.75' LOAMY TOPSOIL MEDIUM GRAY SAND HARD PACKED FINE SAND/TILL		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP7 - TEST PIT NO. 7	0'-12" 12'-7.25' TOPSOIL MEDIUM GRAY SAND PACKED FINE SAND/TILL		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP8 - TEST PIT NO. 8	0'-6" 6'-8.5' TOPSOIL FINE/MEDIUM GRAY SAND PACKED FINE SAND/TILL		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP9 - TEST PIT NO. 9	0'-12" 12'-7' LOAMY TOPSOIL FINE/MEDIUM GRAY SAND PACKED FINE SILTY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP10 - TEST PIT NO. 10	0'-12" 12'-7.75' LOAMY TOPSOIL FINE/MEDIUM GRAY SAND FINE PACKED SILTY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				

DESIGN POINT 1

EXISTING CONDITIONS PLAN



LEGEND	
	SUBCATCHMENT BOUNDARY
	FLOW PATH
	PROPERTY LINE
	SOIL TYPE BOUNDARY
	PROJECT BOUNDARY
	EXISTING TREELINE
	SUBCATCHMENT BOUNDARY
	SIZE (ACRES) CURVE NUMBER

CASELLA - FORT EDWARD HAULING FACILITY SITE PLAN

1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK

LANSING ENGINEERING


PRELIMINARY / NOT FOR CONSTRUCTION

CIVIL/TRANSPORTATION/ENVIRONMENTAL/LAND SURVEYING

EXISTING CONDITIONS PLAN





EC-1

1 OF 2



Appendix C

Pre-Development and Post-Development Run-off Calculations



Routing Diagram for Existing Conditions

Prepared by Lansing Engineering PC, Printed 10/8/2026
HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Existing Conditions

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 2

Rainfall Events Listing (selected events)

Event#	Event Name	Storm Type	Curve	Mode	Duration (hours)	B/B	Depth (inches)	AMC
1	1-yr	NY-Moreau 24-hr S1	1-yr	Default	24.00	1	2.24	2
2	10-yr	NY-Moreau 24-hr S1	10-yr	Default	24.00	1	3.72	2
3	25-yr	NY-Moreau 24-hr S1	25-yr	Default	24.00	1	4.58	2
4	100-yr	NY-Moreau 24-hr S1	100-yr	Default	24.00	1	6.26	2

Existing Conditions

NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 3

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN

Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1:

Runoff Area=26.950 ac 2.41% Impervious Runoff Depth=0.00"

Flow Length=1,100' Tc=17.8 min CN=42 Runoff=0.00 cfs 0.000 af

Reach DP1:

Inflow=0.00 cfs 0.000 af

Outflow=0.00 cfs 0.000 af

Total Runoff Area = 26.950 ac Runoff Volume = 0.000 af Average Runoff Depth = 0.00"
97.59% Pervious = 26.300 ac 2.41% Impervious = 0.650 ac

Existing Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Printed 10/8/2026

Page 4

Summary for Subcatchment 1:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Area (ac)	CN	Description
16.360	36	Woods, Fair, HSG A
9.940	49	Pasture/grassland/range, Fair, HSG A
* 0.650	98	
26.950	42	Weighted Average
26.300		97.59% Pervious Area
0.650		2.41% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
7.3	100	0.0400	0.23		Sheet Flow, Range n= 0.130 P2= 2.60"
4.6	503	0.0670	1.81		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
5.9	497	0.0800	1.41		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Summary for Reach DP1:

Inflow Area = 26.950 ac, 2.41% Impervious, Inflow Depth = 0.00" for 1-yr event
 Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
 Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Existing Conditions

NY-Moreau 24-hr S1 10-yr Rainfall=3.72"

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 5

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN

Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1:

Runoff Area=26.950 ac 2.41% Impervious Runoff Depth>0.04"

Flow Length=1,100' Tc=17.8 min CN=42 Runoff=0.17 cfs 0.086 af

Reach DP1:

Inflow=0.17 cfs 0.086 af

Outflow=0.17 cfs 0.086 af

Total Runoff Area = 26.950 ac Runoff Volume = 0.086 af Average Runoff Depth = 0.04"
97.59% Pervious = 26.300 ac 2.41% Impervious = 0.650 ac

Existing Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 10-yr Rainfall=3.72"

Printed 10/8/2026

Page 6

Summary for Subcatchment 1:

Runoff = 0.17 cfs @ 16.86 hrs, Volume= 0.086 af, Depth> 0.04"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 10-yr Rainfall=3.72"

Area (ac)	CN	Description
16.360	36	Woods, Fair, HSG A
9.940	49	Pasture/grassland/range, Fair, HSG A
* 0.650	98	
26.950	42	Weighted Average
26.300		97.59% Pervious Area
0.650		2.41% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
7.3	100	0.0400	0.23		Sheet Flow, Range n= 0.130 P2= 2.60"
4.6	503	0.0670	1.81		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
5.9	497	0.0800	1.41		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Summary for Reach DP1:

Inflow Area = 26.950 ac, 2.41% Impervious, Inflow Depth > 0.04" for 10-yr event
 Inflow = 0.17 cfs @ 16.86 hrs, Volume= 0.086 af
 Outflow = 0.17 cfs @ 16.86 hrs, Volume= 0.086 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Existing Conditions

NY-Moreau 24-hr S1 25-yr Rainfall=4.58"

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 7

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN

Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1:

Runoff Area=26.950 ac 2.41% Impervious Runoff Depth>0.16"

Flow Length=1,100' Tc=17.8 min CN=42 Runoff=1.30 cfs 0.355 af

Reach DP1:

Inflow=1.30 cfs 0.355 af

Outflow=1.30 cfs 0.355 af

Total Runoff Area = 26.950 ac Runoff Volume = 0.355 af Average Runoff Depth = 0.16"
97.59% Pervious = 26.300 ac 2.41% Impervious = 0.650 ac

Existing Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 25-yr Rainfall=4.58"

Printed 10/8/2026

Page 8

Summary for Subcatchment 1:

Runoff = 1.30 cfs @ 12.65 hrs, Volume= 0.355 af, Depth> 0.16"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 25-yr Rainfall=4.58"

Area (ac)	CN	Description
16.360	36	Woods, Fair, HSG A
9.940	49	Pasture/grassland/range, Fair, HSG A
* 0.650	98	
26.950	42	Weighted Average
26.300		97.59% Pervious Area
0.650		2.41% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
7.3	100	0.0400	0.23		Sheet Flow, Range n= 0.130 P2= 2.60"
4.6	503	0.0670	1.81		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
5.9	497	0.0800	1.41		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Summary for Reach DP1:

Inflow Area = 26.950 ac, 2.41% Impervious, Inflow Depth > 0.16" for 25-yr event
 Inflow = 1.30 cfs @ 12.65 hrs, Volume= 0.355 af
 Outflow = 1.30 cfs @ 12.65 hrs, Volume= 0.355 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Existing Conditions

NY-Moreau 24-hr S1 100-yr Rainfall=6.26"

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 9

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN

Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1:

Runoff Area=26.950 ac 2.41% Impervious Runoff Depth>0.59"

Flow Length=1,100' Tc=17.8 min CN=42 Runoff=8.57 cfs 1.316 af

Reach DP1:

Inflow=8.57 cfs 1.316 af

Outflow=8.57 cfs 1.316 af

Total Runoff Area = 26.950 ac Runoff Volume = 1.316 af Average Runoff Depth = 0.59"
97.59% Pervious = 26.300 ac 2.41% Impervious = 0.650 ac

Existing Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 100-yr Rainfall=6.26"

Printed 10/8/2026

Page 10

Summary for Subcatchment 1:

Runoff = 8.57 cfs @ 12.42 hrs, Volume= 1.316 af, Depth> 0.59"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 100-yr Rainfall=6.26"




Area (ac)	CN	Description
16.360	36	Woods, Fair, HSG A
9.940	49	Pasture/grassland/range, Fair, HSG A
* 0.650	98	
26.950	42	Weighted Average
26.300		97.59% Pervious Area
0.650		2.41% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
7.3	100	0.0400	0.23		Sheet Flow, Range n= 0.130 P2= 2.60"
4.6	503	0.0670	1.81		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
5.9	497	0.0800	1.41		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Summary for Reach DP1:

Inflow Area = 26.950 ac, 2.41% Impervious, Inflow Depth > 0.59" for 100-yr event
 Inflow = 8.57 cfs @ 12.42 hrs, Volume= 1.316 af
 Outflow = 8.57 cfs @ 12.42 hrs, Volume= 1.316 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

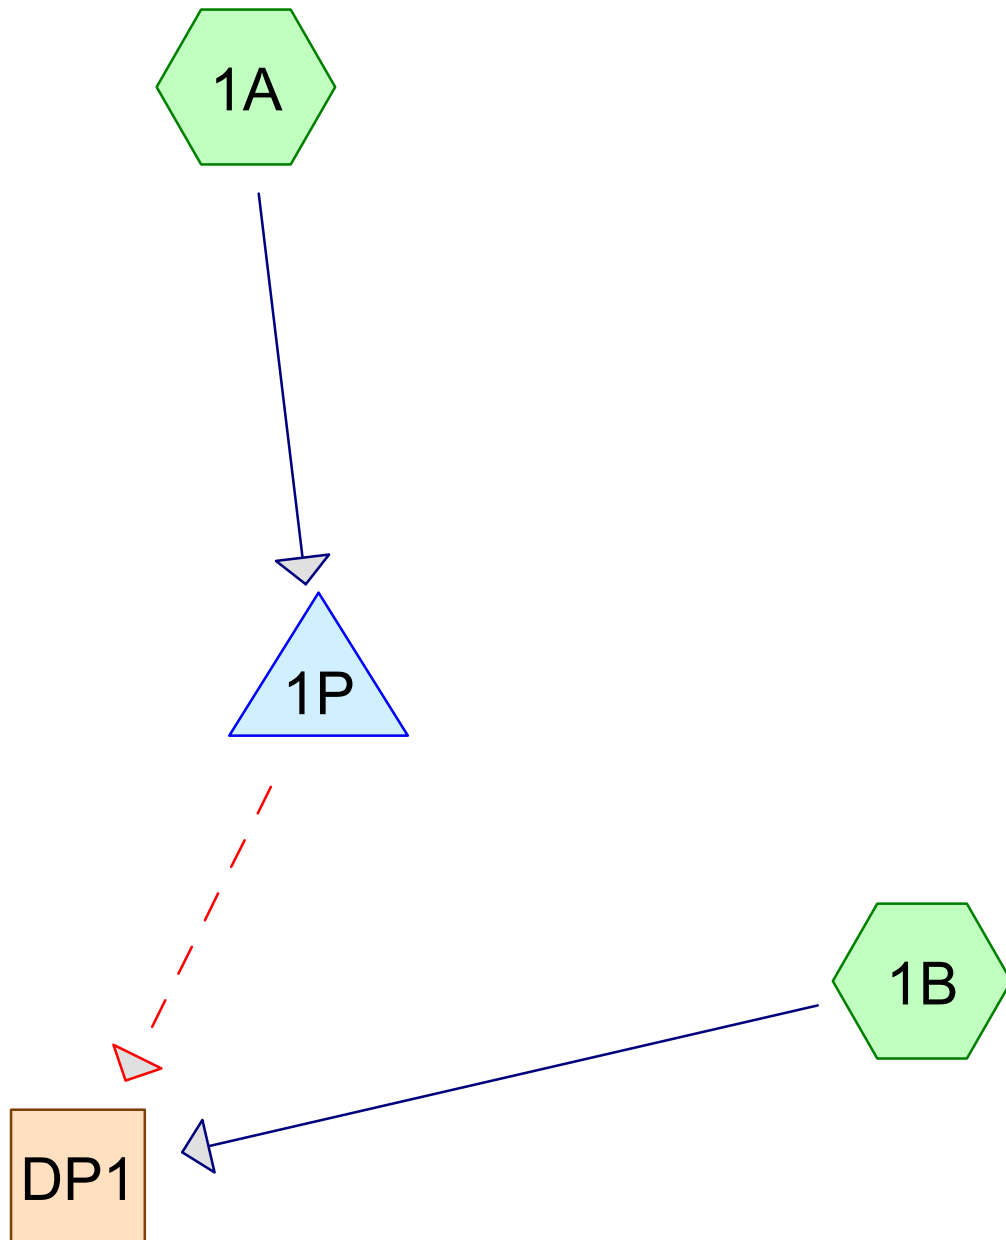

Proposed Conditions

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 2

Rainfall Events Listing (selected events)

Event#	Event Name	Storm Type	Curve	Mode	Duration (hours)	B/B	Depth (inches)	AMC
1	1-yr	NY-Moreau 24-hr S1	1-yr	Default	24.00	1	2.24	2
2	10-yr	NY-Moreau 24-hr S1	10-yr	Default	24.00	1	3.72	2
3	25-yr	NY-Moreau 24-hr S1	25-yr	Default	24.00	1	4.58	2
4	100-yr	NY-Moreau 24-hr S1	100-yr	Default	24.00	1	6.26	2

Proposed Conditions

NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 3

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1A:

Runoff Area=14.520 ac 46.69% Impervious Runoff Depth>0.21"
Flow Length=1,167' Tc=16.3 min CN=67 Runoff=1.50 cfs 0.250 af

Subcatchment1B:

Runoff Area=12.430 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=1,100' Tc=17.8 min CN=37 Runoff=0.00 cfs 0.000 af

Reach DP1:

Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Pond 1P:

Peak Elev=358.06' Storage=891 cf Inflow=1.50 cfs 0.250 af
Discarded=1.21 cfs 0.246 af Secondary=0.00 cfs 0.000 af Outflow=1.21 cfs 0.246 af

Total Runoff Area = 26.950 ac Runoff Volume = 0.250 af Average Runoff Depth = 0.11"
74.84% Pervious = 20.170 ac 25.16% Impervious = 6.780 ac

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Printed 10/8/2026

Page 4

Summary for Subcatchment 1A:

Runoff = 1.50 cfs @ 12.30 hrs, Volume= 0.250 af, Depth> 0.21"
 Routed to Pond 1P :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Area (ac)	CN	Description
* 6.780	98	
7.740	39	>75% Grass cover, Good, HSG A
14.520	67	Weighted Average
7.740		53.31% Pervious Area
6.780		46.69% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.0	100	0.0400	0.14		Sheet Flow, Grass: Dense n= 0.240 P2= 2.60"
2.0	239	0.0830	2.02		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
2.3	828	0.0100	5.94	10.50	Pipe Channel, CMP_Round 18" 18.0" Round Area= 1.8 sf Perim= 4.7' r= 0.38' n= 0.013
16.3	1,167	Total			

Summary for Subcatchment 1B:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Area (ac)	CN	Description
1.100	39	>75% Grass cover, Good, HSG A
10.900	36	Woods, Fair, HSG A
0.430	49	Pasture/grassland/range, Fair, HSG A
12.430	37	Weighted Average
12.430		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.60"
4.1	1,000	0.6700	4.09		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 1-yr Rainfall=2.24"

Printed 10/8/2026

Page 5

Summary for Reach DP1:

Inflow Area = 12.430 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P:

Inflow Area = 14.520 ac, 46.69% Impervious, Inflow Depth > 0.21" for 1-yr event
Inflow = 1.50 cfs @ 12.30 hrs, Volume= 0.250 af
Outflow = 1.21 cfs @ 12.59 hrs, Volume= 0.246 af, Atten= 20%, Lag= 17.4 min
Discarded = 1.21 cfs @ 12.59 hrs, Volume= 0.246 af
Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Routed to Reach DP1 :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
Peak Elev= 358.06' @ 12.59 hrs Surf.Area= 15,649 sf Storage= 891 cf

Plug-Flow detention time= 12.2 min calculated for 0.245 af (98% of inflow)
Center-of-Mass det. time= 8.1 min (894.0 - 885.8)

Volume	Invert	Avail.Storage	Storage Description
#1	358.00'	142,613 cf	Custom Stage Data (Prismatic) Listed below (Recalc)

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
358.00	15,523	0	0
360.00	19,946	35,469	35,469
362.00	24,775	44,721	80,190
364.00	37,648	62,423	142,613

Device	Routing	Invert	Outlet Devices
#1	Discarded	358.00'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	363.00'	8.0' long x 12.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.57 2.62 2.70 2.67 2.66 2.67 2.66 2.64

Discarded OutFlow Max=1.27 cfs @ 12.59 hrs HW=358.06' (Free Discharge)
↑**1=Exfiltration** (Exfiltration Controls 1.27 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=358.00' (Free Discharge)
↑**2=Broad-Crested Rectangular Weir** (Controls 0.00 cfs)

Proposed Conditions*NY-Moreau 24-hr S1 10-yr Rainfall=3.72"*

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 6

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1A:

Runoff Area=14.520 ac 46.69% Impervious Runoff Depth>0.85"
Flow Length=1,167' Tc=16.3 min CN=67 Runoff=11.13 cfs 1.034 af

Subcatchment1B:

Runoff Area=12.430 ac 0.00% Impervious Runoff Depth>0.00"
Flow Length=1,100' Tc=17.8 min CN=37 Runoff=0.01 cfs 0.001 af

Reach DP1:

Inflow=0.01 cfs 0.001 af
Outflow=0.01 cfs 0.001 af

Pond 1P:

Peak Elev=359.12' Storage=18,790 cf Inflow=11.13 cfs 1.034 af
Discarded=1.46 cfs 0.942 af Secondary=0.00 cfs 0.000 af Outflow=1.46 cfs 0.942 af

Total Runoff Area = 26.950 ac Runoff Volume = 1.034 af Average Runoff Depth = 0.46"
74.84% Pervious = 20.170 ac 25.16% Impervious = 6.780 ac

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 10-yr Rainfall=3.72"

Printed 10/8/2026

Page 7

Summary for Subcatchment 1A:

Runoff = 11.13 cfs @ 12.21 hrs, Volume= 1.034 af, Depth> 0.85"
 Routed to Pond 1P :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 10-yr Rainfall=3.72"

Area (ac)	CN	Description
* 6.780	98	
7.740	39	>75% Grass cover, Good, HSG A
14.520	67	Weighted Average
7.740		53.31% Pervious Area
6.780		46.69% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.0	100	0.0400	0.14		Sheet Flow, Grass: Dense n= 0.240 P2= 2.60"
2.0	239	0.0830	2.02		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
2.3	828	0.0100	5.94	10.50	Pipe Channel, CMP_Round 18" 18.0" Round Area= 1.8 sf Perim= 4.7' r= 0.38' n= 0.013
16.3	1,167	Total			

Summary for Subcatchment 1B:

Runoff = 0.01 cfs @ 20.00 hrs, Volume= 0.001 af, Depth> 0.00"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 10-yr Rainfall=3.72"

Area (ac)	CN	Description
1.100	39	>75% Grass cover, Good, HSG A
10.900	36	Woods, Fair, HSG A
0.430	49	Pasture/grassland/range, Fair, HSG A
12.430	37	Weighted Average
12.430		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.60"
4.1	1,000	0.6700	4.09		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 10-yr Rainfall=3.72"

Printed 10/8/2026

Page 8

Summary for Reach DP1:

Inflow Area = 12.430 ac, 0.00% Impervious, Inflow Depth > 0.00" for 10-yr event
Inflow = 0.01 cfs @ 20.00 hrs, Volume= 0.001 af
Outflow = 0.01 cfs @ 20.00 hrs, Volume= 0.001 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P:

Inflow Area = 14.520 ac, 46.69% Impervious, Inflow Depth > 0.85" for 10-yr event
Inflow = 11.13 cfs @ 12.21 hrs, Volume= 1.034 af
Outflow = 1.46 cfs @ 13.59 hrs, Volume= 0.942 af, Atten= 87%, Lag= 83.0 min
Discarded = 1.46 cfs @ 13.59 hrs, Volume= 0.942 af
Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Routed to Reach DP1 :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
Peak Elev= 359.12' @ 13.59 hrs Surf.Area= 18,002 sf Storage= 18,790 cf

Plug-Flow detention time= 145.8 min calculated for 0.942 af (91% of inflow)
Center-of-Mass det. time= 116.5 min (953.6 - 837.1)

Volume	Invert	Avail.Storage	Storage Description
#1	358.00'	142,613 cf	Custom Stage Data (Prismatic) Listed below (Recalc)
Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
358.00	15,523	0	0
360.00	19,946	35,469	35,469
362.00	24,775	44,721	80,190
364.00	37,648	62,423	142,613

Device	Routing	Invert	Outlet Devices
#1	Discarded	358.00'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	363.00'	8.0' long x 12.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.57 2.62 2.70 2.67 2.66 2.67 2.66 2.64

Discarded OutFlow Max=1.46 cfs @ 13.59 hrs HW=359.12' (Free Discharge)
↑—1=Exfiltration (Exfiltration Controls 1.46 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=358.00' (Free Discharge)
↑—2=Broad-Crested Rectangular Weir (Controls 0.00 cfs)

Proposed Conditions*NY-Moreau 24-hr S1 25-yr Rainfall=4.58"*

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 9

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1A:

Runoff Area=14.520 ac 46.69% Impervious Runoff Depth>1.35"
Flow Length=1,167' Tc=16.3 min CN=67 Runoff=18.36 cfs 1.631 af

Subcatchment1B:

Runoff Area=12.430 ac 0.00% Impervious Runoff Depth>0.05"
Flow Length=1,100' Tc=17.8 min CN=37 Runoff=0.09 cfs 0.048 af

Reach DP1:

Inflow=0.09 cfs 0.048 af
Outflow=0.09 cfs 0.048 af

Pond 1P:

Peak Elev=360.03' Storage=35,971 cf Inflow=18.36 cfs 1.631 af
Discarded=1.62 cfs 1.087 af Secondary=0.00 cfs 0.000 af Outflow=1.62 cfs 1.087 af

Total Runoff Area = 26.950 ac Runoff Volume = 1.679 af Average Runoff Depth = 0.75"
74.84% Pervious = 20.170 ac 25.16% Impervious = 6.780 ac

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 25-yr Rainfall=4.58"

Printed 10/8/2026

Page 10

Summary for Subcatchment 1A:

Runoff = 18.36 cfs @ 12.20 hrs, Volume= 1.631 af, Depth> 1.35"
 Routed to Pond 1P :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 25-yr Rainfall=4.58"

Area (ac)	CN	Description
* 6.780	98	
7.740	39	>75% Grass cover, Good, HSG A
14.520	67	Weighted Average
7.740		53.31% Pervious Area
6.780		46.69% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.0	100	0.0400	0.14		Sheet Flow, Grass: Dense n= 0.240 P2= 2.60"
2.0	239	0.0830	2.02		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
2.3	828	0.0100	5.94	10.50	Pipe Channel, CMP_Round 18" 18.0" Round Area= 1.8 sf Perim= 4.7' r= 0.38' n= 0.013
16.3	1,167	Total			

Summary for Subcatchment 1B:

Runoff = 0.09 cfs @ 16.67 hrs, Volume= 0.048 af, Depth> 0.05"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 25-yr Rainfall=4.58"

Area (ac)	CN	Description
1.100	39	>75% Grass cover, Good, HSG A
10.900	36	Woods, Fair, HSG A
0.430	49	Pasture/grassland/range, Fair, HSG A
12.430	37	Weighted Average
12.430		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.60"
4.1	1,000	0.6700	4.09		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 25-yr Rainfall=4.58"

Printed 10/8/2026

Page 11

Summary for Reach DP1:

Inflow Area = 12.430 ac, 0.00% Impervious, Inflow Depth > 0.05" for 25-yr event
Inflow = 0.09 cfs @ 16.67 hrs, Volume= 0.048 af
Outflow = 0.09 cfs @ 16.67 hrs, Volume= 0.048 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P:

Inflow Area = 14.520 ac, 46.69% Impervious, Inflow Depth > 1.35" for 25-yr event
Inflow = 18.36 cfs @ 12.20 hrs, Volume= 1.631 af
Outflow = 1.62 cfs @ 14.28 hrs, Volume= 1.087 af, Atten= 91%, Lag= 124.6 min
Discarded = 1.62 cfs @ 14.28 hrs, Volume= 1.087 af
Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Routed to Reach DP1 :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
Peak Elev= 360.03' @ 14.28 hrs Surf.Area= 20,007 sf Storage= 35,971 cf

Plug-Flow detention time= 201.2 min calculated for 1.084 af (66% of inflow)
Center-of-Mass det. time= 123.9 min (949.4 - 825.5)

Volume	Invert	Avail.Storage	Storage Description
#1	358.00'	142,613 cf	Custom Stage Data (Prismatic) Listed below (Recalc)

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
358.00	15,523	0	0
360.00	19,946	35,469	35,469
362.00	24,775	44,721	80,190
364.00	37,648	62,423	142,613

Device	Routing	Invert	Outlet Devices
#1	Discarded	358.00'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	363.00'	8.0' long x 12.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.57 2.62 2.70 2.67 2.66 2.67 2.66 2.64

Discarded OutFlow Max=1.62 cfs @ 14.28 hrs HW=360.03' (Free Discharge)
↑**1=Exfiltration** (Exfiltration Controls 1.62 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=358.00' (Free Discharge)
↑**2=Broad-Crested Rectangular Weir** (Controls 0.00 cfs)

Proposed Conditions*NY-Moreau 24-hr S1 100-yr Rainfall=6.26"*

Prepared by Lansing Engineering PC

Printed 10/8/2026

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

Page 12

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment1A:

Runoff Area=14.520 ac 46.69% Impervious Runoff Depth>2.47"
Flow Length=1,167' Tc=16.3 min CN=67 Runoff=34.32 cfs 2.985 af

Subcatchment1B:

Runoff Area=12.430 ac 0.00% Impervious Runoff Depth>0.32"
Flow Length=1,100' Tc=17.8 min CN=37 Runoff=1.74 cfs 0.334 af

Reach DP1:

Inflow=1.74 cfs 0.334 af
Outflow=1.74 cfs 0.334 af

Pond 1P:

Peak Elev=361.92' Storage=78,099 cf Inflow=34.32 cfs 2.985 af
Discarded=1.99 cfs 1.411 af Secondary=0.00 cfs 0.000 af Outflow=1.99 cfs 1.411 af

Total Runoff Area = 26.950 ac Runoff Volume = 3.319 af Average Runoff Depth = 1.48"
74.84% Pervious = 20.170 ac 25.16% Impervious = 6.780 ac

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 100-yr Rainfall=6.26"

Printed 10/8/2026

Page 13

Summary for Subcatchment 1A:

Runoff = 34.32 cfs @ 12.19 hrs, Volume= 2.985 af, Depth> 2.47"
 Routed to Pond 1P :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 100-yr Rainfall=6.26"

Area (ac)	CN	Description
* 6.780	98	
7.740	39	>75% Grass cover, Good, HSG A
14.520	67	Weighted Average
7.740		53.31% Pervious Area
6.780		46.69% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.0	100	0.0400	0.14		Sheet Flow, Grass: Dense n= 0.240 P2= 2.60"
2.0	239	0.0830	2.02		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
2.3	828	0.0100	5.94	10.50	Pipe Channel, CMP_Round 18" 18.0" Round Area= 1.8 sf Perim= 4.7' r= 0.38' n= 0.013
16.3	1,167	Total			

Summary for Subcatchment 1B:

Runoff = 1.74 cfs @ 12.60 hrs, Volume= 0.334 af, Depth> 0.32"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY-Moreau 24-hr S1 100-yr Rainfall=6.26"

Area (ac)	CN	Description
1.100	39	>75% Grass cover, Good, HSG A
10.900	36	Woods, Fair, HSG A
0.430	49	Pasture/grassland/range, Fair, HSG A
12.430	37	Weighted Average
12.430		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.60"
4.1	1,000	0.6700	4.09		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.8	1,100	Total			

Proposed Conditions

Prepared by Lansing Engineering PC

HydroCAD® 10.20-8a s/n 10911 © 2025 HydroCAD Software Solutions LLC

NY-Moreau 24-hr S1 100-yr Rainfall=6.26"

Printed 10/8/2026

Page 14

Summary for Reach DP1:

Inflow Area = 12.430 ac, 0.00% Impervious, Inflow Depth > 0.32" for 100-yr event
Inflow = 1.74 cfs @ 12.60 hrs, Volume= 0.334 af
Outflow = 1.74 cfs @ 12.60 hrs, Volume= 0.334 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P:

Inflow Area = 14.520 ac, 46.69% Impervious, Inflow Depth > 2.47" for 100-yr event
Inflow = 34.32 cfs @ 12.19 hrs, Volume= 2.985 af
Outflow = 1.99 cfs @ 15.30 hrs, Volume= 1.411 af, Atten= 94%, Lag= 186.2 min
Discarded = 1.99 cfs @ 15.30 hrs, Volume= 1.411 af
Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Routed to Reach DP1 :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
Peak Elev= 361.92' @ 15.30 hrs Surf.Area= 24,570 sf Storage= 78,099 cf

Plug-Flow detention time= 212.5 min calculated for 1.411 af (47% of inflow)
Center-of-Mass det. time= 126.7 min (937.5 - 810.8)

Volume	Invert	Avail.Storage	Storage Description
#1	358.00'	142,613 cf	Custom Stage Data (Prismatic) Listed below (Recalc)

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
358.00	15,523	0	0
360.00	19,946	35,469	35,469
362.00	24,775	44,721	80,190
364.00	37,648	62,423	142,613

Device	Routing	Invert	Outlet Devices
#1	Discarded	358.00'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	363.00'	8.0' long x 12.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.57 2.62 2.70 2.67 2.66 2.67 2.66 2.64

Discarded OutFlow Max=1.99 cfs @ 15.30 hrs HW=361.92' (Free Discharge)
↑**1=Exfiltration** (Exfiltration Controls 1.99 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=358.00' (Free Discharge)
↑**2=Broad-Crested Rectangular Weir** (Controls 0.00 cfs)



Appendix D

Calculations – Storm Management, Green Infrastructure, Pipe Sizing

Steps 3 and 5 - Apply RR Techniques and Standard SMPs

Is this project subject to Section 4.3 of the NYS Design Manual for Enhanced Phosphorus Removal?						No		
What is the nature of this construction project?			Redevelopment with increase in impervious area					
Project Title	Horstman Phase 2		Enter 90% Rainfall Event as P					
P=	1.15	inches						
Calculate Required WQv								
	Contributing Area (Acres)	Impervious Area (Acres)	Percent Impervious %	Rv	WQv (cf)	SMP Description		
Project Area Total	25.69	6.13	23.86	0.26	28,393			
SMP Practice								
1	14.52	7.74	53	0.53	32,110	Infiltration Basin		
2								
3								
4								
5								
6								
7								
8								
9								
10								
11								
12								
13								
14								
15								
16								
17								
18								
19								
20								
21								
22								
23								
24								
25								
26								
27								
Sum of Practices	14.52	7.74	53	0.53	32,110			
Total	25.69	6.13	24	0.265	28393	Required WQv	0.652 af	

Steps 3 and 5 - Apply RR Techniques and Standard SMPs

Enter the Soils Data for the site						
Hydrologic Soil Group	Acres	S				
A	25.69	55%				
B		40%				
C		30%				
D		20%				
Total Area	25.69					
Calculate the Minimum RRv						
S =	0.55					
Impervious =	6.13	acres				
Precipitation	1.15	inches				
Rv	0.95					
Minimum RRv	0.307	af				
	13373	cf				


Infiltration Basin (I-2)

Design Point:	Horstman Phase 2						
Enter Site Data For Drainage Area to be Treated by Practice							
Drainage Area Number	Contributing Area (Acres)	Impervious Area (Acres)	Percent Impervious %	Rv	WQv (cf)	Precipitation (in)	Description
1	14.52	7.74	53	0.53	32,110	1.15	Infiltration Basin
Design Criteria							
Enter underlying soil infiltration rate (based on geotechnical testing, refer to Appendix D)			10				
Is the contributing area to the practice an "Infiltration Restricted" stormwater hotspot?			No				
Is the contributing area to the practice an "Infiltration Prohibited" stormwater hotspot?			No				
Maximum contributing area (acres)			25				
Is the contributing area greater than the maximum allowed contributing area?			No				
Enter depth to seasonal high water table (ft)			10				
Enter depth to bedrock (ft)			10				
Enter pretreatment volume provided (cf)			17160				
Enter depth of freeboard (ft)			1.04				
Enter depth of basin (ft)			6				
Enter slope of maintenance access (%)			10				
Enter width of maintenance access (ft)			12				
Sizing Criteria							
		Value	Units	Notes			
Water Quality Volume		WQv	32110	cf			
Basin depth		db	6.0	ft			
Required Surface Area		Ab	5,352	sf			
Enter Surface Area Provided		Ab	8658	sf			
Determine Runoff Reduction							
RRv Provided		32,110	cf				





Appendix E

Grading/Drainage/Sediment, Erosion Control, and Landscaping Plan

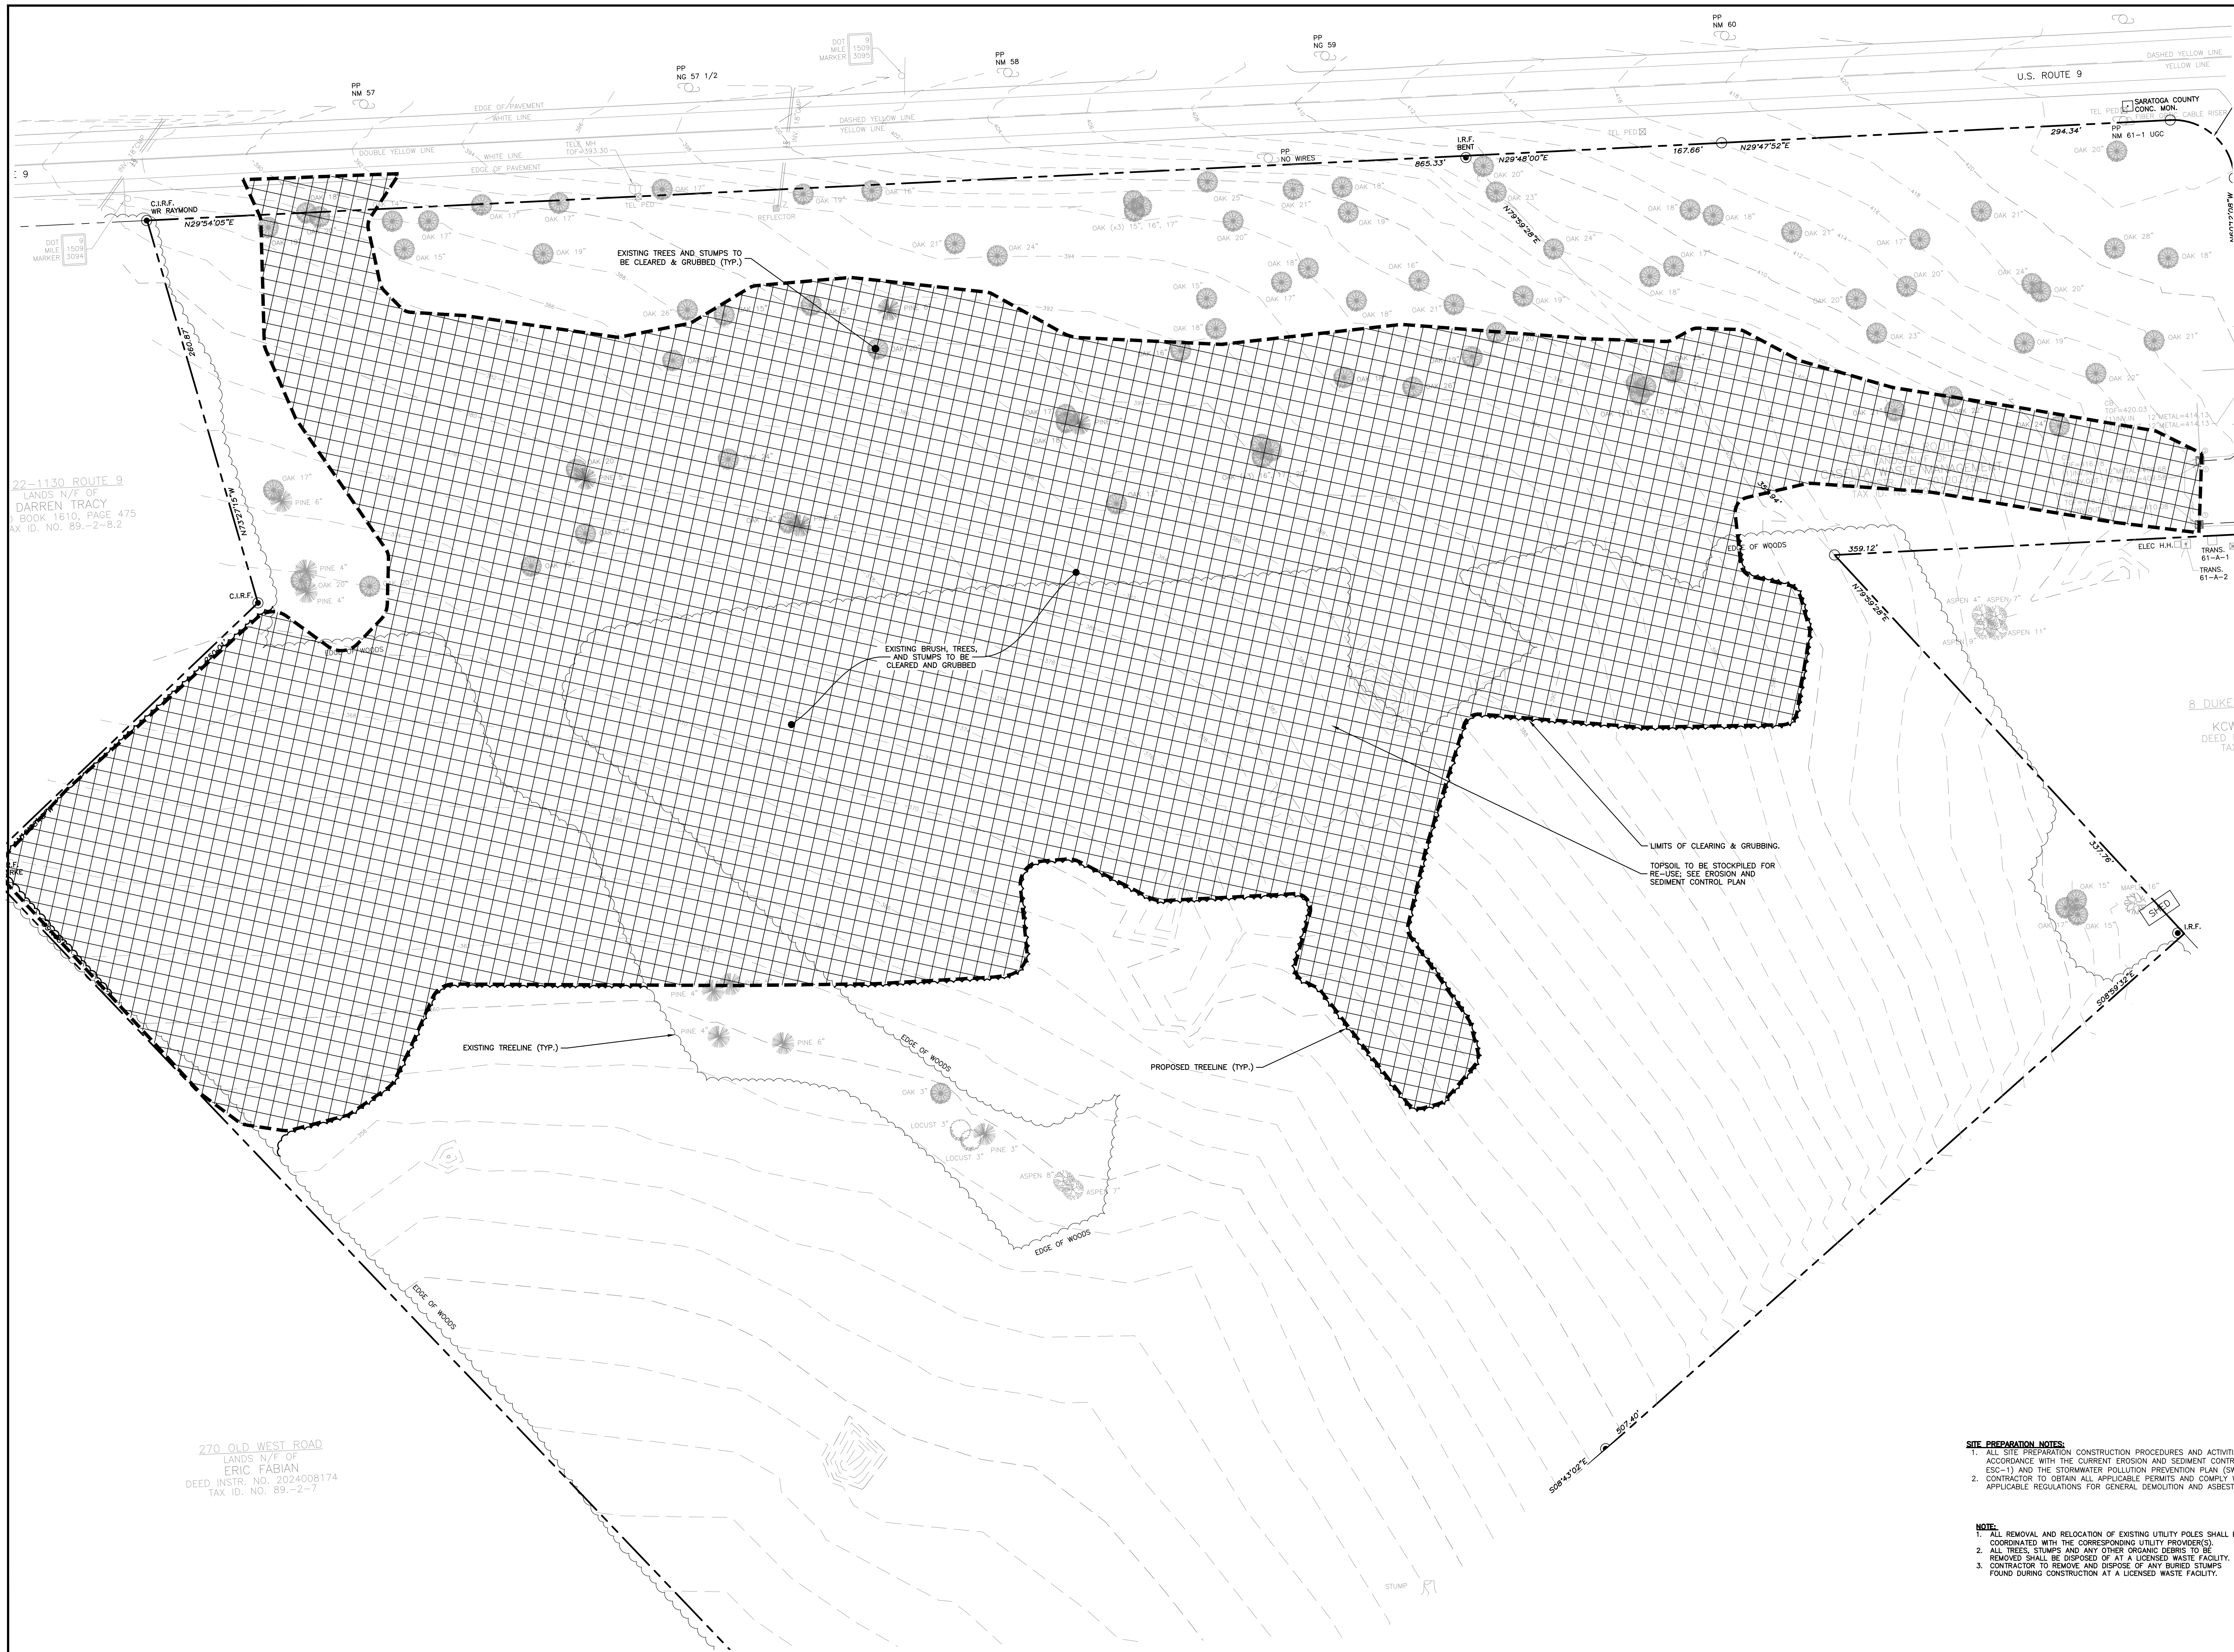

EXISTING CONDITIONS & DEMOLITION PLAN



- SITE PREPARATION NOTES:**
1. ALL SITE PREPARATION CONSTRUCTION PROCEDURES AND ACTIVITIES SHALL BE IN ACCORDANCE WITH THE CURRENT EROSION AND SEDIMENT CONTROL PLAN (SHEET ESC-11) AND THE STORMWATER POLLUTION PREVENTION PLAN (SWPPP).
 2. CONTRACTOR TO OBTAIN ALL APPLICABLE PERMITS AND COMPLY WITH ALL APPLICABLE REGULATIONS FOR GENERAL DEMOLITION AND ASBESTOS REMOVAL.

- NOTE:**
1. ALL REMOVAL AND RELOCATION OF EXISTING UTILITY POLES SHALL BE COORDINATED WITH THE CORRESPONDING UTILITY PROVIDER(S).
 2. ALL TREES, STUMPS AND ANY OTHER ORGANIC DEBRIS TO BE REMOVED SHALL BE DISPOSED OF AT A LICENSED WASTE FACILITY.
 3. CONTRACTOR TO REMOVE AND DISPOSE OF ANY BURIED STUMPS FOUND DURING CONSTRUCTION AT A LICENSED WASTE FACILITY.

CASELLA - FORT EDWARD HAULING FACILITY SITE PLAN
1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK


REVISION RECORD/DESCRIPTION
DATE
PRELIMINARY / NOT FOR CONSTRUCTION

LANSING
ENGINEERING
2450 WEST 10TH STREET
SUITE 301
MILWAUKEE, WI 53214
(414) 383-8843



EXISTING
CONDITIONS &
DEMO PLAN

PROJ. NO: 1238.04
SCALE: AS SHOWN
DATE: 10/01/26
SHEET 2 OF 13

LEGEND	
EXISTING FEATURES	PROPOSED FEATURES
	LIGHT POLE
	YARD HYDRANT
	FIRE HYDRANT
	WATER LINE
	SANITARY LINE
	CATCH BASIN
	SANITARY MANHOLE
	SANITARY CLEAN-OUT
	STORM WATER LINE
	PROPERTY LINE
	GUIDE RAIL
	WING CURB
	STANDARD CURB

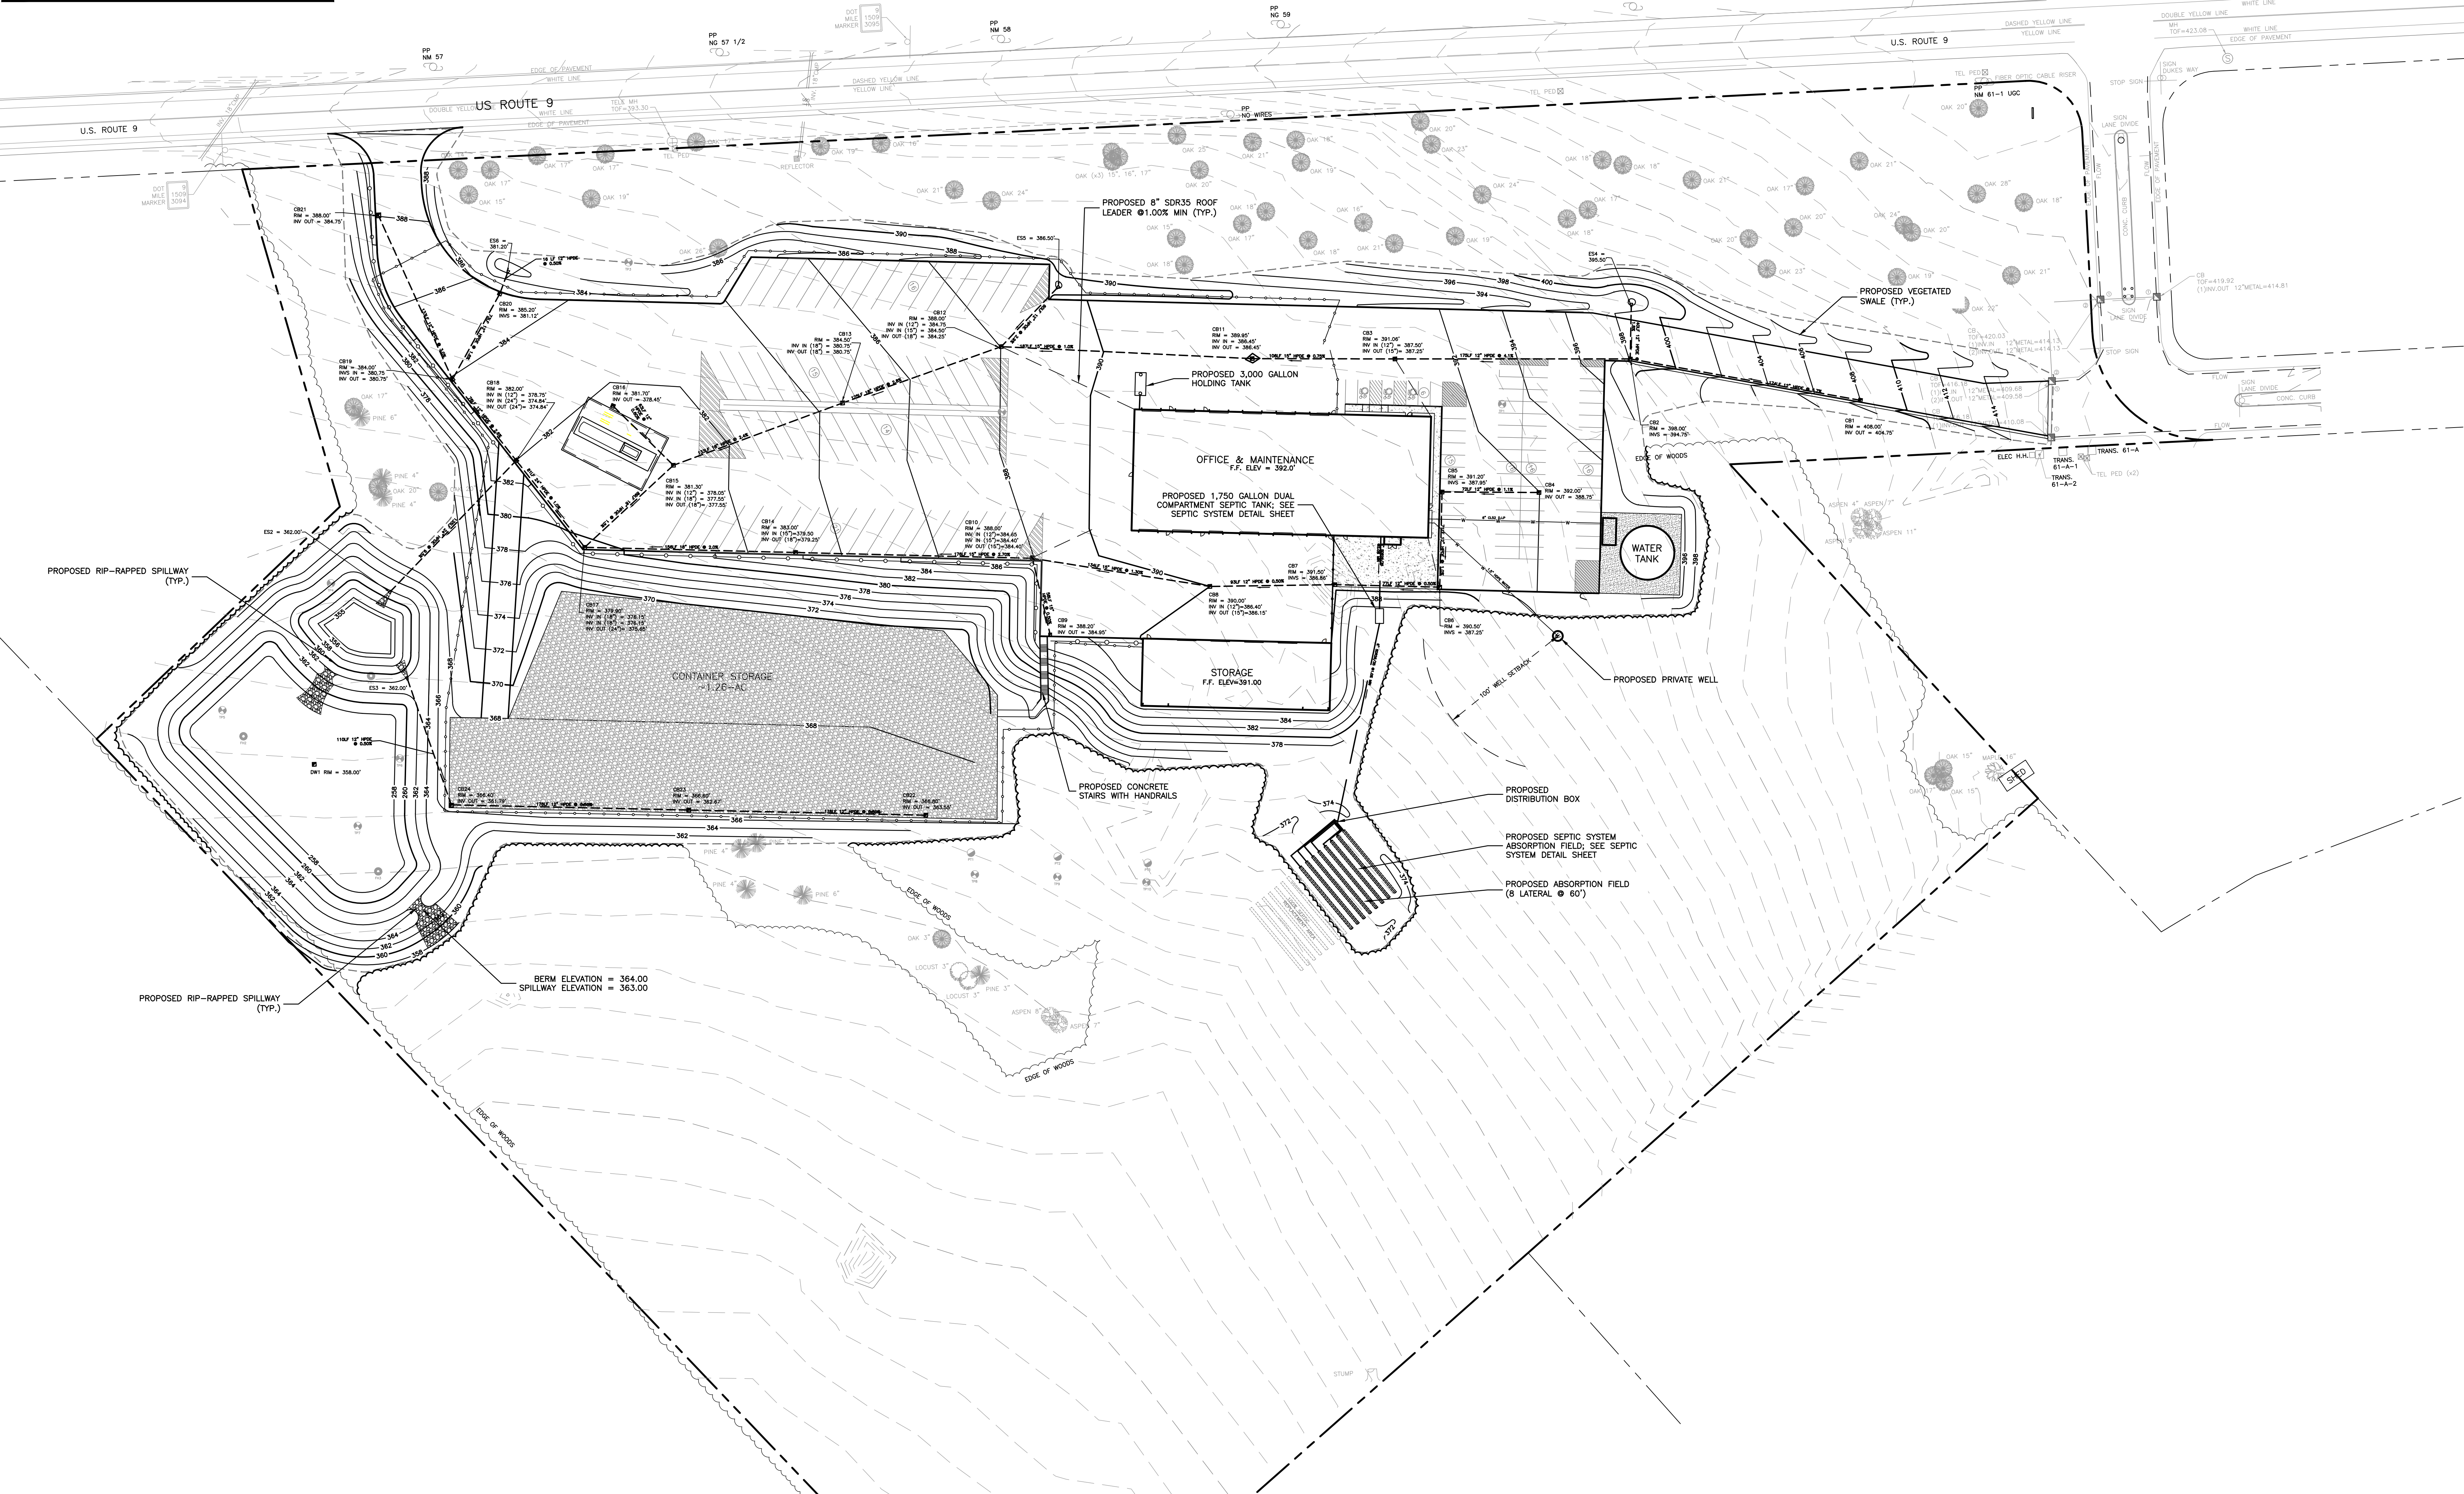

UTILITIES & GRADING PLAN



CASELLA - FORT EDWARD HAULING FACILITY SITE PLAN
1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK

REVISIONS RECORD/DESCRIPTION
DATE
DATE
DATE

LANSING ENGINEERING
2000 WEST 10TH STREET
MILWAUKEE, WI 53233
(414) 333-3443

PRELIMINARY / NOT FOR CONSTRUCTION

UTILITIES & GRADING PLAN

1. ALL NEW PLANT MATERIAL SHALL CONFORM TO THE MINIMAL GUIDELINES ESTABLISHED BY THE AMERICAN STANDARD FOR NURSERY STOCK PUBLISHED BY THE AMERICAN ASSOCIATION OF NURSERYMEN, INC. PROVIDE QUALITY, SIZE, GROWTH, VARIETY OF TREES AND SHRUBS INDICATED, AND ROOT BALL SIZE COMPLYING WITH APPLICABLE REQUIREMENTS OF ANSI Z60.1 AMERICAN STANDARD FOR NURSERY STOCK. ALL PLANTS SHALL BE NURSERY GROWN UNDER CLIMATIC CONDITIONS SIMILAR TO THOSE IN THE LOCALITY OF THE PROJECT.
2. PLANT SIZES: MEASURE TREES AND SHRUBS ACCORDING TO ANSI Z60.1 WITH BRANCHES AND TRUNKS OR CANES IN THEIR NORMAL POSITION. TAKE CALIPER MEASUREMENTS 6 INCHES ABOVE GROUND FOR TREES UP TO 4-INCH CALIPER SIZE. MEASURE MAIN BODY OF TREE OR SHRUB FOR HEIGHT AND SPREAD; DO NOT MEASURE BRANCHES OR ROOTS 10'-10'-10'.
3. ALL CONTAINER GROWN PLANTS SHALL BE SIZED ACCORDING TO ANSI Z60.1 FOR TYPE AND SIZE OF PLANT REQUIRED. PLANTS SHALL BE PREMIUM QUALITY, APPEAR 'FULL', OR 'HEAVY' WITHIN THEIR CONTAINER, AND BE REPRESENTATIVE OF THE CONTAINER SIZE SPECIFIED. PLANTS DEEMED TO BE SUBSTANDARD IN SIZE BY THE LANDSCAPE ARCHITECT WILL BE REJECTED.
4. ALL NEW PLANTS TO BE DULLED AND OVERLAPPED OR CONTAINER GROWN UNLESS OTHERWISE NOTED ON THE PLANT SCHEDULE.
5. TREES SHOULD BE FREELY DUG DURING THE SEASON OF PLANTING, MARCH 1ST TO MAY 1ST FOR SPRING PLANTING AND OCTOBER 15TH TO DECEMBER 15TH FOR FALL PLANTING. PLANTS KNOWN AS FALL DIG HAZARDS SHALL BE DUG IN THE SPRING ONLY.
6. THE CONTRACTOR SHALL SUPPLY ALL NEW PLANT MATERIAL IN QUANTITIES SUFFICIENT TO COMPLETE THE PLANTING SHOWN ON THE DRAWINGS.
7. IN GENERAL, PLANT SPECIES SUBSTITUTIONS WILL NOT BE ACCEPTED. IF SPECIFIED MATERIAL IS NOT OBTAINABLE, CONTRACTOR SHALL SUBMIT PROOF OF NON-AVAILABILITY TO THE LANDSCAPE ARCHITECT ALONG WITH PROPOSED SUBSTITUTION. ANY PROPOSED SUBSTITUTIONS OF PLANT SPECIES SHALL BE MADE WITH PLANTS OF EQUIVALENT OVERALL FORM, HEIGHT, SIZE, BRANCHING HABIT, FLOWER, LEAF, COLOR, FRUIT AND CULTURE, AND ONLY AFTER WRITTEN APPROVAL OF THE LANDSCAPE ARCHITECT.
8. THE LANDSCAPE ARCHITECT RETAINS THE RIGHT TO INSPECT TREES AND SHRUBS FOR SIZE AND CONDITION OF BALLS AND ROOT SYSTEMS, INSECTS, INJURIES AND LATENT DEFECTS, AND TO REJECT UNSATISFACTORY OR DEFECTIVE MATERIAL AT ANY TIME DURING PROGRESS OF WORK. CONTRACTOR SHALL REMOVE REJECTED TREES OR SHRUBS IMMEDIATELY FROM PROJECT SITE.
9. CONTRACTOR SHALL LOCATE AND VERIFY ALL EXISTING UTILITY LINES PRIOR TO PLANTING AND SHALL REPORT ANY CONFLICTS TO THE LANDSCAPE ARCHITECT.
10. THE CONTRACTOR SHALL STAKE THE LOCATIONS OF ALL PROPOSED PLANT MATERIAL AND PLANT BEDS FOR APPROVAL BY THE LANDSCAPE ARCHITECT PRIOR TO THE COMMENCEMENT OF PLANTING.
11. INSTALLED PLANTS SHALL BEAR THE SAME RELATIONSHIP TO PROPOSED GRADE AS THEY BORE TO PREVIOUS GRADE. NO TREES SHALL BE PLANTED BEFORE ACCEPTANCE OF ROUGH GRADING.
12. CONTRACTOR SHALL PROVIDE LONG LASTING, SLOW RELEASE STARTER FERTILIZER IN EACH PLANTING PIT FOR TREES, SHRUBS AND PERENNIALS.
13. ALL PLANT BEDS SHALL RECEIVE THREE INCHES (3") OF SHREDDED BARK MULCH. MULCH SHALL BE FREE FROM DELETERIOUS MATERIALS AND SUITABLE AS A TOP DRESSING OF TREES AND SHRUBS, CONSISTING OF DOUBLE HAMMERED SHREDDED BARK MULCH COMPRISED OF EITHER HARDWOOD OR SOFTWOOD SHREDDED BARK. SHREDDED BARK MULCH SHALL NOT EXCEED 3" IN GREATEST DIMENSION, AND SHALL BE DARK BROWN IN COLOR.
14. PLANTS SHALL BE DELIVERED ONLY AS THEY CAN BE INSTALLED IN REASONABLE TIME. ALL PLANTS ARE SUBJECT TO INSPECTION AT DELIVERY BY THE LANDSCAPE ARCHITECT / OWNER'S REPRESENTATIVE.
15. IF DISCREPANCIES EXIST BETWEEN THE NUMBER OF PLANTS DRAWN ON THE PLANTING PLAN AND THE NUMBER OF PLANTS IN THE PLANT LIST, THE PLANTING PLAN SHALL GOVERN.
16. MAINTENANCE SHALL BEGIN IMMEDIATELY AFTER EACH PLANT IS PLANTED AND SHALL CONTINUE FOR A MINIMUM 30-DAY MONITORING PERIOD AFTER NOTIFICATION OF SUBSTANTIAL COMPLETION AND UNTIL FINAL ACCEPTANCE, WHICHEVER IS GREATER. MAINTENANCE INCLUDES PRUNING, WEEDING, WATERING, FERTILIZATION, AND RE-SEEDING AS NECESSARY.
17. PROTECT PLANTS FROM DAMAGE DUE TO LANDSCAPE OPERATIONS AND OPERATIONS OF OTHER CONTRACTORS AND TRADES. MAINTAIN PROTECTION DURING INSTALLATION AND MAINTENANCE PERIODS. TREAT, REPAIR, OR REPLACE DAMAGED PLANTINGS.
18. UPON COMPLETION OF ALL PLANTING WORK, THE CONTRACTOR SHALL REQUEST IN WRITING THAT THE LANDSCAPE ARCHITECT FORMALLY INSPECT THE PLANTING WORK. IF PLANT MATERIALS AND WORKMANSHIP ARE ACCEPTABLE, THE LANDSCAPE ARCHITECT WILL ISSUE A WRITTEN CERTIFICATE OF SUBSTANTIAL COMPLETION.
19. FOLLOWING THE ISSUANCE OF THE CERTIFICATE OF SUBSTANTIAL COMPLETION TO THE CONTRACTOR, THE CONTRACTOR SHALL MAINTAIN THE PLANTS FOR THE MAINTENANCE PERIOD SPECIFIED IN THIS SECTION.
20. ACCEPTANCE STANDARDS AT END OF THE MAINTENANCE PERIOD:
- 20.1. PLANTS SHALL BE FREE OF FROST CRACKS, SUN SCALD, DAMAGE DUE TO INSECTS, PESTS, AND DISEASE, STRUCTURAL DEFECTS; AND DAMAGE RESULTING FROM MACHINERY OR TOOLS. ALL PLANTS REGARDLESS OF THE SEASON OF REVIEW SHALL HAVE A MINIMUM OF 70 PERCENT HEALTHY, BALANCED BRANCHING STRUCTURE WITH A HEALTHY TERMINAL LEADER(S) WITH VISIBLE TERMINAL BUD(S). TREES SHALL BE PLUMB AND SHOW NO SIGNS OF UNIFORM SETTLING OR LEANING.
- 20.2. LAWN AREAS SHALL HAVE A HEALTHY, UNIFORM STAND OF GRASS FREE OF WEEDS, SURFACE IRREGULARITIES, WITH COVERAGE EXCEEDING 90% OVER ANY 10 SQ. FT. AND BARE SPOTS NOT EXCEEDING 5"X5"
21. GUARANTEE: CONTRACTOR SHALL GUARANTEE ALL PLANT MATERIAL TO REMAIN ALIVE AND BE IN A HEALTHY, VIGOROUS CONDITION FOR A PERIOD OF ONE YEAR AFTER FINAL ACCEPTANCE OF PLANTING WORK, AGAINST DEFECTS INCLUDING DEATH AND UNSATISFACTORY WORK.
22. CONTRACTOR SHALL REPLACE ALL PLANTS THAT ARE MORE THAN 25% DEAD OR, AS DETERMINED BY THE LANDSCAPE ARCHITECT, ARE IN AN UNHEALTHY OR UNSUITABLE CONDITION. CONTRACTOR SHALL BEAR THE COST OF COMPLETE REPLACEMENTS. REPLACEMENTS SHALL BE OF THE SAME SIZE AND SPECIES AS SPECIFIED ON THE PLANTING LIST.
23. GRASS SEED: FRESH, CLEAN, DRY, NEW-CROP SEED COMPLYING WITH AGA'S "RULES FOR TESTING SEEDS" FOR PURITY AND GERMINATION TOLERANCES. PROVIDE SEED MIXTURE COMPOSED OF SPECIES, PROPORTIONS AND MINIMUM PERCENTAGES OF PURITY, GERMINATION, AND MAXIMUM PERCENTAGE OF WEED SEED, AS FOLLOWS:


COMMON NAME	PROPORTION BY WEIGHT	GERMINATION MINIMUM	PURITY MINIMUM
OREOPHYTE RED FESCUE OR CHEWINGS FESCUE	50%	85%	90%
KENTUCKY BLUEGRASS	25%	85%	90%
PERENNIAL RYE	25%	90%	90%

24. NATIVE WILDFLOWER & GRASS SEED: FRESH, CLEAN, DRY, NEW-CROP SEED COMPLYING WITH AGA'S "RULES FOR TESTING SEEDS" FOR PURITY AND GERMINATION TOLERANCES. PROVIDE SEED MIXTURE COMPOSED OF SPECIES, PROPORTIONS AND MINIMUM PERCENTAGES OF PURITY, GERMINATION, AND MAXIMUM PERCENTAGE OF WEED SEED, AS FOLLOWS:

BASIS OF DESIGN: ERNST SEEDS - MESIC TO DRY NATIVE POLLINATOR MIX (ERNM-105)
SEEDING RATE: 20LBS/AC WITH 30 LBS/AC COVER CROP
COVER CROP: EITHER GRASS ONLY (JANUARY 1 TO JULY 31)
OR, GRASS RYE (AUGUST 1 TO DECEMBER 31)

MIX COMPOSITION:


- 29.1% Schizanthus scapularis (Little Bluestem 'Prairie View')
- 20.0% Sorghastrum nutans (Indiangrass)
- 15.0% Elymus virginicus (Virginian Wildrye)
- 8.0% Echinochloa purpurea (Purple Coneflower)
- 5.0% Panicum clandestinum (Dwarf Fescue)
- 3.0% Chamaecrista fasciculata (Partridge Pea)
- 3.0% Coreopsis lanceolata (Lanceleaf Coreopsis)
- 3.0% Rudbeckia hirta (Black-eyed Susan)
- 3.0% Verbena hastata (Blue Vervain)
- 2.0% Helianthus annuus (Common Sunflower)
- 1.5% Asclepias incarnata (Swamp Milkweed)
- 1.0% Aster novae-angliae (New England Aster)
- 1.0% Pycnanthemum tenuifolium (Narrowleaf Mountainmint)
- 1.0% Senecio jacobaea (Wild Sennel)
- 0.8% Tradescantia ohiensis (Ohio Spiderwort)
- 0.6% Eupatorium perfoliatum (Boneset)
- 0.5% Zizia aurea (Golden Alexander)
- 0.5% Baptisia australis (Blue False Indigo)
- 0.5% Monarda fistulosa (Wild Bergamot)
- 0.5% Solidago nemoralis (Gray Goldenrod)
- 0.3% Asclepias syriaca (Common Milkweed)
- 0.3% Penstemon digitalis (Tall White Beardtongue)
- 0.2% Solidago rugosa (Wrinkleleaf Goldenrod)
- 0.1% Aster umbellatus (Flat Topped White Aster)

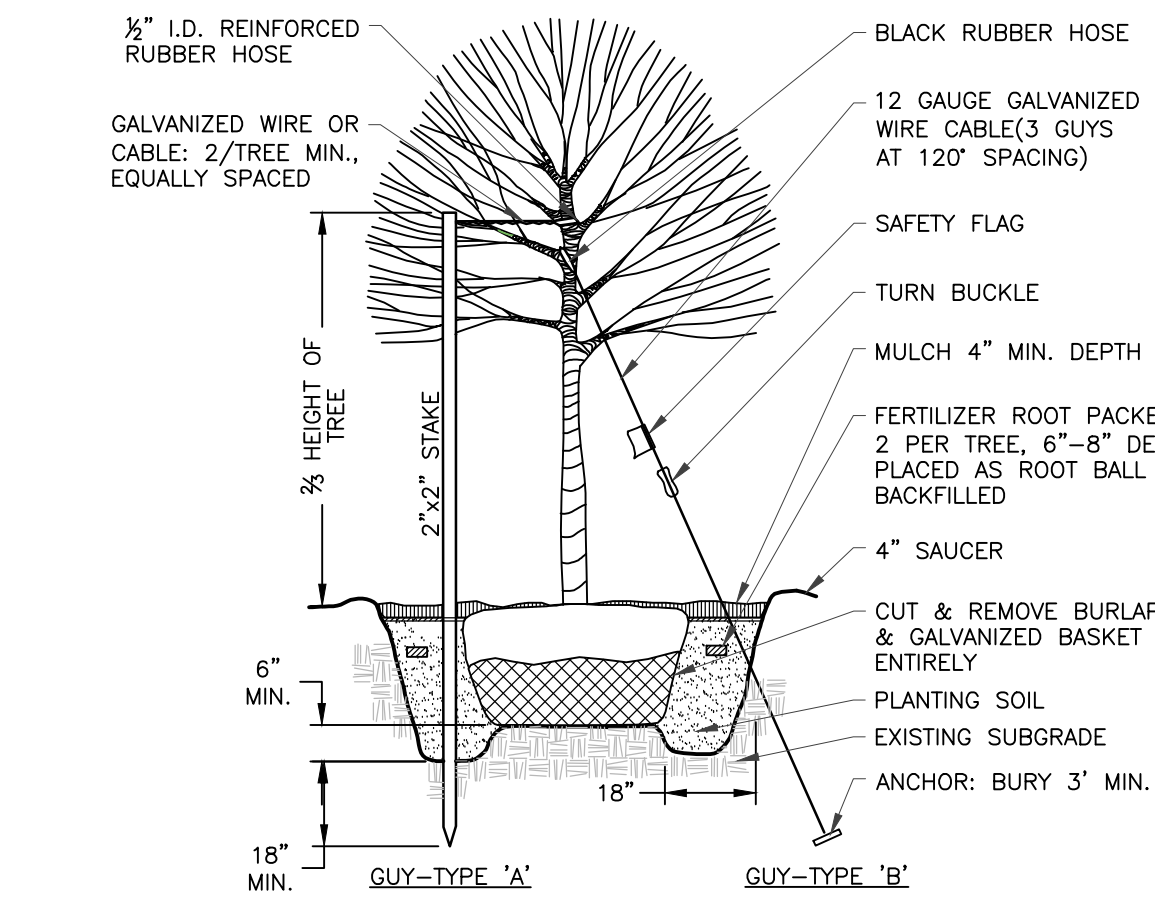

NOTE:
- GUY TYPE "A" IS FOR TREES LESS THAN 3" CALIPER
- GUY TYPE "B" IS FOR TREES 3" CALIPER OR GREATER

1 DECIDUOUS TREE PLANTING


SCALE: NTS

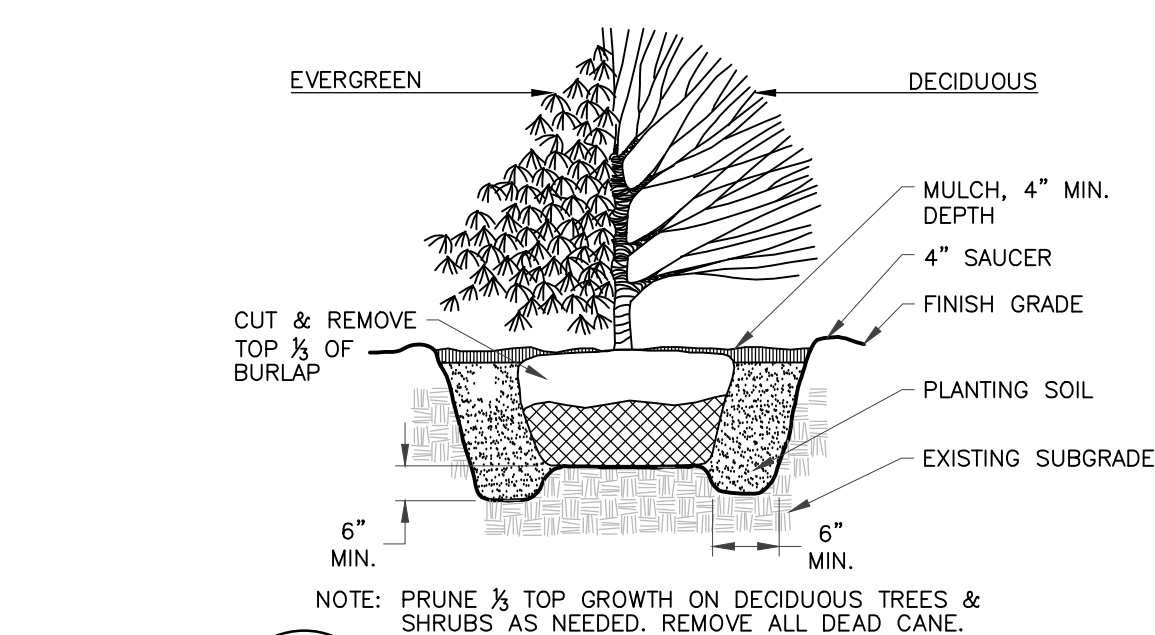

2 SHRUB PLANTING DETAIL

SCALE: NTS

LANDSCAPING PLAN



UNAUTHORIZED
ADDITION TO THIS
DRAWING IS
VIOLATION OF THE
PROFESSIONAL
LANDSCAPING ENGINEERING
PC

CASELLA - FORT EDWARD HAULING FACILITY SITE PLAN
1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK

PRELIMINARY / NOT FOR CONSTRUCTION

LANSING
ENGINEERING

LANDSCAPING
PLAN

PROJ. NO:1238.04
SCALE: AS SHOWN
DATE: 10/01/26
SHEET 5 OF 13

ADDITIONAL EROSION CONTROL MEASURES:

1. THE CONTRACTOR WILL BE RESPONSIBLE FOR THE REMOVAL AND DISPOSAL OF ANY CUT MATERIAL.
2. SOILS CONTAMINATED DURING CONSTRUCTION MUST BE REMOVED AND DISPOSED OF AT A LICENSED WASTE FACILITY.
3. EXPOSED SOILS TO BE STABILIZED WITHIN 3 DAYS DURING THE WINTER MONTHS (NOVEMBER 15 - APRIL1).
4. EROSION CONTROL MEASURES DURING THE WINTER MONTHS SHALL ALSO INCLUDE AN ENLARGED ENTRANCE, PERIMETER BUFFER OF 25 FEET, TALL MARKER STAKES ON SILT FENCE, CLEAR PATHS TO DRAINAGE STRUCTURES, STABILIZED SOIL STOCKPILES TWICE THE TYPICAL MULCHING RATE, SNOW STORAGE DURING CONSTRUCTION SHALL BE CONSISTENT WITH THE SNOW STORAGE AREAS OUTLINED ON SHEET LM-1.
5. RIP RAP WEIGHT RANGE SHALL BE 20 TO 35 POUNDS WITH 75% OF ITS MATERIAL IN THE 25 TO 35 POUND RANGE.
6. MULCH SHALL BE A WOOD FIBER HYDRO MULCH OR SPRAYABLE PRODUCT. MULCHING BLANKETS MUST BE USED ON STEEP SLOPES AND DRAINAGE SWALES. MULCHING BLANKETS MUST BE "OURLEX ENFORCER" BY AMERICAN EXCELSIOR COMPANY OR "GEOWEB SLOPE PROTECTION SYSTEM" BY PRESTO GEOSYSTEMS.
7. ALL TOPSOIL MUST COMPLY WITH THE BLUE BOOK. TOPSOIL PH MUST BE BETWEEN 5.5 AND 7.5. TOPSOIL ORGANICS CONTENT MUST BE BETWEEN 2% AND 20%. TOPSOIL GRADATION MUST COMPLY WITH THE FOLLOWING:
100% PASSING 1 1/2" IN SIEVE
85-100% PASSING 1" IN SIEVE
65-100% PASSING 3/4" IN SIEVE
20-100% PASSING NO. 200 SIEVE
8. TOTAL LIVE SEED MUST BE 80 POUNDS PER ACRE. TOTAL WEED CONTENT SHALL NOT EXCEED 1%. ALL SEED MIXTURES MUST COMPLY WITH THE TOWN OF COLONIE HIGHWAY AND DRAINAGE STANDARDS, TABLE 11-2.

RECOMMENDED SOIL EROSION AND SEDIMENT CONTROL MEASURES

MEASURES SHOWN ARE TO DEFINE INTENT. ACTUAL MEASURES WILL BE IMPLEMENTED AS SITE CONDITIONS WARRANT BY THE CONTRACTOR. CONTRACTOR SHALL PROVIDE ALL NEEDED CONTROL MEASURES TO PREVENT SOIL EROSION.

GENERAL MEASURES:


1. DAMAGE TO SURFACE WATERS RESULTING FROM EROSION AND SEDIMENTATION SHALL BE MINIMIZED BY STABILIZING DISTURBED AREAS AND BY REMOVING SEDIMENT FROM CONSTRUCTION SITE.
 2. INsofar AS PRACTICABLE, EXISTING VEGETATION SHALL BE PRESERVED. FOLLOWING THE COMPLETION OF CONSTRUCTION ACTIVITIES IN ANY PORTION OF THE SITE, PERMANENT VEGETATION SHALL BE ESTABLISHED ON ALL EXPOSED SOILS.
 3. SITE PREPARATION ACTIVITIES SHALL BE PLANNED TO MINIMIZE THE AREA AND DURATION OF SOIL DISRUPTION.
 4. PERMANENT TRAFFIC CORRIDORS SHALL BE ESTABLISHED AND "ROUTES OF CONVENIENCE" SHALL BE AVOIDED.
- PARTICULAR MEASURES:**
1. IMMEDIATELY FOLLOWING COMPLETION OF ANY AND ALL OF THE PROPOSED STORM DRAIN INLETS, STORM DRAIN INLET PROTECTION SHALL BE CONSTRUCTED.
 2. DRAINAGE DITCH SEDIMENT FILTERS: UNTIL SUCH TIME AS FINAL SITE STABILIZATION IS COMPLETED, DITCHES SHALL RECEIVE TREATMENT WITH STONE CHECK DAMS SO AS TO EFFECTIVELY TRAP SEDIMENT AND MINIMIZE ITS RELEASE OFF-SITE. STONE CHECK DAMS SHALL BE CONSTRUCTED WITHIN EACH DITCH BEGINNING AT ITS DOWNSTREAM TERMINUS AND SHOULD NOT BE PLACED AT INTERVALS EXCEEDING 20 FEET.
 3. TOPSOIL AND FILL THAT IS TO REMAIN STOCKPILED ON-SITE FOR PERIODS GREATER THAN 14-DAYS SHALL BE STABILIZED BY SEEDING AND MULCHING. PROVIDE SILT FENCE EROSION CONTROL DOWNGRADIENT OF SOIL STOCKPILE AREA.
 4. IN NO CASE SHALL ERODIBLE MATERIALS BE STOCKPILED WITHIN 25 FEET OF ANY DITCH, STREAM, OR OTHER SURFACE WATER BODY.
 5. PERMANENT VEGETATIVE COVER: IMMEDIATELY FOLLOWING THE COMPLETION OF CONSTRUCTION ACTIVITIES IN ANY PORTION OF THE SITE, PERMANENT VEGETATION SHALL BE ESTABLISHED ON ALL EXPOSED SOILS.
 6. ALL HEALTHY TREES OF DESIRABLE SPECIES ARE TO BE PROTECTED FROM DAMAGE. ALL UNNECESSARY REMOVAL OF HEALTHY TREES SHALL BE AVOIDED EXCEPT WHERE NOTED ON SHEETS EC-1 & EC-2.
 7. THE CONTRACTOR IS TO ADHERE TO ALL REQUIREMENTS SET FORTH IN THE SWPPP.
 8. DUST CONTROL SHALL BE A.O.B.E. IN CONFORMANCE WITH TOWN OF COLONIE STANDARDS.

CONSTRUCTION PHASING TABLE	
PHASE NUMBER	
PHASE 1	PHASE 1 = 4.78 ACRES
PHASE 2	PHASE 2 = 4.92 ACRES
PHASE 3	PHASE 3 = 0.47 ACRES


TABLE 5.3 SOIL RESTORATION REQUIREMENTS*

TYPE OF SOIL DISTURBANCE	SOIL RESTORATION REQUIREMENT	COMMENTS/ EXAMPLES
NO SOIL DISTURBANCE	RESTORATION NOT PERMITTED	PRESERVATION OF NATURAL FEATURES
MINIMAL SOIL DISTURBANCE	RESTORATION NOT PERMITTED	CLEARING AND GRUBBING
AREAS WHERE TOPSOIL IS STRIPPED ONLY - NO CHANGE IN GRADE	HSG C&D AERATE** AND APPLY 6" OF TOPSOIL	PROTECT AREA FROM ANY ONGOING CONSTRUCTION ACTIVITIES
AREAS OF CUT OR FILL	HSG C&D APPLY FULL SOIL RESTORATION***	
HEAVY TRAFFIC AREAS ON SITE (ESPECIALLY IN A ZONE 5-25 FEET AROUND BUILDINGS BUT NOT WITHIN A 5' PERIMETER AROUND FOUNDATION WALLS)	APPLY FULL SOIL RESTORATION (DE-COMPACTION AND COMPOST ENHANCEMENT)	
AREAS WHERE RUNOFF REDUCTION AND/OR INFILTRATION PRACTICES ARE APPLIED	RESTORATION NOT REQUIRED, BUT MAY BE APPLIED TO ENHANCE THE REDUCTION SPECIFIED FOR APPROPRIATE PRACTICES	KEEP CONSTRUCTION EQUIPMENT FROM CROSSING THESE AREAS. TO PROTECT NEWLY INSTALLED PRACTICE FROM ANY ONGOING CONSTRUCTION ACTIVITIES, CONSTRUCT A SINGLE PHASE OPERATION FENCE AREA
REDEVELOPMENT PROJECTS	SOIL RESTORATION IS REQUIRED ON REDEVELOPMENT PROJECTS IN AREAS WHERE EXISTING IMPERVIOUS AREA WILL BE CONVERTED TO PERVIOUS AREA	

NOTE: THE PROPOSED PROJECT IS SITUATED ON TYPE D SOILS WITH A HISTORY OF DEVELOPMENT AND COMPACTION. IT IS A SITE REQUIREMENT THAT FULL SOIL RESTORATION WITH DECOMPACTION AND COMPOST ENHANCEMENT IS CARRIED OUT FOR THIS PROJECT IN ACCORDANCE WITH THE DEEP RIPPING AND DE-COMPACTION, DEC 2008 FOUND IN APPENDIX K OF THE PROJECT SWPPP.

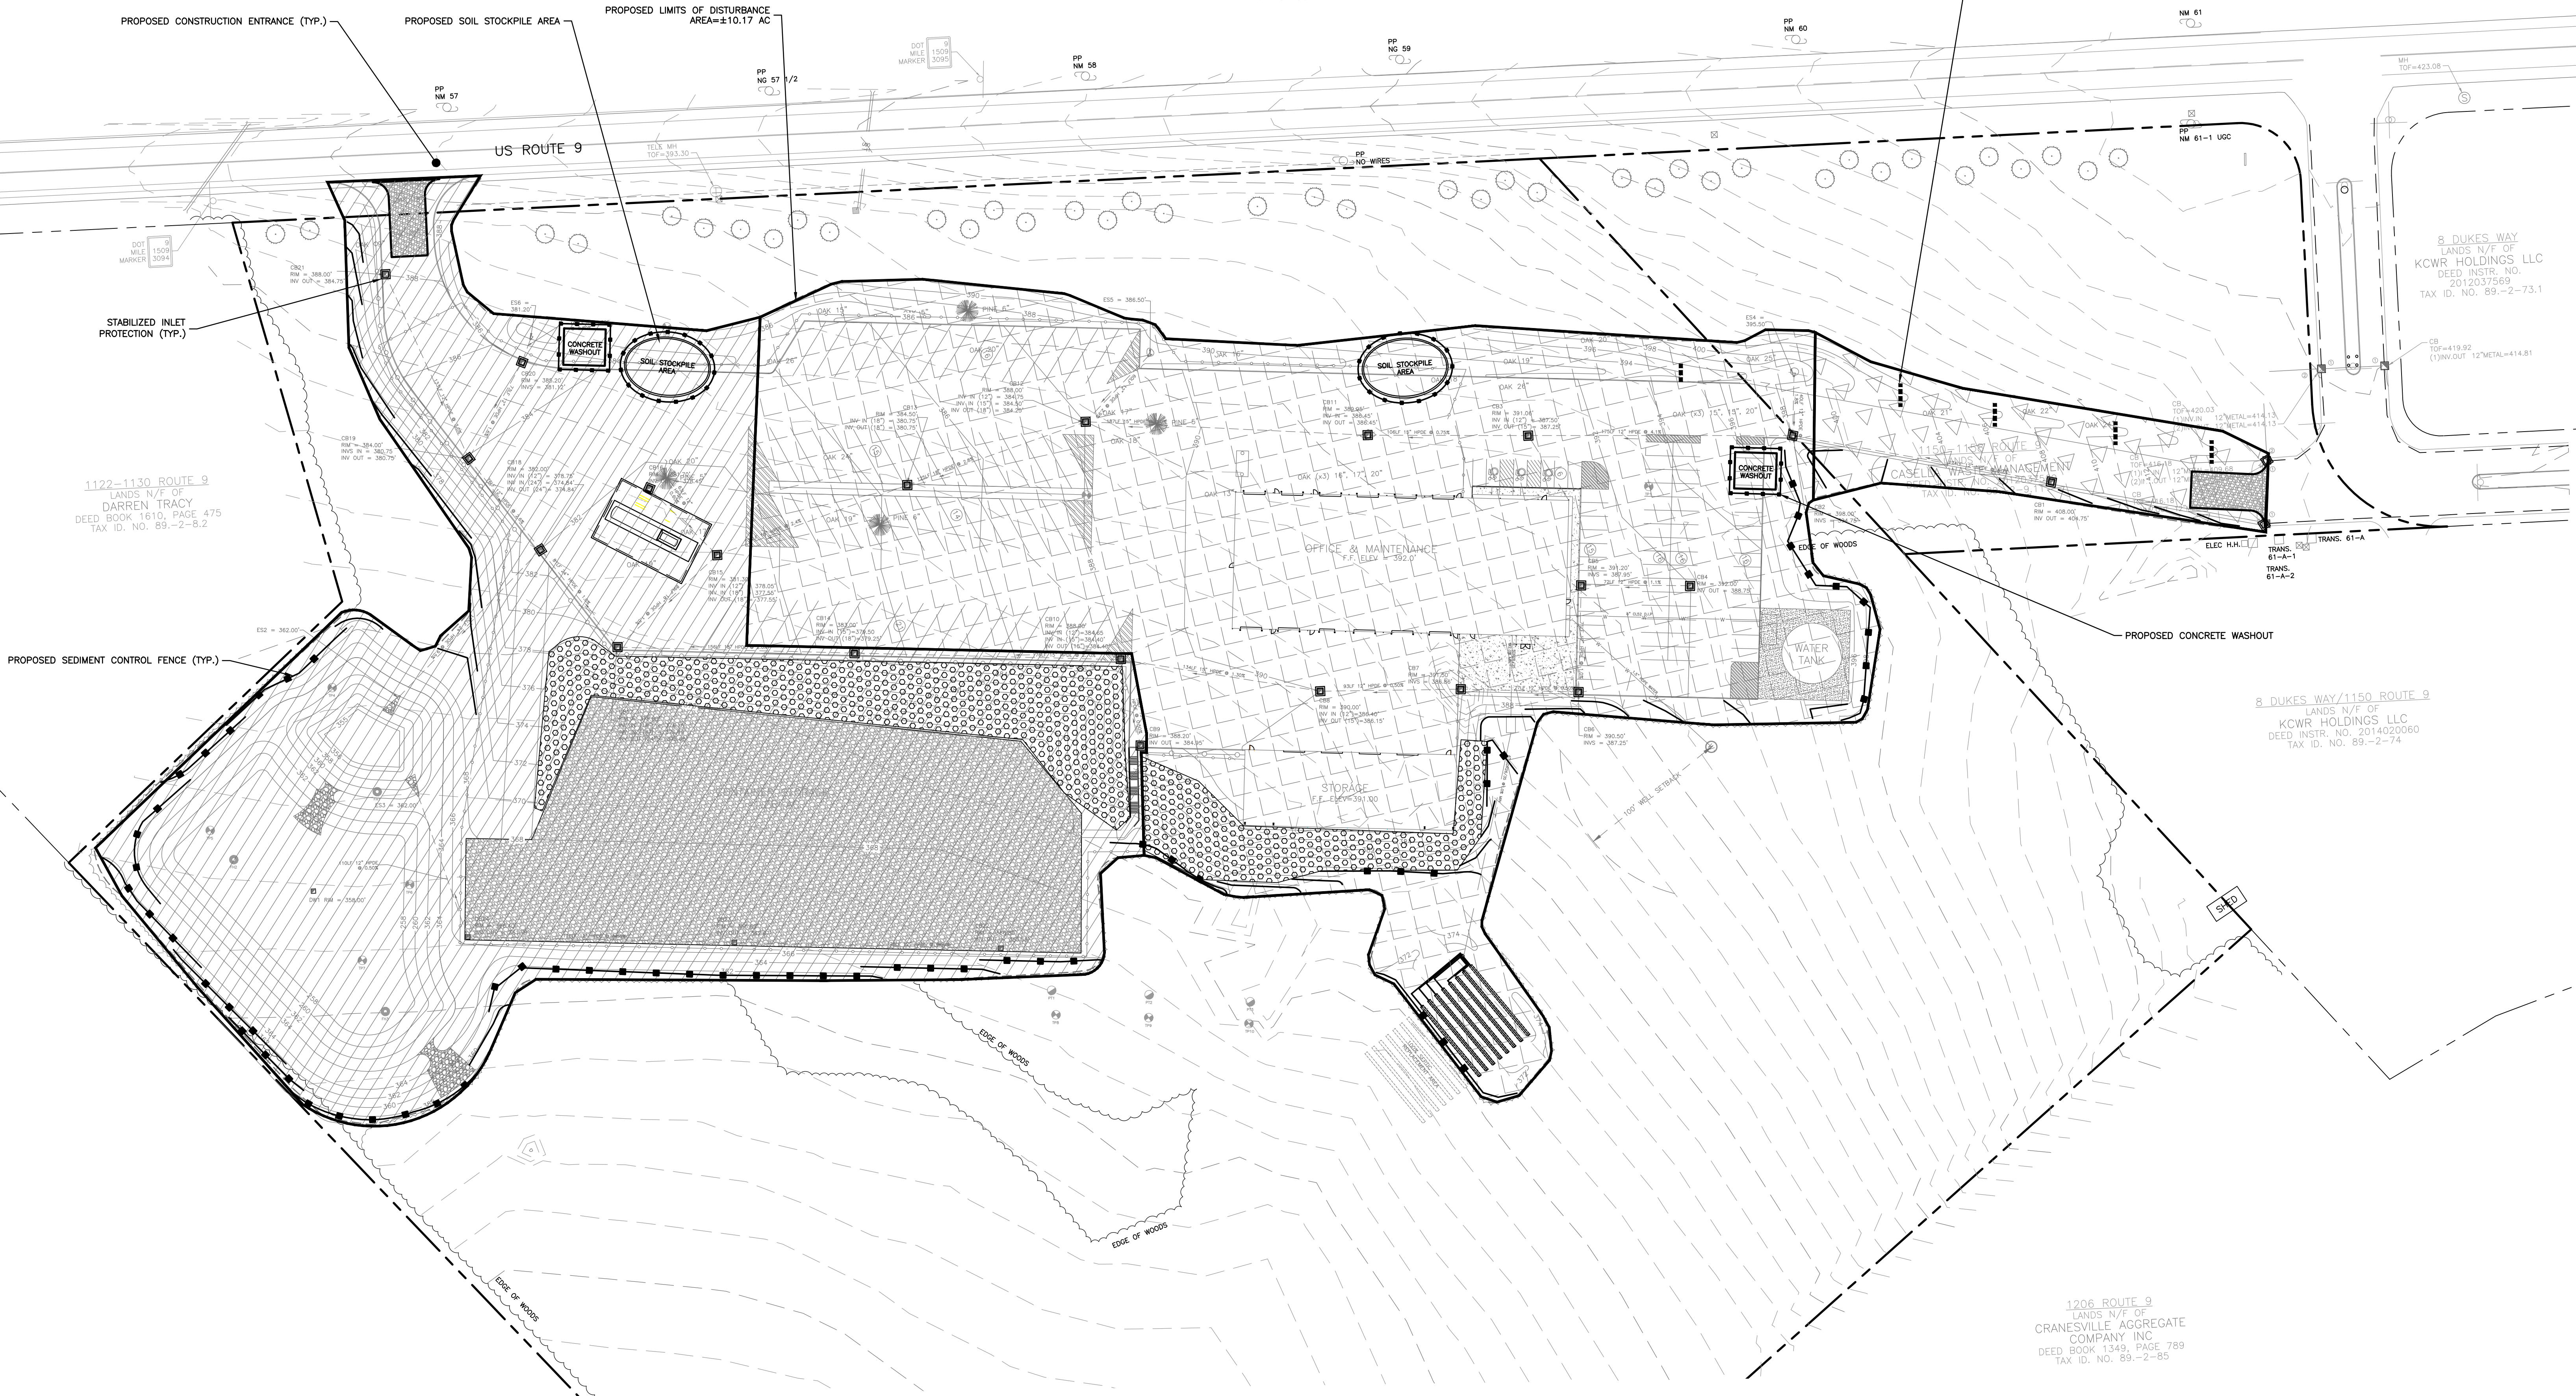

EROSION & SEDIMENT CONTROL PLAN



SOIL APPRAISAL							
DEEP HOLE OBSERVATIONS & PERCOLATION TESTING PERFORMED ON 9/23/2026 IN DRY, 50°F CONDITIONS BY LANSING ENGINEERING AND WITNESSED BY AJM							
MOREAU CASELLA TRUCK SHOP	TRIAL 1	TRIAL 2	TRIAL 3	TRIAL 4	TRIAL 5	TRIAL 6	TRIAL 7
PT1 - PERCOLATION TEST NO. 1	0:49 MIN./IN.	0:53 MIN./IN.	0:58 MIN./IN.	0:59 MIN./IN.	1:02 MIN./IN.		
PT2 - PERCOLATION TEST NO. 2	0:43 MIN./IN.	0:48 MIN./IN.	0:54 MIN./IN.	0:58 MIN./IN.	0:59 MIN./IN.	0:59 MIN./IN.	1:02 MIN./IN.
PT3 - PERCOLATION TEST NO. 3	0:46 MIN./IN.	0:51 MIN./IN.	0:57 MIN./IN.	1:03 MIN./IN.	1:07 MIN./IN.	1:10 MIN./IN.	
TP1 - TEST PIT NO. 1	0'-2" 2'-10.5' TOPSOIL MEDIUM BROWN SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP2 - TEST PIT NO. 2	0'-4" 4'-10.5' TOPSOIL MEDIUM/COARSE GRAY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP3 - TEST PIT NO. 3	0'-12" 12'-11" TOPSOIL MEDIUM/COARSE GRAY SAND MORE FINE @ BOTTOM		SLIGHT MOTTLING @ 132" NO GROUNDWATER OBSERVED				
TP4 - TEST PIT NO. 4	0'-12" 12'-4" 4'-11" TOPSOIL MEDIUM ORANGE SAND MED/COARSE GRAY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP5 - TEST PIT NO. 5	0'-1.5' 1.5'-7" 7'-10" TOPSOIL MEDIUM GRAY SAND SILTY HARD PACKED TILL - NOT PERMEABLE		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP6 - TEST PIT NO. 6	0'-12" 12'-5.75' 5.75'-10" LOAMY TOPSOIL MEDIUM GRAY SAND HARD PACKED FINE SAND/TILL - LIMITING		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP7 - TEST PIT NO. 7	0'-12" 12'-7.25' 7.25'-10" TOPSOIL MEDIUM GRAY SAND HARD FINE SAND/TILL		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP8 - TEST PIT NO. 8	0'-6" 6'-8" 8'-9.5" TOPSOIL FINE/MEDIUM GRAY SAND PACKED FINE SAND/TILL		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP9 - TEST PIT NO. 9	0'-12" 12'-7" 7'-11" LOAMY TOPSOIL FINE/MEDIUM GRAY SAND FINE PACKED SILTY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				
TP10 - TEST PIT NO. 10	0'-12" 12'-7.75' 7.75'-10" LOAMY TOPSOIL FINE/MEDIUM GRAY SAND FINE PACKED SILTY SAND		NO MOTTLING OBSERVED NO GROUNDWATER OBSERVED				

WWTS OPERATION & MAINTENANCE NOTES:

- EFFLUENT FILTER TO BE INSPECTED AND CLEANED EVERY 2 MONTHS OR AS NEEDED. INSPECTION AND CLEANING SHALL BE THE RESPONSIBILITY OF THE OWNER.
- OWNER SHALL BE RESPONSIBLE FOR COORDINATING SEPTIC TANK PUMPING EVERY 2 YEARS MAXIMUM. ANNUAL PUMPING MAY BE REQUIRED BASED ON QUANTITY OF SOLID BUILD-UP IN SEPTIC TANK.
- OWNER SHALL AVOID DISPOSAL OF WIPES, PAPER TOWELS, COOKING OIL/GREASE, FOOD SCRAPS, ECT TO HOUSE SEWAGE SYSTEM AND TO WASTEWATER DISPOSAL SYSTEM.
- STRONG CHEMICALS INCLUDING BUT NOT LIMITED TO BACTERIAL DESTROYING PRODUCTS, DRAIN CLEANERS, SOLVENTS, PAINT, PAINT THINNERS, FLOOR CLEANERS, SINK CLEANERS, OILS, ANTIFREEZE, AND PESTICIDES SHALL NOT BE DISPOSED OF TO WASTEWATER DISPOSAL SYSTEM.
- OWNER SHALL BE RESPONSIBLE FOR INSPECTION AND MAINTENANCE OF THE ROOF LEADER DRAIN(S) AND PERIMETER UNDERDRAIN DISCHARGE AND REMOVE ANY BLOCKAGE AS NEEDED TO ENSURE PROPER FLOW AND DISCHARGE.

SEPTIC TANK

SEPTIC TANK SHALL BE 1,750 GALLON SEAMLESS DUAL COMPARTMENT PRECAST CONCRETE TANK. EFFLUENT FILTER, POLYLOK PL-122 OR EQUAL, SHALL BE INSTALLED ON OUTLET SIDE OF SEPTIC TANK. (ADD 250 GALLONS FOR FOR GARBAGE GRINDER, ADD 250 GALLONS FOR WHIRLPOOL, SPA).

DISTRIBUTION BOX

TO BE PRECAST CONCRETE BOX AND COVER WITH SPEED LEVELERS BY GUARDIAN CONCRETE, INC. OR EQUIVALENT.

BUILDING TO SEPTIC TANK

EXISTING 4" PVC SCH 40 WITH TIGHT JOINTS, MINIMUM SLOPE: 1/4" PER FOOT.

SEPTIC TANK TO DISTRIBUTION BOX

4" PVC SDR35 WITH TIGHT JOINTS, MINIMUM SLOPE: 1/8" PER FOOT.

DISTRIBUTION BOX TO LATERALS

4" PVC SDR35 WITH TIGHT JOINTS, MINIMUM SLOPE 1/16" TO 1/32" PER FOOT.

DISTRIBUTION LATERALS

4" PVC PERFORATED SCHEDULE 20 W/ TIGHT JOINTS, MINIMUM SLOPE 1/16" TO 1/32" PER FOOT.

REQUIRED INSPECTIONS:

ENGINEER SHALL INSPECT SYSTEM CONSTRUCTION AT THE FOLLOWING STAGES OF CONSTRUCTION.

INSPECTION #1: UPON COMPLETION OF INSTALLATION OF NEW ABSORPTION TRENCHES, SEPTIC TANK EFFLUENT FILTER, AND DISTRIBUTION BOX DESIGN ENGINEER SHALL BE NOTIFIED TO COMPLETE INSPECTION.

INSPECTION #2: UPON COMPLETION OF FINAL GRADING INCLUDING PLACEMENT OF TOPSOIL AND FINAL SEEDING.

NOTE: OWNER IS RESPONSIBLE FOR NOTIFYING THE ENGINEER A MINIMUM OF 24 HRS. IN ADVANCE OF EACH REQUIRED INSPECTION. IF WORK COMMENCES WITHOUT THE NOTED INSPECTIONS, THE ENGINEER WILL NOT BE ABLE TO CERTIFY THE SYSTEM AS-BUILT PER PLAN

DESIGN CALCULATIONS:

SEPTIC SYSTEM FLOW ANALYSIS:

THE DAILY DESIGN FLOW IS BASED ON 15 GPD PER EMPLOYEE, PER NYSDOH RESIDENTIAL ONSITE WASTEWATER TREATMENT SYSTEMS DESIGN HANDBOOK

FLOW ANALYSIS: 15 GALLONS PER DAY PER EMPLOYEE X 61 EMPLOYEES (PER OWNER)= 915 GPD

THE STABILIZED PERCOLATION TEST RESULTS WITHIN THE FIELD AREA ARE BETWEEN 3:04 MIN/IN AND 4:55 MIN/INCH. AS A RESULT, A CONSERVATIVE RANGE OF 6 TO 7 MIN/IN PERCOLATION RATE HAS BEEN UTILIZED FOR DESIGN PURPOSES.

APPLICATION RATE: 6 TO 7 MIN/IN PERCOLATION RATE = 1.0 GPD/SF

915 GPD/(1.0 GPD/SF)= 915 SF

915 SF/(2 SF/LF) = 457.5 = 458 LF OF LATERAL MINIMUM

BASED ON THE CALCULATIONS ABOVE, THE TOTAL ABSORPTION TRENCH LENGTH SHALL BE 458 LF MINIMUM. THE LENGTH OF THE PROPOSED ABSORPTION TRENCH SHALL BE 8 LATERALS AT 60 FEET EACH MIN.

WASTE WATER TREATMENT SYSTEM SPECIFICATIONS

GENERAL NOTES:


- ALL SEPTIC SYSTEMS ARE TO BE DESIGNED AND CONSTRUCTED IN COMPLIANCE WITH N.Y.S. HEALTH CODE PART 75A, "WASTEWATER TREATMENT STANDARDS - INDIVIDUAL HOUSEHOLD SYSTEMS", PERTAINING TO CONVENTIONAL SYSTEMS.
- BUILDER TO VERIFY GRADE OF SOIL PIPE AT BUILDING PRIOR TO CONSTRUCTION OF SYSTEM.
- NO EXISTING WELLS, PONDS OR WATER COURSES EXISTING WITHIN 100 FEET OF PROPOSED SEWAGE DISPOSAL SYSTEM.
- NO ROOF, FOOTING, FLOOR, COOLING WATER, BACKWASH DRAINS ETC. SHALL BE CONNECTED TO THE SEPTIC SYSTEM.
- ALL ROOF LEADER DOWNSPOUTS TO BE DIRECTED AWAY FROM ALL PARTS OF THE SEPTIC SYSTEM.
- SEPTIC SYSTEM TO BE GRADED TO PROVIDE POSITIVE DRAINAGE AWAY FROM THE SYSTEM.
- SEDIMENT CONTROL FENCE AND/OR STONE CHECK DAMS ARE TO BE INSTALLED AT LIMITS OF DISTURBANCE UNTIL A PERMANENT STAND OF VEGETATION IS ESTABLISHED.
- ANY CHANGE IN CONDITIONS MUST BE BROUGHT TO THE ATTENTION OF THE DESIGN ENGINEER.
- PRIOR TO THE START OF CONSTRUCTION BUILDER TO VERIFY THAT THE BUILDING FINISHED FLOOR AND TANK INVERTS ARE SET TO ACHIEVE REQUIRED SLOPES AND COVER AS INDICATED ON THE PLANS AND DETAILS.
- CERTIFICATION OF THE SYSTEM IS NECESSARY BEFORE A CERTIFICATE OF OCCUPANCY WILL BE ISSUED.
- VEHICULAR TRAFFIC SHALL BE KEPT OFF ALL WASTEWATER DISPOSAL SYSTEM COMPONENTS AT ALL TIMES. BROKEN SYSTEM COMPONENTS AND OVER-COMPACTION OF SOILS WILL RESULT IN SYSTEM FAILURE AND/OR IMPROPER FUNCTION.
- TREES AND SHRUBS SHALL NOT BE PLANTED ON OR WITHIN 6 FEET OF THE WASTEWATER DISPOSAL SYSTEM COMPONENTS.

MINIMUM SEPARATION DISTANCES


BUILDING TO SEPTIC TANK	10' MIN.
BUILDING TO ABSORPTION FIELD	20' MIN.
PROPERTY LINE TO ABSORPTION FIELD	10' MIN.
WATER LINE TO ANY SEPTIC SYSTEM COMPONENT	10' MIN.
WELL TO ABSORPTION FIELD	100' MIN.

GENERAL NOTES:


- CONTRACTOR TO FIELD VERIFY EXISTING GRADES PRIOR TO CONSTRUCTION OF BUILDING AND WWTS. CONTRACTOR TO SET THE BUILDING ELEVATION TO PROVIDE POSITIVE DRAINAGE FROM BUILDING TO WWTS WITHIN THE MINIMUM DESIGN SPECIFICATIONS OUTLINED ON THESE PLANS. DISCREPANCIES TO BE BROUGHT TO THE ATTENTION OF THE DESIGN ENGINEER.

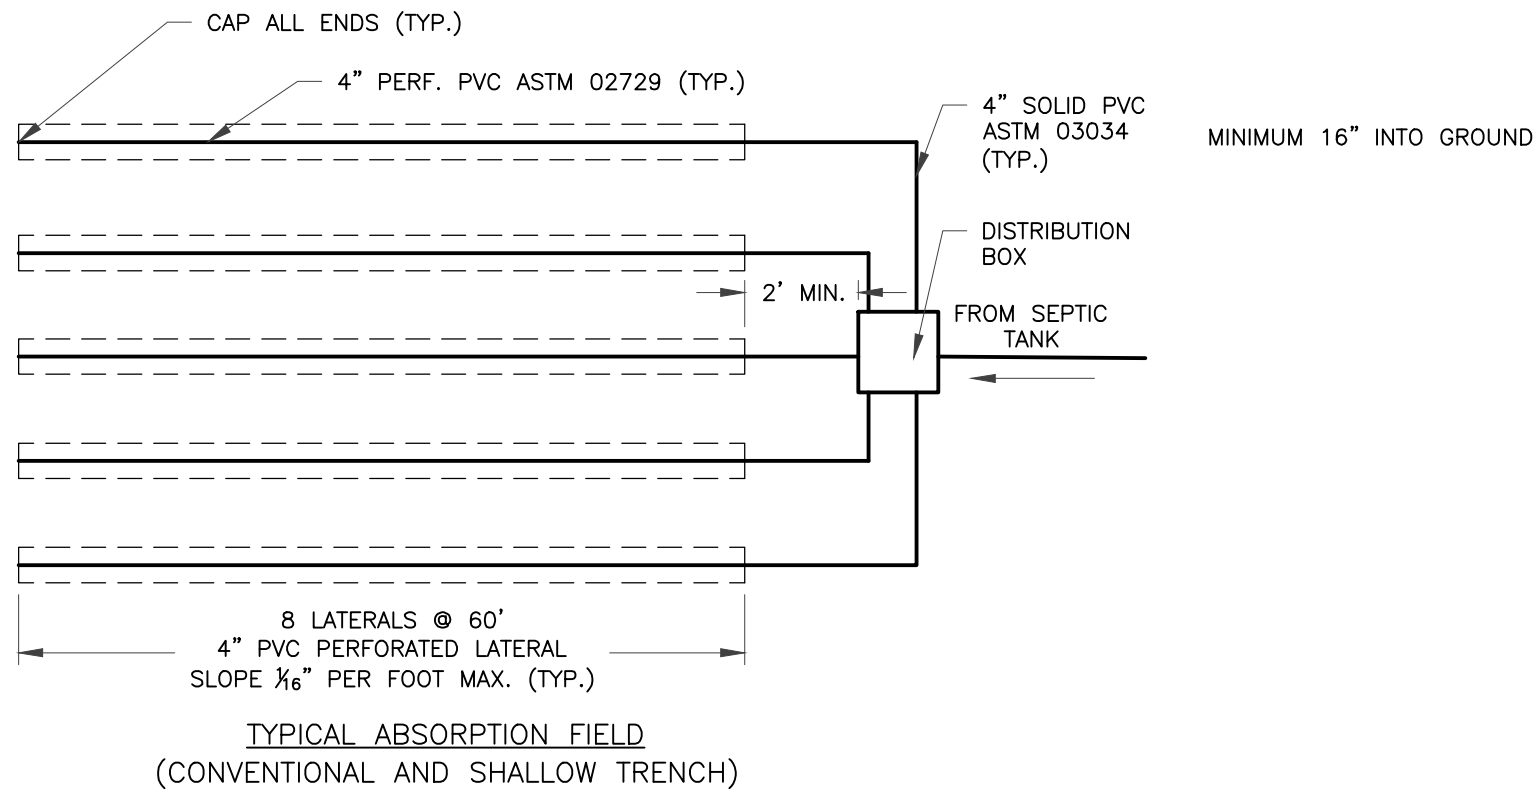


**TYPICAL
ABSORPTION FIELD**
SCALE: NTS

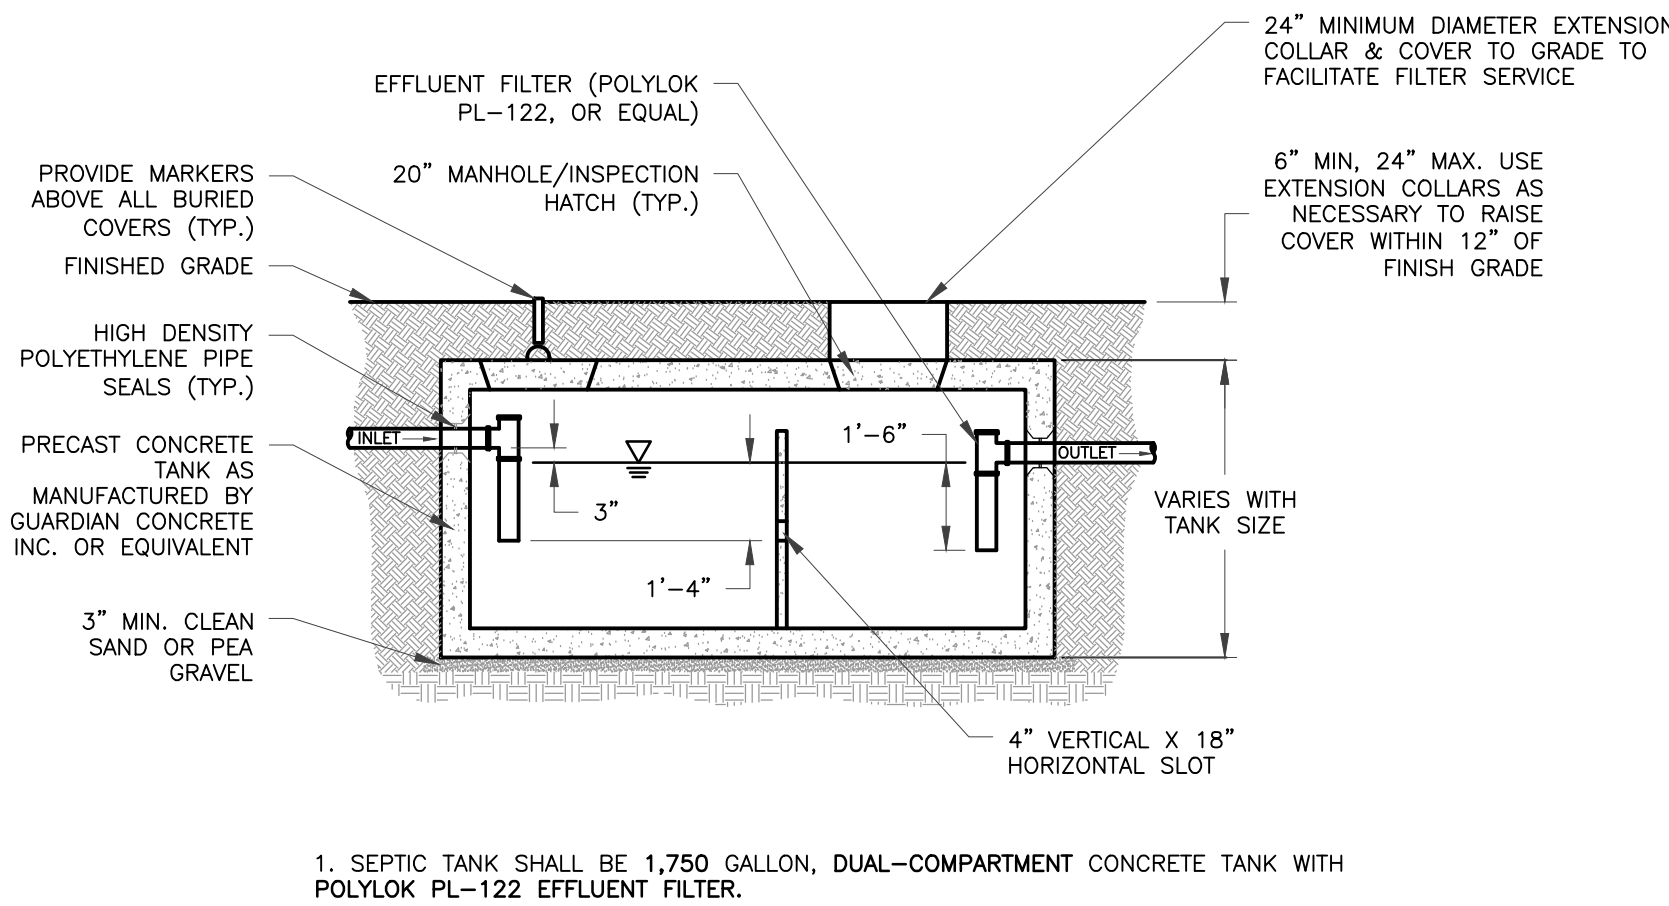


**PRECAST SEPTIC TANK -
(SEAMLESS) DUAL COMPARTMENT**
SCALE: NTS

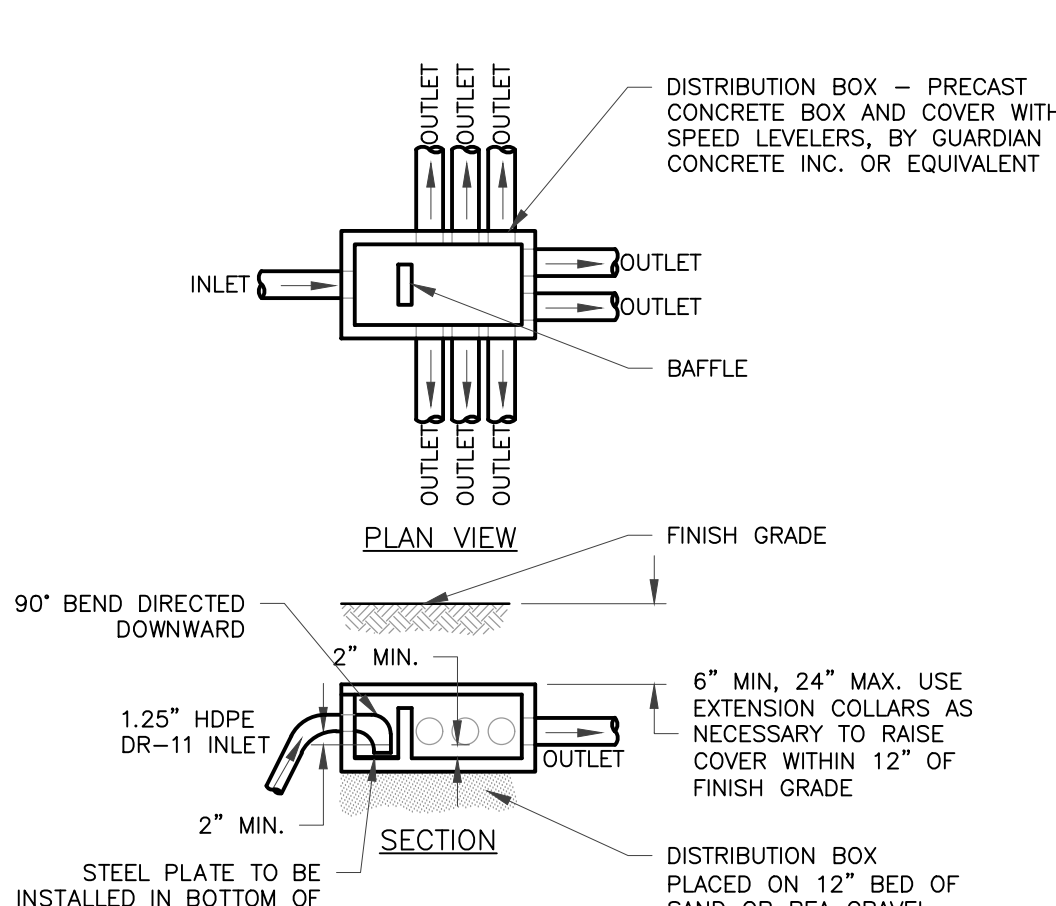


PRECAST DISTRIBUTION BOX
SCALE: NTS

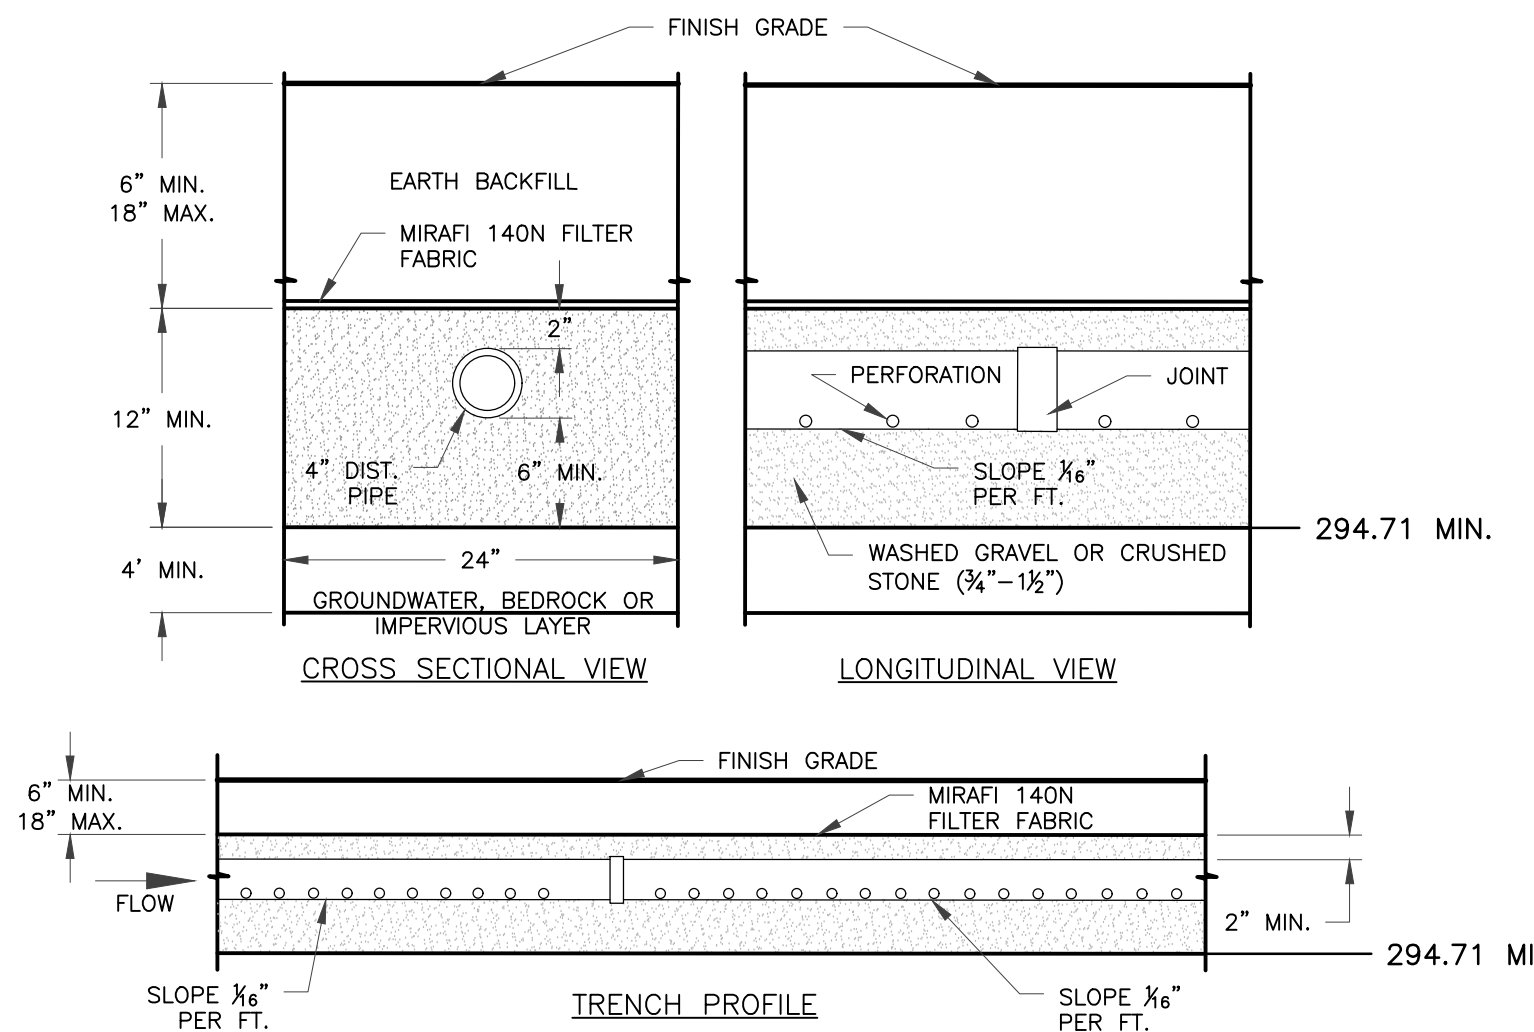

TYPICAL ABSORPTION TRENCH
SCALE: NTS

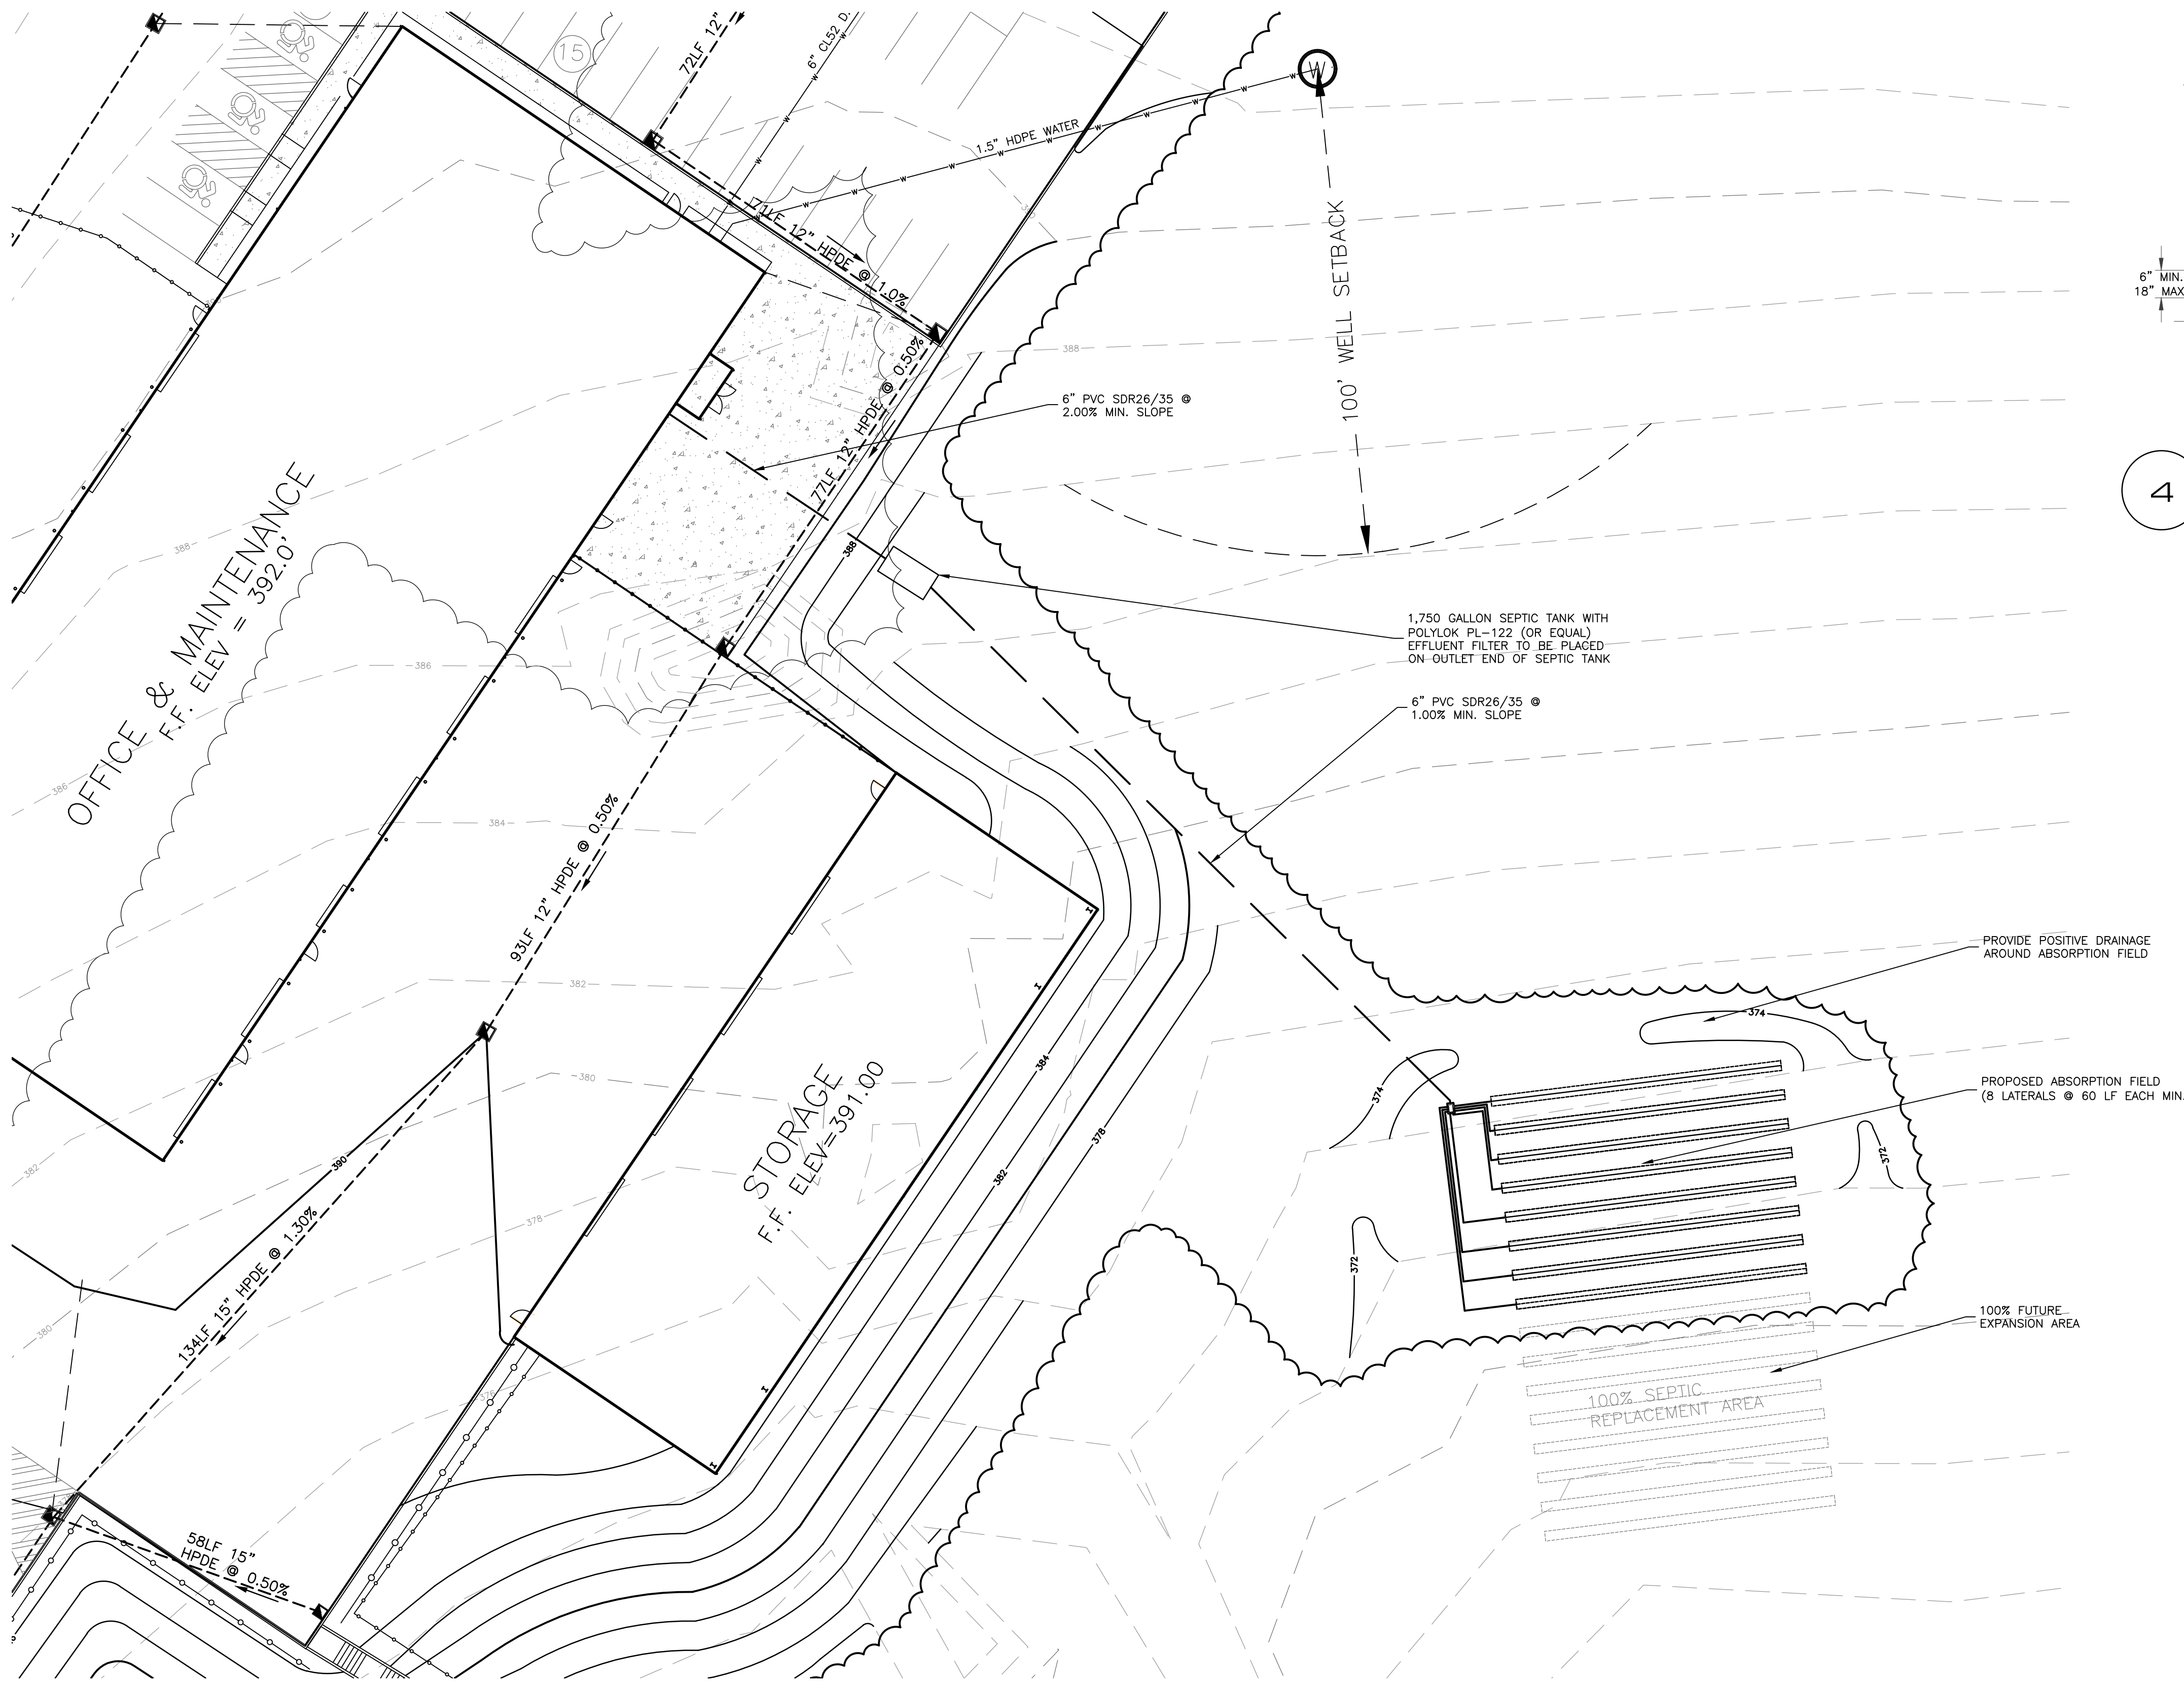

WWTS LAYOUT PLAN



UNAUTHORIZED
REVISIONS TO THIS
DRAWING ARE
PROHIBITED
BY LANSING
ENGINEERING, P.C.

CASELLA - FORT EDWARD HAULING FACILITY SITE PLAN
1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK

REVISION RECORD/DESCRIPTION
DATE
PRELIMINARY / NOT FOR CONSTRUCTION

LANSING
ENGINEERING
2450 N. STATE ST. SUITE 301
VALTIC, NY 12150
(518) 899-8843

WWTS DESIGN
& LAYOUT


PROJ. NO:1238.04
SCALE: AS SHOWN
DATE: 10/01/26

WW-1
SHEET 9 OF 13



1. STONE SIZE - USE MIXTURE OF #2 & #3 STONE (1-4 INCHES), OR RECLAIMED OR RECYCLED CONCRETE EQUIVALENT.
2. LENGTH - NOT LESS THAN 50' (50' FEET) EXCEPT ON A SINGLE RENDON LOT WHERE A THIRTY (30) FOOT MINIMUM LENGTH WOULD APPLY.
3. THICKNESS - NOT LESS THAN SIX INCHES.
4. WIDTH - TWENTY (12) FOOT MINIMUM, BUT NOT LESS THAN THE FULL WIDTH AT POINTS WHERE INGRESS OR EGRESS OCCURS, TWENTY-FOUR (24) FOOT IF SINGLE ENTRANCE TO LOT.
5. SURFACE - NOT TO BE PLACED OVER ANY EXISTING DRIVE OR DRIVE APPROACH.
6. SURFACE WATER - ALL SURFACE WATER FLOWING OR DIVERTED TOWARD CONSTRUCTION SHALL BE DIVERTED ACROSS THE DRIVE APPROACH TO THE MOUNTAINABLE BERM WITH 5:1 SLOPES WILL BE PERMITTED.
7. WHEN THE MOUNTAINABLE BERM IS NOT AVAILABLE AS A CONDITION WHICH WILL PREVENT TRACKING OR FLOWING OF SEDIMENT INTO PERMITS OR RIGHTS-OF-WAY, ALL SEDIMENT SPILLED, TRACKED, OR FLOWED ONTO PUBLIC RIGHTS-OF-WAY SHALL BE IMMEDIATELY CLEANED UP.
8. WHEN MAINTENANCE IS REQUIRED, IT SHALL BE DONE ON AN AREA STABILIZED WITH STONE AND WHICH DRAINAGE IS AN APPROVED SEDIMENT TRAPPING DEVICE.
9. INSPECTION - INSPECTION SHALL BE REQUIRED AND PROVIDED AFTER EACH RAIN.


SCALE: NTS



1. FABRIC SHALL HAVE AN EOS OF 40-85. BURLAP MAY BE USED FOR SHORT TERM APPLICATIONS.
2. CUT FABRIC FROM A CONTINUOUS ROLL TO ELIMINATE JOINTS. IF JOINTS ARE NEEDED THEY WILL BE OVERLAPPED TO THE NEXT STAKE.
3. STAKE MATERIALS WILL BE DRIVEN IN AT 2" x 4" WOOD OR EQUIVALENT, METAL, WITH A MINIMUM LENGTH OF 3 FEET.
4. SPACE STAKES EVENLY AROUND INLET 12" APART AND DRIVE A MINIMUM 18 INCHES DEEP. SPANS GREATER THAN 3 FEET MAY BE BRIDGED WITH THE STAKE MATERIALS, DRIVING THE RIGID STAKE FOR SUPPORT.
5. FABRIC SHALL BE EMBEDDED 1 FOOT MINIMUM BELOW GROUND AND BACKFILLED, IT SHALL BE SECURELY FASTENED TO THE STAKES AND FRAME.
6. IF A WOOD STAKE IS USED, IT SHALL BE COMPLETED AROUND THE CREST OF THE FABRIC, FOR OVER FLOW STABILITY.

**MAXIMUM DRAINAGE AREA 1 ACRE.

SCALE: NTS




1. WOVEN WIRE FENCE TO BE FASTENED SECURELY TO FENCE POSTS WITH WIRE TIES OR STAPLES. POSTS SHALL BE STEEL EITHER "T" OR "U" TYPE OR HARDWOOD.
2. FILTER CLOTH TO BE TO BE FASTENED SECURELY TO WOVEN WIRE FENCE WITH TIES SPACED EVERY 24" AT TOP AND MID SECTION. FENCE SHALL BE WOVEN WIRE, 12% GA. 6" MAXIMUM MESH OPENING.
3. WHEN TWO SECTIONS OF FILTER CLOTH ADJOIN EACH OTHER THEY SHALL BE OVERLAPPED BY (6) INCHES. FILTER CLOTH SHALL BE EITHER FILTER U, MIRAFI 100X, STABILINKA 1140N, OR APPROVED EQUIVALENT.
4. PREFABRICATED UNITS SHALL BE GEOFAB, ENVROFENCE, OR APPROVED EQUIVALENT.
5. MAINTENANCE SHALL BE PERFORMED AS NEEDED AND MATERIAL REMOVED WHEN "BULGES" DEVELOP IN THE SILT FENCE.


		SLOPE LENGTH/FENCE LENGTH (FT)		
SLOPE	STEEPNESS	STANDARD	REINFORCED	SUPER
<2%	<50:1	300/1500	N/A	N/A
2-10%	50:1 TO 10:1	125/1000	250/2000	300/2500
10-20%	10:1 TO 5:1	100/750	150/1000	200/1000
20-33%	5:1 TO 3:1	60/500	80/750	100/1000
33-50%	3:1 TO 2:1	40/250	70/350	100/500
>50%	>2:1	20/125	30/175	50/250

STANDARD SILT FENCE (SF) IS FABRIC ROLLS STAPLED TO WOODEN STAKES DRIVEN 16" IN THE GROUND.
REINFORCED SILT FENCE (RSF) IS FABRIC PLACED AGAINST WELDED WIRE FABRIC WITH ANCHORED STEEL POSTS DRIVEN 16" IN THE GROUND.
SUPER SILT FENCE (SSF) IS FABRIC PLACED AGAINST CHAIN LINK FENCE AS SUPPORT BACKING WITH POSTS DRIVEN 3' IN THE GROUND.


SCALE: NTS

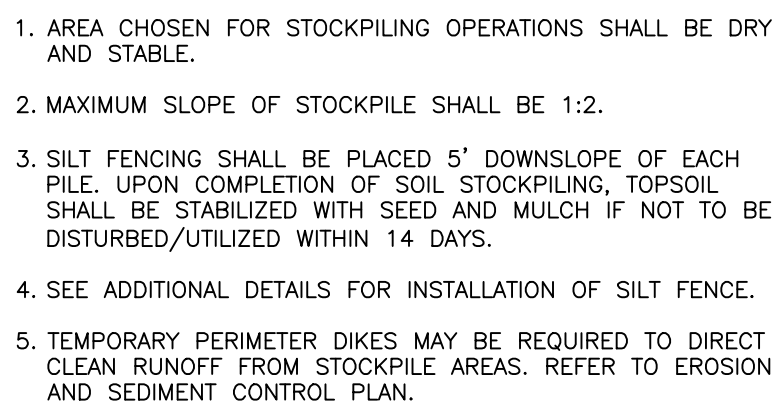

FUEL OR MATERIAL STORAGE AREA

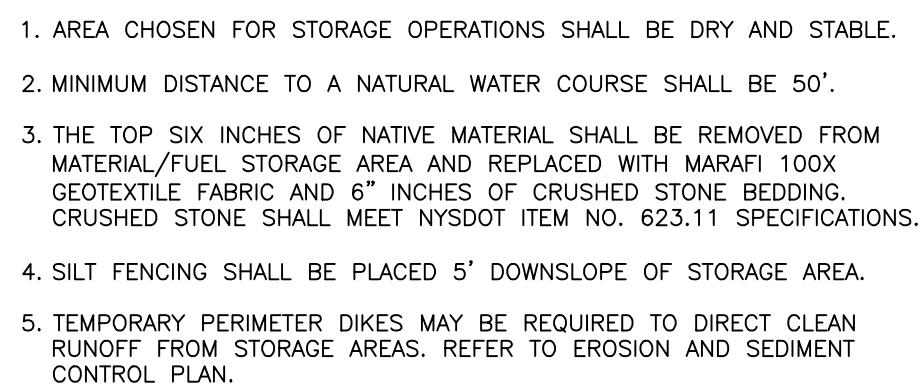


SCALE: NTS



1. CONCRETE WASHOUT LOCATION SHALL BE A MINIMUM OF 100' FROM SENSITIVE AREAS.
2. THE BASIN DIMENSIONS DEPICTED ABOVE ARE REQUIRED MINIMUMS. CONCRETE WASHOUT FACILITY SHALL BE CONSTRUCTED AND MAINTAINED IN SUFFICIENT QUANTITY AND SIZE TO CONTAIN ALL LIQUID AND CONCRETE WASTE GENERATED BY WASHOUT OPERATIONS. (APPROX. 60 GAL. OF WATER/WASTE PER CUM YD OF CONCRETE)
3. PLASTIC LINING MATERIAL SHALL BE 10 MIL(MINIMUM) POLY SHEETING AND BE FREE OF HOLES, TEARS, OR OTHER DEFECTS THAT COMPROMISE THE IMPERMEABILITY OF THE MATERIAL. LINING SHALL BE COVERED BY A MINIMUM OF 12" OF THE FIT WITH AN EARTHEN BERM, SAND BAGS, OR STONE.
4. WASHOUT FACILITY MUST BE CLEANED OR NEW FACILITIES MUST BE CONSTRUCTED AND READY FOR USE ONCE THE WASHOUT IS 75% FULL.







SCALE: NTS

- ### MAINTENANCE AND CLEANING
1. DO NOT DISCHARGE LIQUID OR SLURRY TO WATERWAYS, STORM DRAINS OR DIRECTLY ONTO GROUND.
 2. DO NOT USE SANITARY SEWER WITHOUT LOCAL APPROVAL.
 3. PLACE A SECURE NON-COLLAPSING, NON-WATER COLLECTING COVER OVER AS NECESSARY PRIOR TO PREDICTED WET WEATHER TO PREVENT ACCUMULATION AND OVERFLOW.
 4. REMOVE AND DISPOSE OF HARDENED CONCRETE AND RETURN THE STRUCTURE TO A FUNCTIONAL STATE.
 5. INSPECT THE WASHOUT FACILITY FOR SIGNS OF WEAKENING OR DAMAGE AND REPAIR OR REPLACE AS NECESSARY. LINE THE STRUCTURE WITH NEW POLY SHEETING AFTER EACH CLEANING).





1. STONE WILL BE PLACED ON A FILTER FABRIC FOUNDATION TO THE LINES, GRADES AND LOCATIONS SHOWN IN THE PLAN.
2. SET SPACING OF CHECK DAMS TO ASSUME THAT THE ELEVATIONS OF THE CREST OF THE DOWNSTREAM DAM IS AT THE SAME ELEVATION OF THE TOE OF THE UPSTREAM DAM.
3. EXTEND THE STONE A MINIMUM OF 1.5 FEET BEYOND THE DITCH BANKS TO PREVENT CUTTING AROUND THE DAM.
4. PROVIDE CHANNEL DOWNSTREAM OF THE LOWEST CHECK DAM FROM SCOUR AND EROSION WITH STONE OR LINER AS APPROPRIATE.
5. ENSURE THAT CHANNEL APPEARANCES SUCH AS CULVERT ENTRANCES BELOW CHECK DAMS ARE NOT SUBJECT TO DAMAGE OR BLOCKAGE FROM DISPLACED STONE. MAXIMUM DRAINAGE AREA TWO (2) ACRES.

SCALE: NTS

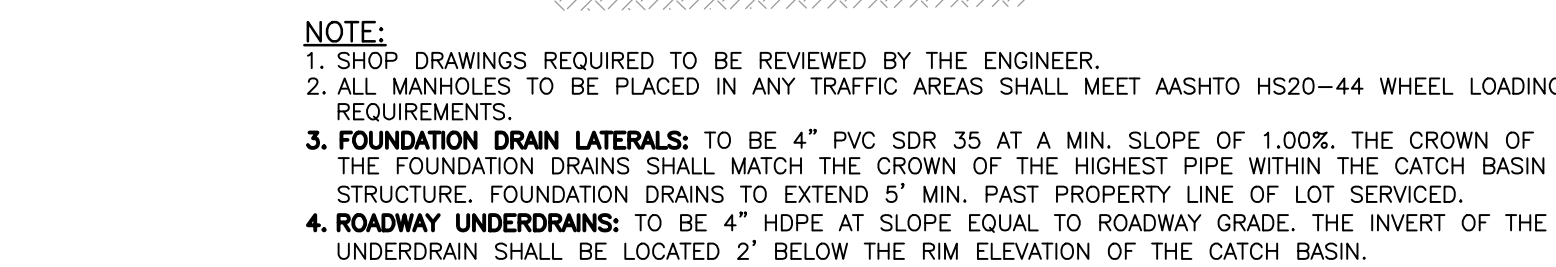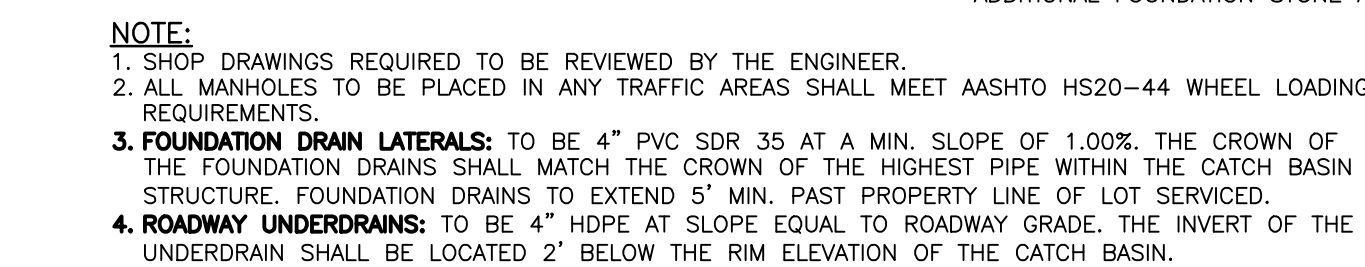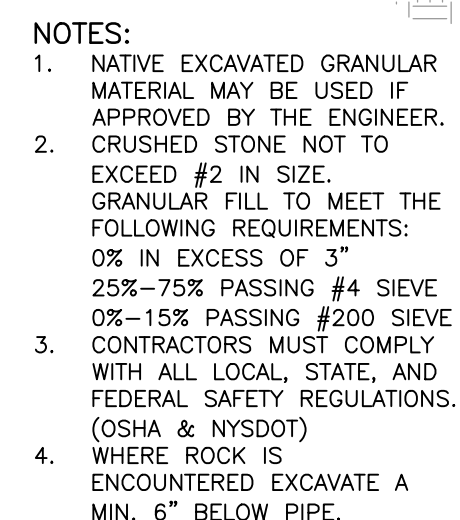


PAPER SIZE (in.)	PAPER SPEED	STONE FILLED APPROX. DESIGN*			
		STONE FILLED (in.)	STONE FILLING	APPROX. DESIGN (in.)	APPROX. DESIGN (in.)
12	0-3%	1	LIGHT	18	10
	5-7%	6	LIGHT	18	14
	7-10%	9	MEDIUM	24	15
15,18	0-3%	6	LIGHT	18	14
	2-5%	9	MEDIUM	24	20
	5-10%	12	MEDIUM	30	24
24	0-1%	6	MEDIUM	24	14
	1-2%	9	MEDIUM	30	20
	2-3%	12	MEDIUM	36	26
30	5-8%	18	HEAVY	36	30
	0-3%	12	MEDIUM	28	28
	3-6%	18	HEAVY	36	36
36	0-1%	9	MEDIUM	24	22
	1-5%	15	HEAVY	36	32
	2-4%	18	HEAVY	36	40
42	4-6%	21	HEAVY	36	45
	0-1%	12	HEAVY	28	28
	1-2%	15	HEAVY	36	36
48	2-3%	18	HEAVY	36	42
	3-4%	21	HEAVY	36	45
	0-1%	12	MEDIUM	28	32
60	1-2%	18	HEAVY	36	42
	3-5%	24	HEAVY	44	48
	0-1%	24	HEAVY	44	52
60	3-4%	18	HEAVY	32	44
	1-2%	24	HEAVY	43	58
	2-3%	30	HEAVY	54	66
60	5-6%	33	HEAVY	59	70

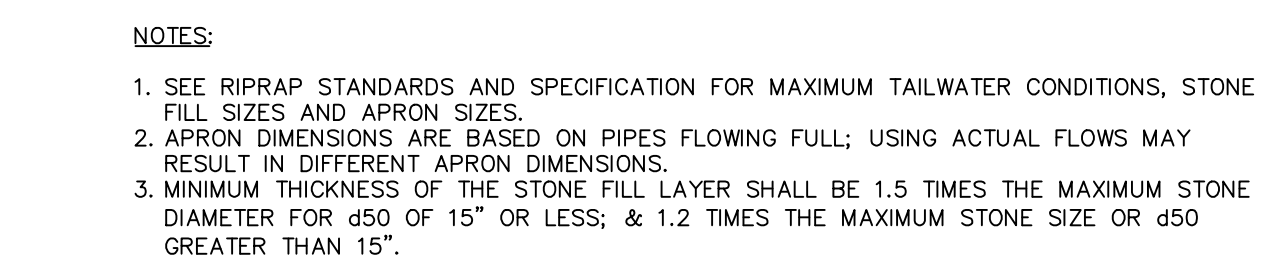


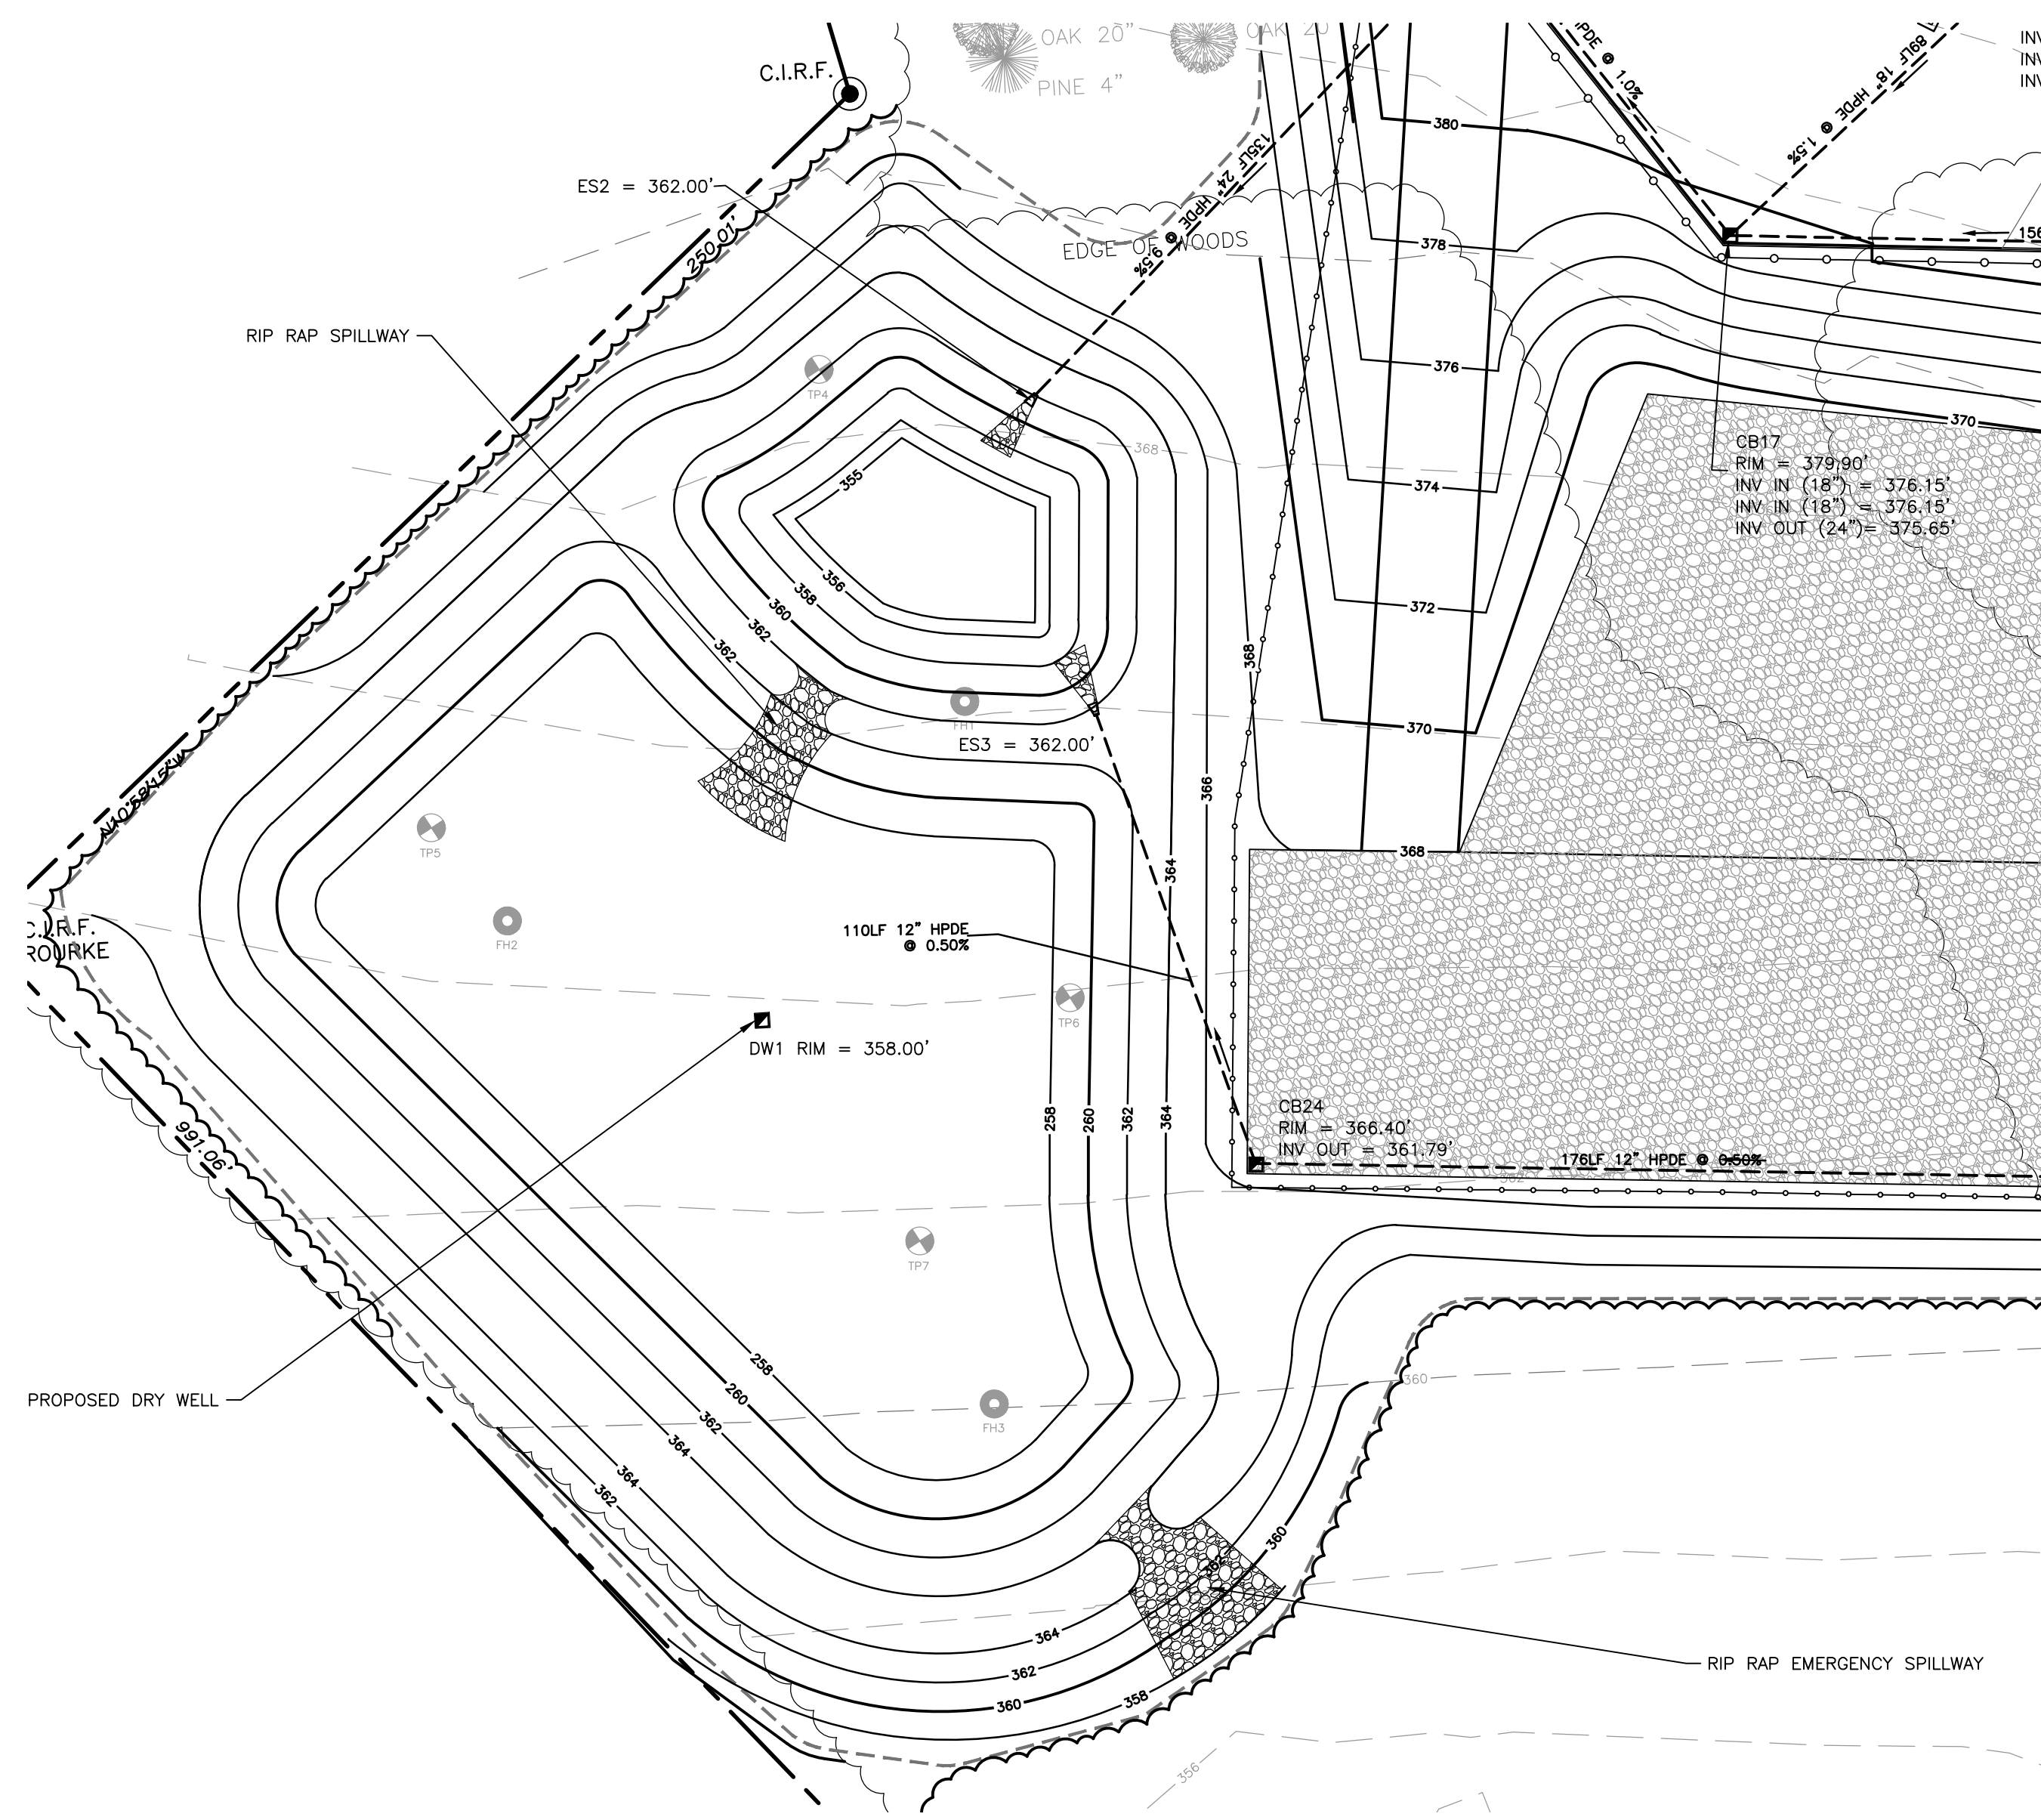

1 STORMWATER INFILTRATION BASIN 1
SCALE: 1"=30'

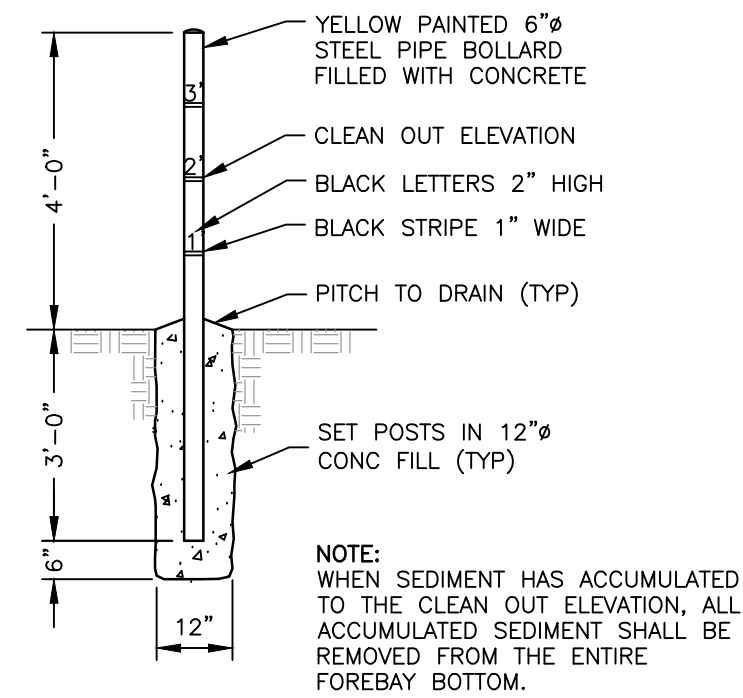


3 SEDIMENT DEPTH MARKER
SCALE: NTS

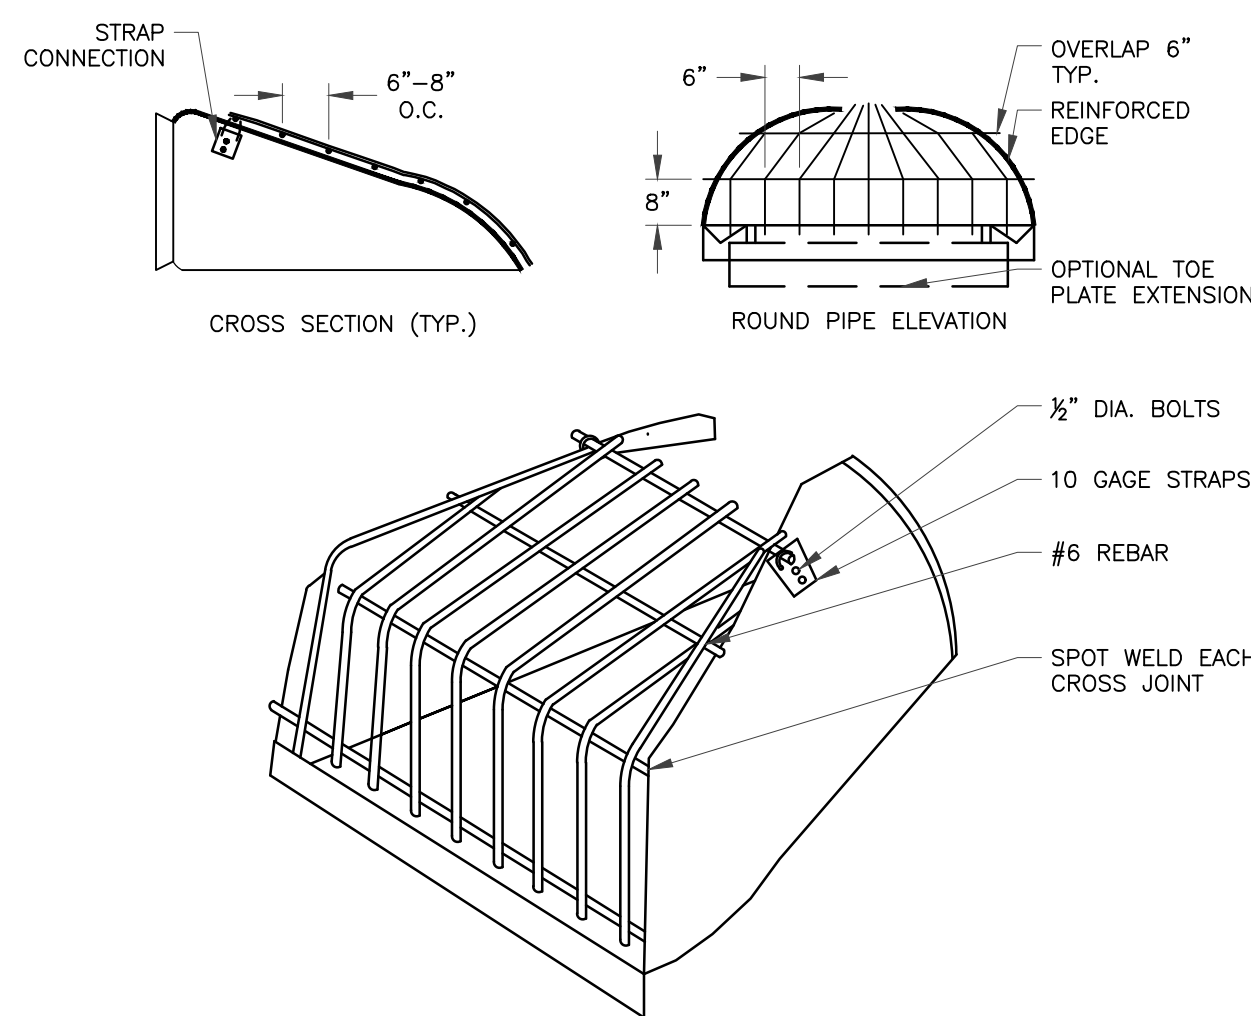

4 EXTERNAL TRASH RACK
SCALE: NTS


EMBANKMENT FILL NOTES:

- EMBANKMENT FILL FOR THE STORMWATER BASIN BERM SHALL CONSIST OF A CLEAN WELL GRADED MIXTURE OF SILT, CLAY, SAND AND GRAVEL WITH NO PARTICLES LARGER THAN (6) INCHES. EXCAVATED ON SITE SOILS SHALL BE SELECTIVELY STOCKPILED FOR USE AS EMBANKMENT FILL IN AREAS DESIGNATED BY THE ENGINEER. SOIL SUITABLE FOR USE AS EMBANKMENT FILL SHALL HAVE AT LEAST 40% BY WEIGHT FINER THAN THE NO. 200 SIEVE AND NO MORE THAN 15% BY WEIGHT COARSER THAN THE NO. 4 SIEVE. THE FILL SHALL BE FREE OF VEGETATION, ORGANIC MATERIAL AND FROZEN SOIL.
- ALL FILL SHALL BE PLACED IN LIFTS NOT EXCEEDING (8) INCHES IN THICKNESS WHEN LOOSE AND BE COMPACTED TO A DENSITY OF AT LEAST 95% OF THE MAXIMUM DRY DENSITY AS DETERMINED IN ACCORDANCE WITH ASTM-1557.
- ACCEPTABLE POND LINER OPTIONS INCLUDE: A) 6"-12" OF CLAY SOIL (MINIMUM 50% PASSING THE #200 SIEVE AND A MAXIMUM PERMEABILITY OF 0.00001 CM/SEC), OR B) A 30 MIL POLYLINER.
- THE STABILIZED ACCESS ROAD SHALL CONSIST OF (12) INCHES OF COMPACTED NYSDOT ITEM NO. 304.12.

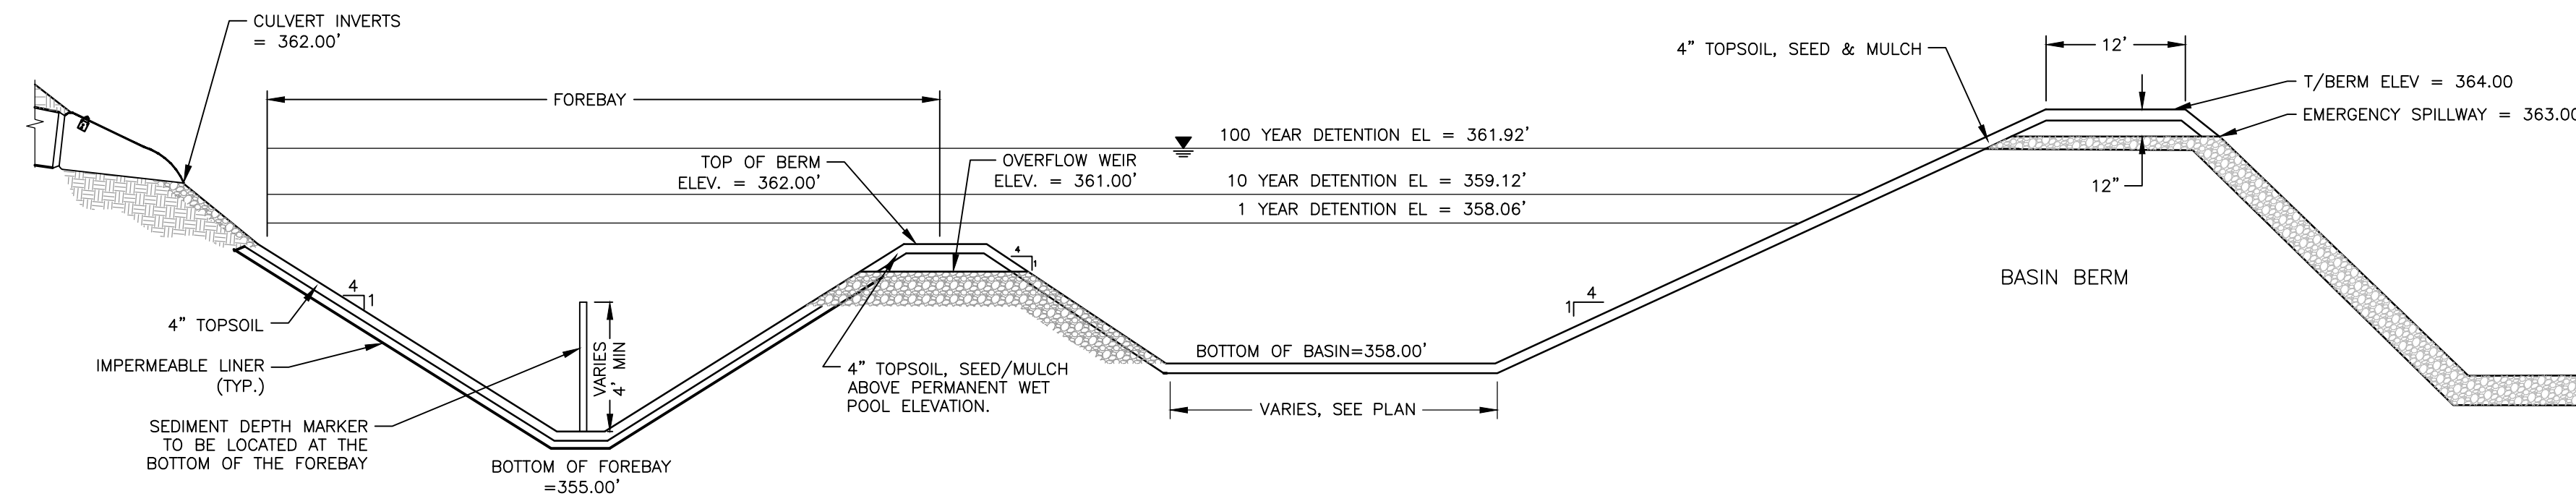

2 STORMWATER INFILTRATION BASIN 1
SCALE: NTS

PH1 - FALLING HEAD TEST 1 4' BELOW GRADE IN MEDIUM SAND	60 IN/HR
PH2 - FALLING HEAD TEST 2 4.5' BELOW GRADE IN TILL LAYER	5.75 IN/HR
PH3 - FALLING HEAD TEST 3 4' BELOW GRADE IN MEDIUM SAND	60 IN/HR

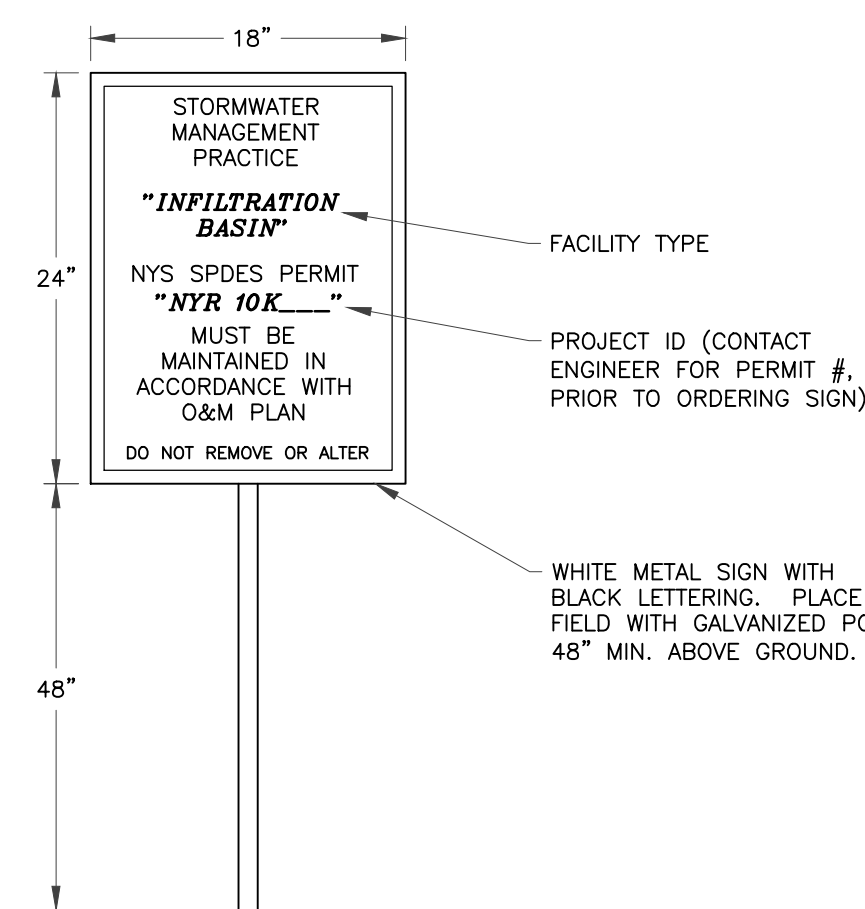


- NOTE:
- SIGNS TO BE PLACED AT ALL STORMWATER MANAGEMENT PRACTICES IN ACCORDANCE WITH SECTION 3.5 OF THE NYS STORMWATER DESIGN MANUAL.
 - "FACILITY TYPE" SHALL BE APPROPRIATE FOR THE ASSOCIATED STORMWATER MANAGEMENT PRACTICE: SEE TABLE 1.
 - USE 10"x12" SIGN FOR STORM PRACTICES SMALLER THAN 400 SF.


TABLE 1

EXAMPLE FACILITY TYPES
MICROPOOL DETENTION
INFILTRATION BASIN
BIORETENTION
RAIN GARDEN
VEGETATED SWALE
INFILTRATION TRENCH
POROUS PAVEMENT
VEGETATED BUFFER


5 STORMWATER MANAGEMENT FACILITY NOTIFICATION SIGN
SCALE: NTS

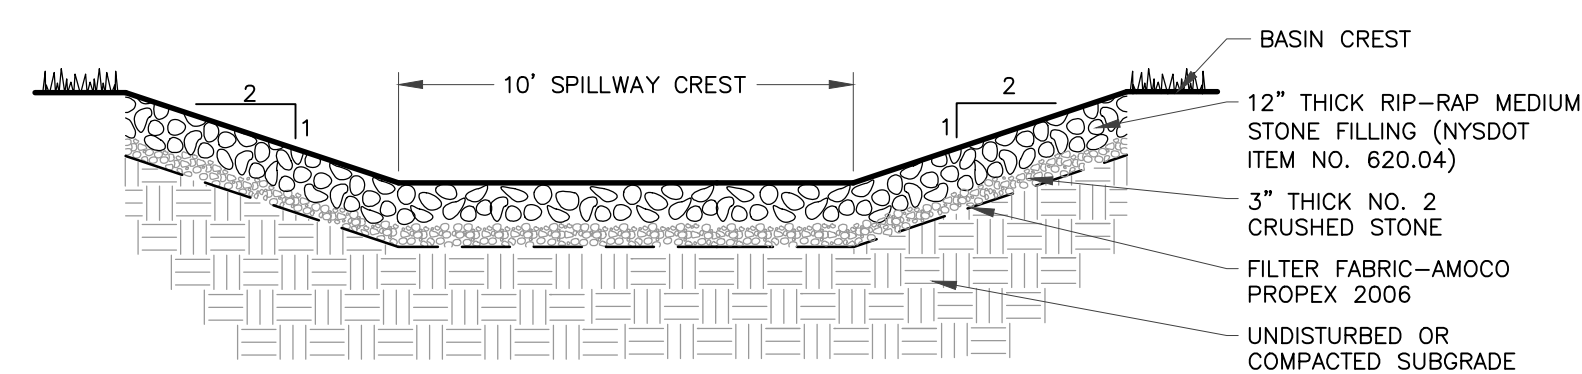

6 EMERGENCY SPILLWAY CROSS SECTION
SCALE: NTS

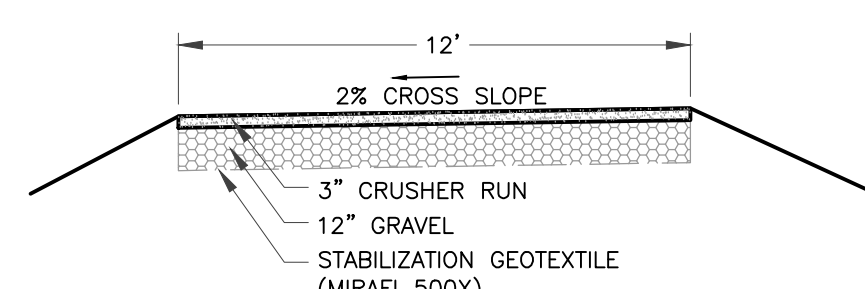

7 PROPOSED SWMB GRAVEL MAINTENANCE ACCESS DRIVE SECTION
SCALE: NTS

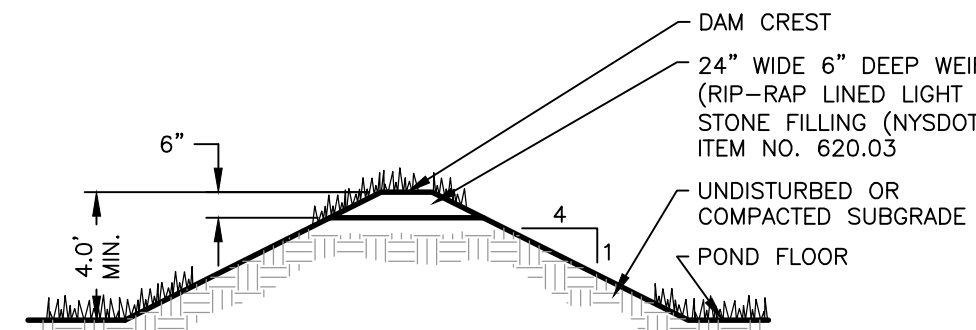

8 FOREBAY DAM/WEIR SECTION
SCALE: NTS

UNAUTHORIZED
REVISIONS TO THIS
DRAWING ARE
PROHIBITED
BY THE NYS
DEPARTMENT OF
TRANSPORTATION
AND PLANNING
DIVISION
LANSING ENGINEERING, P.C.

CASELLA - FORT EDWARD HAULING FACILITY SITE PLAN
1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK

REVISION RECORD/DESCRIPTION
DATE
PRELIMINARY / NOT FOR CONSTRUCTION

LANSING
ENGINEERING
2025
1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK
1132-1148 ROUTE 9, TOWN OF MOREAU, SARATOGA COUNTY, NEW YORK

BASIN DETAILS

Appendix F

NYSDEC SPDES General Permit GP-0-25-001



Department of
Environmental
Conservation

NEW YORK STATE
DEPARTMENT OF ENVIRONMENTAL
CONSERVATION (NYSDEC)

SPDES GENERAL PERMIT
FOR STORMWATER DISCHARGES

From

CONSTRUCTION ACTIVITY

Permit No. GP-0-25-001

Construction General Permit (CGP)

Issued Pursuant to Article 17, Titles 7, 8 and Article 70
of the Environmental Conservation Law

Effective Date: January 29, 2025

Expiration Date: January 28, 2030

Scott E. Sheeley

Chief Permit Administrator

A handwritten signature in blue ink, reading "Scott E. Sheeley". The signature is written over a horizontal line.

Authorized Signature

A handwritten date in blue ink, reading "JAN. 29, 2025". The date is written over a horizontal line.

Date

Address: NYSDEC
Division of Environmental Permits
625 Broadway, 4th Floor
Albany, N.Y. 12233-1750

PREFACE

Pursuant to Section 402 of the Clean Water Act (CWA), and 40 CFR 122.26(b)(14)(x), (15)(i), and (15)(ii), *stormwater discharges* from certain *construction activities* are unlawful unless they are authorized by a National Pollutant Discharge Elimination System (NPDES) permit or by a state permit program. New York State administers the approved State Pollutant Discharge Elimination System (SPDES) program with permits issued in accordance with the New York State Environmental Conservation Law (ECL) Article 17, Titles 7 and 8, and Article 70, as well as 6 NYCRR Parts 621 and 750.

Construction activities constitute construction of a *point source* and, therefore, pursuant to ECL sections 17-0505, 17-0701, and 17-0803, the *owner or operator* must have coverage under a SPDES permit prior to *commencement of construction activities*. The *owner or operator* cannot wait until there is an actual *discharge* from the *construction site* to obtain permit coverage.

***Note: The italicized words/phrases within this permit are defined in Appendix A.**

**NEW YORK STATE DEPARTMENT OF ENVIRONMENTAL CONSERVATION
SPDES CONSTRUCTION GENERAL PERMIT (CGP) GP-0-25-001
FOR STORMWATER DISCHARGES FROM CONSTRUCTION ACTIVITIES**

Table of Contents

Part I. How to Obtain Coverage and General Requirements	5
A. Eligibility Requirements	5
B. Types of <i>Discharges</i> Authorized	9
C. Prohibited <i>Discharges</i>	10
D. Electronic Notice of Intent (eNOI) Submittal.....	10
E. General Requirements for <i>Owners or Operators</i> with Permit Coverage	14
F. Permit Coverage for <i>Discharges</i> Authorized Under GP-0-20-001	18
G. Change of <i>Owner or Operator</i>	19
Part II. Water Quality-Based Effluent Limitations	20
A. Maintaining Water Quality	20
B. Effluent Limitations Applicable to <i>Discharges</i> from <i>Construction Activities</i>	20
C. Post-Construction Stormwater Management Practice (SMP) Requirements ...	23
Part III. Stormwater Pollution Prevention Plan (SWPPP)	28
A. General SWPPP Requirements	28
B. Required SWPPP Contents	32
C. Required SWPPP Components by Project Type.....	37
Part IV. Inspection and Maintenance Requirements	37
A. General Construction Site Inspection and Maintenance Requirements	37
B. Contractor Maintenance Inspection Requirements	37
C. <i>Qualified Inspector</i> Inspection Requirements.....	38
Part V. How to Terminate CGP Coverage.....	43
A. Electronic Notice of Termination (eNOT) Submittal.....	43
Part VI. Record Retention and Reporting.....	45
A. Record Retention	46
B. Reporting	46
Part VII. Standard Permit Requirements	46
A. Duty to Comply.....	46
B. Need to Halt or Reduce Activity Not a Defense.....	46
C. Penalties	46
D. False Statements	47
E. Re-Opener Clause	47
F. Duty to Mitigate	47
G. Requiring Another General Permit or Individual SPDES Permit.....	47
H. Duty to Provide Information.....	49
I. Extension	49
J. Signatories and Certification	50
K. Inspection and Entry	52
L. Confidentiality of Information.....	53
M. Other Permits May Be Required	53

N.	NYSDEC Orders or Civil Decrees/Judgments.....	53
O.	Property Rights	53
P.	Compliance with Interstate Standards.....	53
Q.	Oil and Hazardous Substance Liability.....	54
R.	Severability.....	54
S.	NYSDEC Approved Forms.....	54
APPENDIX A – Abbreviations and Definitions.....		55
	Abbreviations.....	55
	Definitions.....	56
APPENDIX B – Required SWPPP Components by Project Type.....		64
	Table 1.....	64
	Table 2.....	66
APPENDIX C – Watersheds Requiring Enhanced Phosphorus Removal.....		68
APPENDIX D – Impaired Waterbodies (by Construction Related Pollutants)		74
APPENDIX E – List of NYSDEC Regional Offices.....		80
APPENDIX F – SWPPP Preparer Certification Form		81
APPENDIX G – MS4 SWPPP Acceptance Form		83
APPENDIX H – NYCDEP SWPPP Acceptance/Approval Form		86
APPENDIX I – MS4 No Jurisdiction Form.....		89
APPENDIX J – Owner/Operator Certification Form		91

Part I. How to Obtain Coverage and General Requirements

To be covered under this permit, the *owner or operator* must meet all eligibility requirements in Part I.A. and follow the requirements for obtaining permit coverage in Part I.D., F., or G.

A. Eligibility Requirements

For a *common plan of development or sale*, the *phase(s)* that meet the eligibility requirements in Part I.A. may obtain coverage under this permit even if other *phase(s)* of the same *common plan of development or sale* do not meet the eligibility requirements and require an individual SPDES permit.

1. The *owner's or operator's construction activities* involve soil disturbances of:
 - a. one or more acres; or
 - b. less than one acre which are part of a *common plan of development or sale* that will ultimately disturb one or more acres; or
 - c. less than one acre where NYSDEC has determined that a SPDES permit is required for *stormwater discharges* based on the potential for contribution to a violation of a *water quality standard* or for significant contribution of pollutants to *surface waters of the State*.
 - i. 5,000 square feet or more, but less than one acre, and are in the New York City Watershed located east of the Hudson River, Appendix C Figure 1; or
 - ii. 20,000 square feet or more, but less than one acre, within the municipal boundaries of the City of New York (NYC); or
 - iii. less than 20,000 square feet which are part of a *common plan of development or sale* that will ultimately disturb 20,000 square feet or more, but less than one acre, within the municipal boundaries of NYC; or
 - iv. that creates 5,000 square feet or more of *impervious area* within the municipal boundaries of NYC.

2. *Discharges from the owner's or operator's construction activities* are/were not:

- a. already covered by a different SPDES permit; or
- b. covered under a different SPDES permit that was denied, terminated, or revoked; or
- c. identified in an expired individual SPDES permit that was not renewed; or
- d. required to obtain an individual SPDES permit or another general SPDES permit in accordance with Part VII.K.

3. If *construction activities* may adversely affect a species that is endangered or threatened, the *owner or operator* must obtain a:

- a. permit issued pursuant to 6 NYCRR Part 182 for the project; or
- b. letter issued by NYSDEC of non-jurisdiction pursuant to 6 NYCRR Part 182 for the project.

4. If *construction activities* have the potential to affect an *historic property*, the *owner or operator* must obtain one of the following:

- a. documentation that the *construction activity* is not within an archeological buffer area indicated on the sensitivity map, and that the *construction activity* is not located on or immediately adjacent to a property listed or determined to be eligible for listing on the National or State Registers of Historic Places, and that there is no new permanent building on the *construction site* within the following distances from a building, structure, or object that is more than 50 years old, or if there is such a new permanent building on the *construction site* within those parameters that NYS Office of Parks, Recreation and Historic Preservation (OPRHP), a Historic Preservation Commission of a Certified Local Government, or a qualified preservation professional has determined that the building, structure, or object more than 50 years old is not historically/archeologically significant:
 - i. 1-5 acres of disturbance - 20 feet; or
 - ii. 5-20 acres of disturbance - 50 feet; or

- iii. 20+ acres of disturbance - 100 feet.
- b. NYSDEC consultation form sent to OPRHP,¹ and copied to NYSDEC's Agency Historic Preservation Officer (APO), and
 - i. the State Environmental Quality Review Act (SEQR) Environmental Assessment Form (EAF) with a negative declaration or the Findings Statement, with documentation of OPRHP's agreement with the resolution; or
 - ii. documentation from OPRHP that the *construction activity* will result in No Impact; or
 - iii. documentation from OPRHP providing a determination of No Adverse Impact; or
 - iv. a Letter of Resolution signed by the *owner or operator*, OPRHP and the DEC APO which allows for this *construction activity* to be eligible for coverage under the general permit in terms of the State Historic Preservation Act (SHPA).
- c. documentation of satisfactory compliance with Section 106 of the National Historic Preservation Act for a coterminous project area:
 - i. No Affect; or
 - ii. No Adverse Affect; or
 - iii. Executed Memorandum of Agreement.
- d. documentation that SHPA Section 14.09 has been completed by NYSDEC or another state agency.
- 5. If *construction activities* are subject to SEQR, the *owner or operator* must obtain documentation that SEQR has been satisfied.
- 6. If *construction activities* are not subject to SEQR, but subject to the equivalent environmental review from another New York State or federal agency, the

¹ The consultation form can be submitted, along with other project information, through OPRHP's Cultural Resource Information System (CRIS) portal. If submitted through CRIS, paper copies of the consultation form need not be mailed.

Part I.A.6.

owner or operator must obtain documentation that project review, pursuant to a process equivalent to SEQR from another New York State or federal agency, has been satisfied.

7. If *construction activities* require Uniform Procedures Act (UPA) Permits (see 6 NYCRR Part 621) from NYSDEC, or the equivalent from another New York State or federal agency, the *owner or operator* must:
 - a. obtain all such necessary permits; or
 - b. receive notification from NYSDEC pursuant to 6 NYCRR 621.3(a)(4) excepting Part I.A.7.a.
8. *Construction activities* are not eligible if they meet the following criteria in Part I.A.8.a. or b.:
 - a. For linear transportation and linear utility project types, the *construction activities*:
 - i. are within the watershed of *surface waters of the State* classified as AA or AA-S identified utilizing the Stormwater Interactive Map on NYSDEC's website; and
 - ii. are undertaken on land with no existing *impervious cover*; and
 - iii. disturb two or more acres of *steep slope*.
 - b. For all other project types, the *construction activities*:
 - i. are within the watershed of *surface waters of the State* classified as AA or AA-S identified utilizing the Stormwater Interactive Map on NYSDEC's website; and
 - ii. are undertaken on land with no existing *impervious cover*; and
 - iii. disturb one or more acres of *steep slope*.

B. Types of *Discharges* Authorized

1. The following *stormwater discharges* are authorized under this permit:
 - a. *Stormwater discharges*, including *stormwater* runoff, snowmelt runoff, and surface runoff and drainage, associated with *construction activity*, are authorized under this permit provided that appropriate *stormwater* controls are designed, installed, and maintained in accordance with Part II. and Part III.
 - b. *Stormwater discharges* from construction support activities at the *construction site* (including concrete or asphalt batch plants, equipment staging yards, material storage areas, excavated material disposal areas, and borrow areas) if the following requirements are met:
 - i. The support activity is directly related to the *construction site* required to have permit coverage for *stormwater discharges*; and
 - ii. The support activity is not a commercial operation, nor does it serve multiple unrelated *construction sites*; and
 - iii. The support activity does not continue to operate beyond the completion of the *construction activity* at the site it supports; and
 - iv. *Stormwater* controls are implemented in accordance with Part II. and Part III. for *discharges* from the support activity areas.
2. The following non-*stormwater discharges* associated with *construction activity* are authorized under this permit:
 - a. Non-*stormwater discharges* listed in 6 NYCRR 750-1.2(a)(29)(vi), with the following exception: “*Discharges* from firefighting activities are authorized only when the firefighting activities are emergencies/unplanned”; and
 - b. Non-*stormwater discharges* of waters to which other components have not been added that are used in accordance with the *SWPPP* to control dust or irrigate vegetation in stabilized areas; and
 - c. Uncontaminated *discharges* from *dewatering* operations

3. Authorized *discharges of stormwater* or authorized *discharges* of non-*stormwater*, commingled with a *discharge* authorized by a different SPDES permit and/or a *discharge* that does not require SPDES permit authorization, are also authorized under this permit.

C. Prohibited *Discharges*

1. Non-*stormwater discharges* prohibited under this permit include but are not limited to:
 - a. Wastewater from washout of concrete; and
 - b. Wastewater from washout and cleanout of stucco, paint, form release oils, curing compounds, and other construction materials; and
 - c. Fuels, oils, or other *pollutants* used in vehicle and equipment operation and maintenance; and
 - d. Soaps, solvents, or detergents used in vehicle and equipment washing or external building washdown; and
 - e. Toxic or hazardous substances from a spill or other release.

D. Electronic Notice of Intent (eNOI) Submittal

To receive authorization in accordance with Part I.D.3.b., the *owner or operator* must submit a complete eNOI in accordance with the requirements in Part I.D. The eNOI contains questions to: ensure eligibility requirements in Part I.A. have been met; obtain *owner or operator* contact information; obtain the total area to be disturbed and the existing/future *impervious areas* (rounded to the nearest tenth of an acre); confirm *Traditional Land Use Control MS4 Operator* jurisdiction over construction projects; satisfy the EPA eRule requirements; confirm that the Water Quality-Based Effluent Limitations in Part II. have been met; demonstrate consideration of the future risks due to climate change in accordance with Part III.A.2.; and confirm that the other *Stormwater Pollution Prevention Plan (SWPPP)* requirements in Part III. have been met.

1. An eNOI may be submitted for:
 - a. *construction activities* that are not part of a *common plan of development or sale*; or

- b. an entire *common plan of development or sale*; or
 - c. separate *phase(s)* of a *common plan of development or sale* if the following requirements are met:
 - i. the *common plan of development or sale* meets the eligibility requirements of Part I.A.5. or 6.; and
 - ii. the *phase(s)* meet(s) all other eligibility requirements of Part I.A.; and
 - iii. Part III.C. Required *SWPPP* Components by Project Type is based on the *common plan of development or sale*, not the *phase(s)*; or
 - d. *tree clearing* that is associated with, or will support, a *renewable energy* generation, transmission, or storage project that meets Part I.A.5. and 6., if the *tree clearing*:
 - i. meets all other eligibility requirements of Part I.A.; and
 - ii. will occur in NYSDEC's Regions 3-9; and
 - iii. is not within ¼ mile of a bat hibernaculum protected pursuant to 6 NYCRR Part 182; and
 - iv. will occur between November 1st and March 31st.
2. As prerequisites for submitting an eNOI, the *owner or operator* must:
- a. prepare a *SWPPP* for Part I.D.1.a., b., c., or d. in accordance with Part III.; and
 - b. based on the following criteria, upload the following signature forms signed in accordance with Part VII.J. to the eNOI prior to submission:
 - i. for all eNOIs:
 - 1. the *SWPPP* Preparer Certification Form, Appendix F, signed by the *SWPPP* preparer; and

2. the Owner/Operator Certification Form, Appendix J, signed by the *owner or operator*; and
- ii. if an eNOI includes *construction activities* within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)* that will *discharge* to the *MS4(s)*:
 1. determine if the *Traditional Land Use Control MS4 Operator(s)* have review authority. A *Traditional Land Use Control MS4 Operator* does not have review authority where:
 - a. the *owner or operator* of the *construction activities* in Part I.D.2.b.ii. is the same entity as the *Traditional Land Use Control MS4 Operator* identified in Part I.D.2.b.ii.; or
 - b. there is a statute exempting the *owner or operator* from zoning review by the *Traditional Land Use Control MS4 Operator*; or
 - c. there is no such statute per Part I.D.2.b.ii.1.b., the *Traditional Land Use Control MS4 Operator* concludes, after public hearing, that it does not have zoning review authority in accordance with Legal Memorandum LU14 Updated January 2020 “Governmental Immunity from Zoning and Other Legislation”; and
 2. if the *Traditional Land Use Control MS4 Operator(s)* have review authority, submit the *SWPPP* to the *Traditional Land Use Control MS4 Operator(s)* for review and have:
 - a. if outside the municipal boundaries of NYC: the *MS4 SWPPP Acceptance Form*, Appendix G, signed by the principal executive officer or ranking elected official from the *Traditional Land Use Control MS4 Operator*, or by a duly authorized representative of that person in accordance with Part VII.J.2.; or

- b. if within the municipal boundaries of NYC: The City of New York Department of Environmental Protection (NYCDEP) SWPPP Acceptance/Approval Form, Appendix H, signed by the principal executive officer or ranking elected official from the Traditional Land Use Control MS4 Operator, or by a duly authorized representative of that person in accordance with Part VII.J.2.; and
 - 3. if the *Traditional Land Use Control MS4 Operator* does not have review authority, have the MS4 No Jurisdiction Form, Appendix I, signed by the principal executive officer or ranking elected official from the *Traditional Land Use Control MS4 Operator*, or by a duly authorized representative of that person in accordance with Part VII.J.2.
3. Submitting an eNOI:
- a. The *owner or operator* must submit a complete Notice of Intent electronically using a NYSDEC approved form.²
 - b. The *owner or operator* is authorized to *commence construction activity* as of the authorization date indicated in the Letter of Authorization (LOA), which is sent by NYSDEC after a complete eNOI is submitted.
 - i. If an eNOI is received for a *SWPPP* that deviates from one of the technical standards but demonstrates *equivalence* in accordance with Part III.B.1.a.ii. or Part III.B.2.b.ii., if the *SWPPP* includes *construction activities* that are not within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)*, and/or if the *SWPPP* includes *construction activities* within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)* that do not have review authority in accordance with Part I.D.2.b.ii.1., the authorization date indicated in the LOA will be 60 business days after the eNOI submission date.

² Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

- c. If *Traditional Land Use Control MS4 Operator(s)* have review authority in accordance with Part I.D.2.b.ii.2., the *owner or operator* must, within five business days of receipt of the LOA, send an electronic copy of the LOA to the *Traditional Land Use Control MS4 Operator(s)* with review authority.

E. General Requirements for Owners or Operators with Permit Coverage

1. As of the date the LOA is received, the *owner or operator* must make the eNOI, *SWPPP*, and LOA available for review and copying in accordance with the requirements in Part VII.H. When applicable, as of the date an updated LOA is received, the *owner or operator* must make the updated LOA available for review and copying in accordance with the requirements in Part VII.H.
2. The *owner or operator* must ensure compliance with all requirements of this permit and that the provisions of the *SWPPP*, including any changes made to the *SWPPP* in accordance with Part III.A.5., are properly implemented and maintained from the *commencement of construction activity* until:
 - a. all areas of disturbance have achieved *final stabilization*; and
 - b. the owner's or operator's coverage under this permit is terminated in accordance with Part V.A.5.a.
3. As of the date of the *commencement of construction activities* until Part I.E.2.a. and b. have been met, the *owner or operator* must maintain at the *construction site*, a copy of:
 - a. all documentation necessary to demonstrate eligibility with this permit; and
 - b. this permit; and
 - c. the *SWPPP*; and
 - d. the signed *SWPPP Preparer Certification Form*; and
 - e. the signed *MS4 SWPPP Acceptance Form* or signed *NYCDEP SWPPP Acceptance/Approval Form* or signed *MS4 No Jurisdiction Form* (when applicable); and
 - f. the signed *Owner/Operator Certification Form*; and

- g. the eNOI; and
 - h. the LOA; and
 - i. the LOA transmittal to the Traditional Land Use Control MS4 Operator in accordance with Part I.D.3.c. (when applicable).
4. The *owner or operator* must maintain at the *construction site*, until Part I.E.2.a. and b. have been met, as of the date the documents become final or are received, a copy of the:
- a. responsible contractor's or subcontractor's certification statement(s) in accordance with Part III.A.7.; and
 - b. inspection reports in accordance with Part IV.C.4. and 6.; and
 - c. Request to Disturb Greater Than Five Acres and the Authorization Letter to Disturb Greater Than Five Acres in accordance with Part I.E.6. (when applicable); and
 - d. Request to Continue Coverage and the Letter of Continued Coverage (LOCC) in accordance with Part I.F.2. and 4. (when applicable); and
 - e. The updated LOA(s) in accordance with Part I.E.9. (when applicable).
5. The *owner or operator* must maintain the documents in Part I.E.3. and 4. in a secure location, such as a job trailer, on-site construction office, or mailbox with lock. The secure location must be accessible during normal business hours to an individual performing a compliance inspection. The documents must be paper documents unless electronic documents are accessible to the inspector during an inspection to the same extent as a paper copy stored at the site would be. If electronic documents are kept on site, the *owner or operator* must maintain functional equipment on site available to an inspector during normal hours of operation such that an inspector may view the electronic documents in a format that can be read in a similar manner as a paper record and in a legally dependable format with no less evidentiary value than their paper equivalent.
6. The *owner or operator* must meet the following requirements prior to disturbing greater than five acres of soil at any one time:
- a. The *owner or operator* must submit a written Request to Disturb Greater Than Five Acres to:

Part I.E.6.a.i.

- i. NYSDEC's Regional Office Division of Water staff based on the project location, Appendix E, if a *Traditional Land Use Control MS4 Operator* does not have review authority in accordance with Part I.D.2.b.ii.1.; or
 - ii. the *Traditional Land Use Control MS4 Operator*, if a *Traditional Land Use Control MS4 Operator* has review authority in accordance with Part I.D.2.b.ii.1.; or
 - iii. NYSDEC's Regional Office Division of Water staff based on the project location, Appendix E, and each involved *Traditional Land Use Control MS4 Operator*, if the project spans multiple municipalities with more than one *Traditional Land Use Control MS4 Operator* involved with review authority in accordance with Part I.D.2.b.ii.1.
- b. The written Request to Disturb Greater Than Five Acres must include:
- i. The SPDES permit identification number (Permit ID); and
 - ii. Full technical justification demonstrating why alternative methods of construction that would result in five acres of soil disturbance or less at any one time are not feasible; and
 - iii. The phasing plan for the project and sequencing plans for all *phases* from the *SWPPP* in accordance with Part III.B.1.d.; and
 - iv. Plans with locations and details of erosion and sediment control practices such that the heightened concern for erosion when disturbing greater than five acres at one time has been addressed; and
 - v. Acknowledgment that "the *owner or operator* will comply with the requirements in Part IV.C.2.b."; and
 - vi. Acknowledgment that "the *owner or operator* will comply with the requirements in Part II.B.1.b."
- c. The *owner or operator* must be in receipt of an Authorization Letter to Disturb Greater Than Five Acres, which will include when the

authorization begins and ends and indicate a maximum area (acres) of soil disturbance allowed at any one time, from:

- i. NYSDEC, if Part I.E.6.a.i. or iii. apply; or
 - ii. the *Traditional Land Use Control MS4 Operator*, if Part I.E.6.a.ii. applies.
7. Upon a finding of significant non-compliance with the practices described in the *SWPPP* or violation of this permit, NYSDEC may order an immediate stop to all *construction activity* at the site until the non-compliance is remedied. The stop work order must be in writing, describe the non-compliance in detail, and be sent to the *owner or operator*.
 8. If any human remains or archaeological remains are encountered during excavation, the *owner or operator* must immediately cease, or cause to cease, all *construction activity* in the area of the remains and notify the appropriate Regional Water Engineer (RWE).³ *Construction activity* shall not resume until written permission to do so has been received from the RWE.
 9. To be authorized to implement modifications to the information previously submitted in the eNOI, the *owner or operator* must:
 - a. notify NYSDEC via email at Stormwater_info@dec.ny.gov requesting access to update the eNOI; and
 - b. update the eNOI to reflect the modifications and resubmit the eNOI in accordance with Part I.D.; and
 - c. receive an updated LOA.
 10. The eNOI, *SWPPP*, LOA, updated LOAs (when applicable), and inspection reports required by this permit are public documents that the *owner or operator* must make available for review and copying by any person within five business days of the *owner or operator* receiving a written request by any such person to review these documents. Copying of documents will be done at the requester's expense.

³ The Regional Water Manager where a DEC Region does not have a RWE.

F. Permit Coverage for *Discharges* Authorized Under GP-0-20-001

When applicable:

1. Upon the effective date of this permit, an *owner or operator* of a *construction activity*, with coverage under GP-0-20-001, will have interim coverage under GP-0-25-001 for 45 calendar days starting on the effective date of GP-0-25-001 so long as the *owner or operator* maintains compliance with all applicable requirements of this permit.
2. Within 30 calendar days of the effective date of this permit, the *owner or operator*, with coverage under GP-0-20-001, must submit a complete Request to Continue Coverage electronically using a NYSDEC approved form,⁴ which contains the information identified in Part I.F.3. below, if:
 - a. the *owner or operator* continues to implement the SMP component in conformance with the technical standards in place at the time of initial project authorization; and
 - b. the *owner or operator* will comply with all non-design requirements of GP-0-25-001.
3. The Request to Continue Coverage form contains questions to: ensure eligibility requirements in Part I.A. have been met; verify *owner or operator* contact information; verify the permit identification number; verify the original eNOI submission ID, if applicable; verify Part I.F.2.a. and b.; verify the version of the Design Manual that the technical/design components conform to; and receive an updated Owner/Operator Certification Form, Appendix I.
4. The *owner or operator* has obtained continued coverage under GP-0-25-001 as of the date indicated in the LOCC, which is sent by NYSDEC after a complete Request to Continue Coverage form is submitted.
5. If the owner or operator does not submit the Request to Continue Coverage form in accordance with Part I.F.2. and 3., coverage under this permit is automatically terminated after interim coverage expires.

⁴ Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

G. Change of *Owner or Operator*

When applicable:

1. When property ownership changes, or when there is a change in operational control over the construction plans and specifications, the following process applies:
 - a. The new *owner or operator* must meet the applicable prerequisites for submitting an eNOI in accordance with Part I.D.2.; and
 - b. The new *owner or operator* must submit an eNOI in accordance with Part I.D.3.; and
 - c. Permit coverage for the new *owner or operator* will be effective upon receipt of the LOA in accordance with Part I.D.3.b.; and
 - d. The new *owner or operator*, upon receipt of their LOA, must provide their Permit ID to the original *owner or operator*; and
 - e. If the original *owner or operator* will no longer be the *owner or operator* of the *construction activity* identified in the original *owner's or operator's* eNOI, the original *owner or operator*, upon receipt of the new *owner's or operator's* Permit ID in accordance with Part I.G.1.d., must submit to NYSDEC a completed eNOT in accordance with Part V. that includes the name and Permit ID of the new *owner or operator*; or
 - f. If the original *owner or operator* maintains ownership of a portion of the *construction activity*, the original *owner or operator* must maintain their coverage under the permit by modifying their eNOI; modifications to the eNOI must include:
 - i. the revised area of disturbance and/or *impervious area(s)*; and
 - ii. the revised SMP information, if applicable; and
 - iii. a narrative description of what has changed; and
 - iv. the new *owner's or operator's* Permit ID for the portion of the project removed from the eNOI.

Owners or operators must follow Part I.E.9. to modify the eNOI.

Part II. Water Quality-Based Effluent Limitations

A. Maintaining Water Quality

NYSDEC expects that compliance with the requirements of this permit will control *discharges* necessary to meet applicable *water quality standards*. It shall be a violation of the *ECL* for any *discharge* to either cause or contribute to a violation of the following *water quality standards* as contained in Parts 700 through 705 of Title 6 of the Official Compilation of Codes, Rules and Regulations of the State of New York:

1. There must be no increase in turbidity that will cause a substantial visible contrast to natural conditions; and
2. There must be no increase in suspended, colloidal or settleable solids that will cause deposition or impair the waters for their best usages; and
3. There must be no residue from oil and floating substances, nor visible oil film, nor globules of grease.

If there is evidence indicating that the *stormwater discharges* authorized by this permit are causing, have the reasonable potential to cause, or are contributing to a violation of the *water quality standard*, the *owner or operator* must take appropriate corrective action in accordance with Part IV.C.5. of this permit and document in accordance with Part IV.C.4. of this permit. To address the *water quality standard* violation the *owner or operator* must include and implement appropriate controls in the *SWPPP* to correct the problem or obtain an individual SPDES permit.

If, despite compliance with the requirements of this permit, it is demonstrated that the *stormwater discharges* authorized by this permit are causing or contributing to a violation of *water quality standards*, or if NYSDEC determines that a modification of this permit is necessary to prevent a violation of *water quality standards*, the authorized *discharges* will no longer be eligible for coverage under this permit, and the *owner or operator* must obtain an individual SPDES permit prior to further *discharges* from the *construction site*.

B. Effluent Limitations Applicable to *Discharges* from *Construction Activities*

Discharges authorized by this permit must achieve, at a minimum, the effluent limitations in Part II.B.1.a., b., c., d., and e. These limitations represent the

degree of effluent reduction attainable by the application of best practicable technology currently available.

1. Erosion and Sediment Control Requirements - The *owner or operator* must select, design, install, implement, and maintain control measures to *minimize* the *discharge of pollutants* and prevent a violation of the *water quality standards*. The selection, design, installation, implementation, and maintenance of these control measures must meet the non-numeric effluent limitations in Part II.B.1.a., b., c., d., and e. and be in accordance with the New York State Standards and Specifications for Erosion and Sediment Control (BB), dated November 2016, using sound engineering judgment. Where control measures are not designed in conformance with the design criteria included in the technical standard, the *owner or operator* must include in *SWPPP* the reason(s) for the deviation, or alternative design, and provide information in the *SWPPP* demonstrating that the deviation or alternative design is *equivalent* to the technical standard.

- a. **Erosion and Sediment Controls.** At a minimum, erosion and sediment controls must be selected, designed, installed, implemented, and maintained to:
 - i. *Minimize* soil erosion through application of runoff control and soil stabilization control measure to *minimize pollutant discharges*; and
 - ii. Control *stormwater discharges*, including both peak flow rates and total *stormwater* volume, to *minimize* channel and *streambank* erosion and scour in the immediate vicinity of the *discharge* points; and
 - iii. *Minimize* the amount of soil exposed during *construction activity*; and
 - iv. *Minimize* the disturbance of *steep slope*; and
 - v. *Minimize* sediment *discharges* from the site; and
 - vi. Provide and maintain *natural buffers* around surface waters, direct *stormwater* to vegetated areas and maximize *stormwater* infiltration to reduce *pollutant discharges*, unless *infeasible*; and
 - vii. *Minimize* soil compaction. *Minimizing* soil compaction is not required

where the intended function of a specific area of the site dictates that it be compacted; and

- viii. Unless *infeasible*, preserve a sufficient amount of topsoil to complete soil restoration and establish a uniform, dense vegetative cover; and
 - ix. *Minimize* dust. On areas of exposed soil, *minimize* dust through the appropriate application of water or other dust suppression techniques to control the generation of *pollutants* that could be discharged from the site.
- b. **Soil Stabilization.** In areas where soil disturbance activity has ceased, whether permanently or *temporarily ceased*, the application of soil stabilization measures must be initiated by the end of the next business day and completed within 14 calendar days from the date the current soil disturbance activity ceased. For *construction sites* that *directly discharge* to one of the 303(d) segments listed in Appendix D, or are located in one of the watersheds listed in Appendix C, or are authorized to disturb greater than five acres in accordance with Part I.E.5.a.viii., the application of soil stabilization measures must be initiated by the end of the next business day and completed within seven calendar days from the date the soil disturbance activity ceased.
- c. **Dewatering.** *Discharges* from *dewatering* activities, including *discharges* from *dewatering* of trenches and excavations, must be managed by appropriate control measures.
- d. **Pollution Prevention Measures.** Select, design, install, implement, and maintain effective pollution prevention measures to *minimize* the *discharge of pollutants* and prevent a violation of the *water quality standards*. At a minimum, such measures must be selected, designed, installed, implemented, and maintained to:
- i. *Minimize* the *discharge of pollutants* from equipment and vehicle washing, wheel wash water, and other wash waters. Soaps, detergents and solvents cannot be used; and
 - ii. *Minimize* the exposure of building materials, building products, construction wastes, trash, landscape materials, fertilizers, pesticides, herbicides, detergents, sanitary waste, hazardous and toxic waste, and other materials present on the site to precipitation

and to *stormwater*. *Minimization* of exposure is not required in cases where the exposure to precipitation and to *stormwater* will not result in a *discharge* of *pollutants*, or where exposure of a specific material or product poses little risk of *stormwater* contamination (such as final products and materials intended for outdoor use); and

- iii. Prevent the *discharge* of *pollutants* from spills and leaks and implement chemical spill and leak prevention and response procedures.

- e. **Surface Outlets.** When discharging from basins and impoundments, the surface outlets must be designed, constructed, and maintained in such a manner that sediment does not leave the basin or impoundment and that erosion at or below the outlet does not occur.

C. Post-Construction Stormwater Management Practice (SMP) Requirements

1. The *owner or operator* of a *construction activity* that requires post-construction SMPs, in accordance with Part III.C., must select, design, install, implement, and maintain the SMPs to meet the *performance criteria* in the New York State Stormwater Management Design Manual, dated July 31, 2024 (DM), using sound engineering judgment. Where SMPs are not designed in conformance with the *performance criteria* in the DM, the *owner or operator* must include in the *SWPPP* the reason(s) for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the technical standard.
2. The *owner or operator* of a *construction activity*, that requires SMPs in accordance with Part III.C., must design the practices to meet the applicable *sizing criteria* in Part II.C.2.a., b., c., or d.

a. Sizing Criteria for New Development

- i. Runoff Reduction Volume (RRv) and Water Quality Volume (WQv):
 1. Reduce the total WQv by application of RR techniques and standard SMPs with RRv capacity. The total WQv must be calculated in accordance with the criteria in Section 4.2 of the DM; or

2. Minimum RRV and Treatment of Remaining Total WQv: *Construction activities* that cannot meet the requirements in Part II.C.2.a.i.1. due to *site limitations* must direct runoff from all newly constructed *impervious areas* to a RR technique or standard SMP with RRV capacity unless *infeasible*. The specific *site limitations* that prevent the reduction of 100% of the WQv must be documented in the *SWPPP*. For each *impervious area* that is not directed to a RR technique or standard SMP with RRV capacity, the *SWPPP* must include documentation which demonstrates that all options were considered and for each option explains why it is considered *infeasible*.

In no case shall the runoff reduction achieved from the newly constructed *impervious areas* be less than the Minimum RRV as calculated using the criteria in Section 4.4 of the DM. The remaining portion of the total WQv that cannot be reduced must be treated by application of standard SMPs.

- ii. Channel Protection Volume (CPv): Provide 24 hour extended detention of the post-developed 1-year, 24-hour storm event, remaining after runoff reduction. Where a CPv control orifice is provided, the minimum orifice size must be 3 inches, with acceptable external trash rack or orifice protection. The CPv requirement does not apply when:
 1. Reduction of the entire CPv is achieved by application of runoff reduction techniques or infiltration systems; or
 2. The 1-year post-development peak *discharge* is less than or equal to 2.0 cfs without detention or velocity controls; or
 3. The site *directly discharges* into a fifth order or larger water body (stream, river, or lake), or tidal waters, where the increase in smaller flows will not impact the stream bank or channel integrity. However, the point of *discharge* must be adequately protected against scour and erosion by the increased peak *discharge*.

- iii. **Overbank Flood Control Criteria (Qp):** Requires storage to attenuate the post-development 10-year, 24-hour peak *discharge* rate (Qp) to predevelopment rates. The Qp requirement does not apply when:
 - 1. the site *directly discharges* to tidal waters or fifth order or larger streams, or
 - 2. A downstream analysis reveals that *overbank* control is not required.
- iv. **Extreme Flood Control Criteria (Qf):** Requires storage to attenuate the post-development 100-year, 24-hour peak *discharge* rate (Qf) to predevelopment rates. The Qf requirement does not apply when:
 - 1. the site *directly discharges* to tidal waters or fifth order or larger streams, or
 - 2. A downstream analysis reveals that *overbank* control is not required.

b. Sizing Criteria for New Development in Enhanced Phosphorus Removal Watersheds

- i. Runoff Reduction Volume (RRv) and Water Quality Volume (WQv):
 - 1. Reduce the WQv by application of RR techniques and standard SMPs with RRv capacity. The total WQv is the runoff volume from the 1-year, 24-hour design storm over the post-developed watershed and must be calculated in accordance with the criteria in Section 4.3 of the DM; or
 - 2. Minimum RRv and Treatment of Remaining Total WQv: *Construction activities* that cannot meet the criteria in Part II.C.2.b.i.1. due to *site limitations* must direct runoff from all newly constructed *impervious areas* to a RR technique or standard SMP with RRv capacity unless *infeasible*. The specific *site limitations* that prevent the reduction of 100% of the WQv must be documented in the *SWPPP*. For each *impervious area* that is not directed to a RR technique or standard SMP with RRv capacity, the *SWPPP* must include

documentation which demonstrates that all options were considered and for each option explains why it is considered *infeasible*.

In no case shall the runoff reduction achieved from the newly constructed *impervious areas* be less than the Minimum RRv as calculated using the criteria in Section 4.5 of the DM. The remaining portion of the total WQv that cannot be reduced must be treated by application of standard SMPs.

- ii. Channel Protection Volume (CPv): Provide 24 hour extended detention of the post-developed 1-year, 24-hour storm event, remaining after runoff reduction. Where a CPv control orifice is provided, the minimum orifice size must be 3 inches, with acceptable external trash rack or orifice protection. The CPv requirement does not apply when:
 - 1. Reduction of the entire CPv is achieved by application of runoff reduction techniques or infiltration systems; or
 - 2. The 1-year post-development peak *discharge* is less than or equal to 2.0 cfs; or
 - 3. The site *directly discharges* to tidal waters, or a fifth order or larger water body (stream, river, or lake) where the increase in smaller flows will not impact the stream bank or channel integrity. However, the point of *discharge* must be adequately protected against scour and erosion by the increased peak *discharge*.
- iii. *Overbank* Flood Control Criteria (Qp): Requires storage to attenuate the post-development 10-year, 24-hour peak *discharge* rate (Qp) to predevelopment rates. The Qp requirement does not apply when:
 - 1. the site *directly discharges* to tidal waters or fifth order or larger streams; or
 - 2. A downstream analysis reveals that *overbank* control is not required.

- iv. Extreme Flood Control Criteria (Qf): Requires storage to attenuate the post-development 100-year, 24-hour peak *discharge* rate (Qf) to predevelopment rates. The Qf requirement does not apply when:
 - 1. the site *directly discharges* to tidal waters or fifth order or larger streams; or
 - 2. A downstream analysis reveals that *overbank* control is not required.

c. Sizing Criteria for Redevelopment Activity

- i. Water Quality Volume (WQv): The WQv treatment objective for *redevelopment activity* must be addressed by one of the following options, as outlined in Section 9.2.1. *Redevelopment activities* located in an Enhanced Phosphorus Removal Watershed (see Part III.B.3. and Appendix C) must calculate the WQv in accordance with Section 4.3 of the DM. All other *redevelopment activities* must calculate the WQv in accordance with Section 4.2 of the DM.
 - 1. Reduce the existing *impervious cover* by a minimum of 25% of the total disturbed, *impervious area*. The Soil Restoration criteria in Section 5.1.6 of the DM must be applied to all newly created pervious areas; or
 - 2. Capture and treat 100% of the required WQv, for a minimum of 25% of the disturbed redevelopment *impervious area*, by implementation of standard SMPs or reduced by application of runoff reduction techniques; or
 - 3. Capture and treat 100% of the required WQv, for a minimum of 75% of the disturbed redevelopment *impervious area*, by implementation of a volume-based alternative SMP, as defined in Section 9.4 of the DM; or
 - 4. Capture and treat 100% of the required WQv, for a minimum of 75% of the disturbed redevelopment *impervious area*, by implementation of a flow-through alternative SMP sized to treat the peak rate of runoff from the WQv design storm; or

5. Application of a combination of 1 through 4 above that provide a weighted average of at least two of the above methods. Application of this method must be in accordance with the criteria in Section 9.2.1(A)(V) of the DM; or
 6. If there is an existing SMP located on the site that captures and treats runoff from the *impervious area* that is being disturbed, the WQv treatment option selected must, at a minimum, provide treatment equal to the treatment that was being provided by the existing practice(s) if that treatment is greater than the treatment required by options 1 through 5 above.
- ii. Channel Protection Volume (CPv) is not required if there is 0% change to hydrology that increases the *discharge* rate and volume from the project site.
 - iii. *Overbank* Flood Control (Qp) is not required if there is 0% change to hydrology that increases the *discharge* rate from the project site.
 - iv. Extreme Flood Control (Qf) is not required if there is 0% change to hydrology that increases the *discharge* rate from the project site.

d. *Sizing Criteria for Combination of Redevelopment Activity and New Development*

Construction projects, that include both *new development* and *redevelopment activity*, must use SMPs that meet the *sizing criteria* calculated as an aggregate of the *sizing criteria* in Part II.C.2.a. or b. for the *new development* portion of the project and Part II.C.2.c. for the *redevelopment activity* portion of the project.

Part III. Stormwater Pollution Prevention Plan (SWPPP)

A. General SWPPP Requirements

1. A SWPPP must be prepared and implemented by the *owner or operator* of all *construction activity* covered by this permit. All authorized *discharges* must be identified in the SWPPP. The SWPPP must document the selection, design, installation, implementation and maintenance of the control measures and

- practices that will be used to meet the effluent limitations in Part II.B. and, where applicable, the SMP requirements in Part II.C.
2. The *SWPPP* must demonstrate consideration in narrative format of the future physical risks due to climate change pursuant to the Community Risk and Resiliency Act (CRRA), 6 NYCRR Part 490, and associated guidance.
 - a. The owner or operator must consider:
 - i. the following physical risks due to climate change:
 - (i) increasing temperature; and
 - (ii) increasing precipitation; and
 - (iii) increasing variability in precipitation, including chance of drought; and
 - (iv) increasing frequency and severity of flooding; and
 - (v) rising sea level; and
 - (vi) increasing storm surge; and
 - (vii) shifting ecology.
 - ii. for each of the following:
 - (i) overall site planning; and
 - (ii) location, elevation, and sizing of:
 - a. control measures and practices; and
 - b. conveyance system(s); and
 - c. detention system(s).
 3. The *SWPPP* must describe the erosion and sediment control practices and where required, SMPs that will be used and/or constructed to reduce the *pollutants* in *stormwater discharges* and to assure compliance with the

requirements of this permit. In addition, the *SWPPP* must identify potential sources of pollution which may reasonably be expected to affect the quality of *stormwater discharges*.

4. All *SWPPPs*, that require the SMP component in accordance with Part III.B.2., must be prepared by a *qualified professional*.
5. The *owner or operator* must keep the *SWPPP* current so that, at all times, it accurately documents the erosion and sediment control practices that are being used or will be used during construction, and all SMPs that will be constructed on the site. At a minimum, the *owner or operator* must modify the *SWPPP*, including construction drawings:
 - a. whenever the current provisions prove to be ineffective in *minimizing pollutants* in *stormwater discharges* from the site; and
 - b. whenever there is a change in design, construction, or operation at the *construction site* that has or could have an effect on the *discharge of pollutants*; and
 - c. to address issues or deficiencies identified during an inspection by the *qualified inspector*, NYSDEC, or other regulatory authority; and
 - d. to document the final construction conditions in an as-built drawing.
6. NYSDEC may notify the *owner or operator* at any time that the *SWPPP* does not meet one or more of the minimum requirements of this permit. The notification must be in writing and identify the provisions of the *SWPPP* that require modification. Within fourteen (14) calendar days of such notification, or as otherwise indicated by NYSDEC, the *owner or operator* must make the required changes to the *SWPPP* and submit written notification to NYSDEC that the changes have been made. If the *owner or operator* does not respond to NYSDEC's comments in the specified time frame, NYSDEC may suspend the *owner's or operator's* coverage under this permit or require the *owner or operator* to obtain coverage under an individual SPDES permit in accordance with Part II.D.4.
7. Prior to the *commencement of construction activity*, the *owner or operator* must identify the contractor(s) and subcontractor(s) that will be responsible for installing, constructing, repairing, replacing, inspecting, and maintaining the erosion and sediment control practices included in the *SWPPP* and the

contractor(s) and subcontractor(s) that will be responsible for constructing the SMPs included in the *SWPPP*. The *owner or operator* must have each of the contractors and subcontractors identify at least one person from their company to be *trained contractor* that will be responsible for implementation of the *SWPPP*. The *owner or operator* must ensure that at least one *trained contractor* is on site daily when soil disturbance activities are being performed.

The *owner or operator* must have each of the contractors and subcontractors identified above sign a copy of the following certification statement below before the *commencement of construction activities*:

"I hereby certify under penalty of law that I understand and agree to comply with the requirements of the *SWPPP* and agree to implement any corrective actions identified by the *qualified inspector* during a site inspection. I also understand that the *owner or operator* must comply with the requirements of the most current version of the New York State Pollutant Discharge Elimination System (SPDES) Construction General Permit (CGP) for Stormwater Discharges from Construction Activities and that it is unlawful for any person to cause or contribute to a violation of *water quality standards*. Furthermore, I am aware that there are significant penalties for submitting false information, that I do not believe to be true, including the possibility of fine and imprisonment for knowing violations"

In addition to providing the certification statement above, the certification page must also identify the specific elements of the *SWPPP* that each contractor and subcontractor will be responsible for and include the name and title of the person providing the signature; the name and title of the *trained contractor* responsible for *SWPPP* implementation; the name, address and telephone number of the contracting firm; the address (or other identifying description) of the site; and the date the certification statement is signed. The *owner or operator* must attach the certification statement(s) to the copy of the *SWPPP* that is maintained at the *construction site*. If new or additional contractors are hired to implement measures identified in the *SWPPP* after the *commencement of construction activities*, they must also sign the certification statement and provide the information listed above prior to performing *construction activities*.

B. Required *SWPPP* Contents

1. Erosion and sediment control component - The *owner or operator* must prepare a *SWPPP* that includes erosion and sediment control practices.
 - a. Erosion and sediment control practices must be designed:
 - i. in conformance with the BB; or
 - ii. *equivalent* to the BB if deviating from Part III.B.1.a.i.
 - b. If the erosion and sediment control practices are designed in conformance with Part III.B.1.a.ii., the *SWPPP* must include a demonstration of *equivalence* to the BB.
 - c. At a minimum, the erosion and sediment control component of the *SWPPP* must include the following:
 - i. Background information about the scope of the project, including the location, type and size of project; and
 - ii. A site map/construction drawing(s) with north arrows for the project, including a general location map. At a minimum, the site map must show the total site area; all improvements; areas of disturbance; areas that will not be disturbed; existing vegetation; on-site and adjacent off-site surface water(s); floodplain/floodway boundaries; wetlands and drainage patterns that could be affected by the *construction activity*; existing and final contours; locations of different soil types with boundaries; material, waste, borrow or equipment storage areas located on adjacent properties; and location(s) of the *stormwater discharge(s)* and receiving surface water(s); and
 - iii. A description of the soil(s) present at the site, including an identification of the Hydrologic Soil Group (HSG); and
 - iv. A phasing plan for the project and sequencing plans for all *phases*, both of which must address clearing and grubbing, excavation and grading, utility and infrastructure installation, *final stabilization*,

and any other *construction activity* at the site that will result in soil disturbance.

1. The phasing plan must include:
 - a. a map delineating and labeling the limits of soil disturbance for all *phases* of a project; and
 - b. a table identifying the order and intended schedule of when each *phase* will begin and end its sequencing plan. The table must identify the total disturbed area for each *phase* at any one time and the total disturbed area for the overall project at any one time all on one timeline showing all overlapping quantities of disturbed area at any one time; and
2. A sequencing plan for a specific *phase* must include:
 - a. a table indicating the order and intended schedule of *construction activities* within a *phase*, and corresponding construction drawings with a description of the work to be performed; and
 - b. all permanent and *temporary stabilization* measures; and
- v. A description of the minimum erosion and sediment control practices to be installed or implemented for each *construction activity* that will result in soil disturbance. Include a schedule that identifies the timing of initial placement or implementation of each erosion and sediment control practice and the minimum time frames that each practice should remain in place or be implemented; and
- vi. A site map/construction drawing(s) showing the specific location(s), size(s), and length(s) of each erosion and sediment control practice; and
- vii. The dimensions, material specifications, installation details, and operation and maintenance requirements for all erosion and sediment control practices. Include the location and sizing of any

temporary sediment basins and structural practices that will be used to divert flows from exposed soils; and

- viii. A maintenance inspection schedule for the contractor(s) and subcontractor(s) identified in Part III.A.7. to ensure continuous and effective operation of the erosion and sediment control practices. The maintenance inspection schedule must be in accordance with the requirements in the BB technical standard; and
 - ix. A description of the pollution prevention measures that will be used to control litter, construction chemicals and construction debris from becoming a *pollutant* source in the *stormwater discharges*; and
 - x. A description and location of any *stormwater discharges* associated with industrial activity other than construction at the site, including, but not limited to, *stormwater discharges* from asphalt plants and concrete plants located on the *construction site*; and
 - xi. Identification of any elements of the design that are not in conformance with the design criteria in the BB technical standard. Include the reason for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the technical standard.
2. SMP component – The *owner or operator of construction activity* identified in Table 2 of Appendix B must prepare a *SWPPP* that includes SMPs.
- a. SMPs must be designed in conformance with the applicable *sizing criteria* in Part II.C.2.a., c., or d.; and
 - b. SMPs must be designed in conformance with the *performance criteria*:
 - i. in the DM; or
 - ii. *equivalent* to the DM if deviating from Part III.B.2.b.i.; or
 - iii. in the New York State Stormwater Management Design Manual, dated January 2015 (2015 Design Manual), or *equivalent* to it, if the following criteria are met:

1. The eNOI is submitted in accordance with Part I.D. before January 29, 2027 for *construction activities* that are either:
 - a. subject to governmental review and approval:
 - i. where the *owner or operator* made any application to that governmental entity prior to the effective date of this permit; and
 - ii. such application included a *SWPPP* developed using the 2015 Design Manual or *equivalent* to it; or
 - b. not subject to governmental review and approval:
 - i. where a fiscal allocation for the *construction activities* has been developed and approved by a governmental entity; and
 - ii. the *SWPPP* was developed using the 2015 Design Manual or *equivalent* to it; and
 - c. If SMPs are designed in conformance with Part III.B.2.b.ii., the *SWPPP* must include the reason(s) for the deviation or alternative design and a demonstration of *equivalence* to the DM; and
 - d. If SMPs are designed in conformance with Part III.B.2.b.iii., the *SWPPP* must include supporting information or documentation demonstrating that Part III.B.2.b.iii.1.a. or b. apply; and
 - e. The SMP component of the *SWPPP* must include the following:
 - i. Identification of all SMPs to be constructed as part of the project, including which option the SMP designs conform to, either Part III.B.2.b.i., ii., or iii. Include the dimensions, material specifications and installation details for each SMP; and
 - ii. A site map/construction drawing(s) showing the specific location and size of each SMP; and

- iii. A Stormwater Modeling and Analysis Report that includes:
 - (i) Map(s) showing pre-development conditions, including watershed/subcatchments boundaries, flow paths/routing, and design points; and
 - (ii) Map(s) showing post-development conditions, including watershed/subcatchments boundaries, flow paths/routing, design points and SMPs; and
 - (iii) Results of *stormwater* modeling (i.e. hydrology and hydraulic analysis) for the required storm events. Include supporting calculations (model runs), methodology, and a summary table that compares pre- and post-development runoff rates and volumes for the different storm events; and
 - (iv) Summary table, with supporting calculations, which demonstrates that each SMP has been designed in conformance with the *sizing criteria* included in the DM; and
 - (v) Identification of any *sizing criteria* that is not required based on the requirements included in Part II.C.; and
 - (vi) Identification of any elements of the design that are not in conformance with the *performance criteria* in the DM. Include the reason(s) for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the DM.
- iv. Soil testing results and locations (test pits, borings); and
- v. Infiltration test results, when required in accordance with Part III.B.2.a.; and
- vi. An operations and maintenance plan that includes inspection and maintenance schedules and actions to ensure continuous and effective operation of each SMP. The plan must identify the entity

that will be responsible for the long-term operation and maintenance of each practice; and

3. Enhanced Phosphorus Removal Standards - The *owner or operator* of *construction activity* identified in Table 2 of Appendix B that is located in a watershed identified in Appendix C must prepare a *SWPPP* that includes SMPs designed in conformance with the applicable *sizing criteria* in Part II.C.2.b., c., or d. and the *performance criteria* Enhanced Phosphorus Removal Standards included in the DM. At a minimum, the SMP component of the *SWPPP* must meet the requirements of Part III.B.2.

C. Required *SWPPP* Components by Project Type

Owners or operators of *construction activities*, identified in Table 1 of Appendix B, are required to prepare a *SWPPP* that only includes erosion and sediment control practices designed in accordance with Part III.B.1. *Owners or operators* of the *construction activities*, identified in Table 2 of Appendix B, must prepare a *SWPPP* that also includes SMPs designed in accordance with Part III.B.2 or 3.

For the entire area of disturbance, including the entire *common plan of development or sale* if applicable, the owner or operator must evaluate every bullet from Appendix B Table 1 and Table 2 separately. If bullets from both Table 1 and Table 2 apply, the *SWPPP* must include erosion and sediment control practices for all *construction activities* but SMPs for only those portions of the *construction activities* that fall under Table 2 bullet(s).

Part IV. Inspection and Maintenance Requirements

A. General Construction Site Inspection and Maintenance Requirements

1. The *owner or operator* must ensure that all erosion and sediment control practices (including pollution prevention measures), and all SMPs identified in the *SWPPP*, are inspected and maintained in accordance with Part IV.B. and C.

B. Contractor Maintenance Inspection Requirements

1. The *owner or operator* of each *construction activity*, identified in Tables 1 and 2 of Appendix B, must have a *trained contractor* inspect the erosion and sediment control practices and pollution prevention measures being

implemented within the active work area daily to ensure that they are being maintained in effective operating condition at all times. If deficiencies are identified, the contractor must:

- a. if the corrective action does not require engineering design:
 - i. begin implementing corrective actions within one business day; and
 - ii. complete the corrective actions within five business days; or
 - b. if the corrective action requires engineering design:
 - i. begin the engineering design process within five business days; and
 - ii. complete the corrective action in a reasonable time frame but no later than within 60 calendar days.
2. For *construction sites* where soil disturbance activities have been temporarily suspended (e.g. winter shutdown) and *temporary stabilization* measures have been applied to all disturbed areas, the *trained contractor* can stop conducting the maintenance inspections in accordance with Part IV.B.1. The *trained contractor* must begin conducting the maintenance inspections in accordance with Part IV.B.1. as soon as soil disturbance activities resume.
 3. For *construction sites* where soil disturbance activities have been shut down with partial project completion, the *trained contractor* can stop conducting the maintenance inspections in accordance with Part IV.B.1. if all areas disturbed as of the project shutdown date have achieved *final stabilization* and all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational.

C. Qualified Inspector Inspection Requirements

1. With the exception of the following *construction activities* identified in Tables 1 and 2 of Appendix B, a *qualified inspector* must conduct site inspections for all other *construction activities* identified in Tables 1 and 2 of Appendix B:
 - a. the construction of a single-family residential subdivision with 25% or less *impervious cover* at total site build-out that involves a soil disturbance of one (1) or more acres of land but less than or equal to five (5) acres and is

not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D; and

- b. the construction of a single-family home that involves soil disturbances of one (1) or more acres but less than or equal to five (5) acres and is not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D; and
 - c. construction on *agricultural property* that involves soil disturbances of one (1) or more acres but less than five (5) acres; and
 - d. *construction activities* located in the New York City Watershed located east of the Hudson River, see Appendix C Figure 1, that involve soil disturbances of 5,000 square feet or more, but less than one acre.
2. The *qualified inspector* must conduct site inspections in accordance with the following timetable:
- a. For *construction sites* where soil disturbance activities are on-going, the *qualified inspector* must conduct a site inspection at least once every seven (7) calendar days; or
 - b. For *construction sites* where soil disturbance activities are on-going and the *owner or operator* has received authorization in accordance with Part I.E.6. to disturb greater than five (5) acres of soil at any one time, the *qualified inspector* must conduct at least two (2) site inspections every seven (7) calendar days. The two (2) inspections must be separated by a minimum of two (2) full calendar days; or
 - c. For *construction sites* where soil disturbance activities have been temporarily suspended (e.g. winter shutdown) and *temporary stabilization* measures have been applied to all disturbed areas, the *qualified inspector* must conduct a site inspection at least once every thirty (30) calendar days. The *owner or operator* must notify the DOW Water (SPDES) Program contact at the Regional Office (see contact information in Appendix E) or, in areas under the jurisdiction of a *Traditional Land Use Control MS4 Operator*, the *Traditional Land Use Control MS4 Operator* (provided the *Traditional Land Use Control MS4 Operator* is not the *owner or operator* of the *construction activity*) by hard copy or email prior to reducing the inspections to this frequency and again by hard copy or email prior to re-commencing construction; or

- d. For *construction sites* where soil disturbance activities have been shut down with partial project completion, the requirement to have the *qualified inspector* conduct inspections ceases if all areas disturbed as of the project shutdown date have achieved *final stabilization* and all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational. The *owner or operator* must notify the DOW Water (SPDES) Program contact at the Regional Office (see contact information in Appendix E) or, in areas subject to the review authority of *Traditional Land Use Control MS4 Operator(s)* in accordance with Part I.D.2.b.ii.1., the *Traditional Land Use Control MS4 Operator(s)* (provided the *Traditional Land Use Control MS4 Operator(s)* are not the *owners or operators* of the *construction activity*) in writing prior to the shutdown and again in writing prior to resuming *construction activity*. If soil disturbance activities are not resumed within 2 years from the date of shutdown, the *owner or operator* must terminate coverage by meeting the requirements of Part V; or
 - e. For *construction sites* involving soil disturbance of one (1) or more acres that *directly discharge* to one of the 303(d) segments listed in Appendix D or is located in one of the watersheds listed in Appendix C, the *qualified inspector* must conduct at least two (2) site inspections every seven (7) calendar days. The two (2) inspections must be separated by a minimum of two (2) full calendar days.
3. At a minimum, the *qualified inspector* must inspect:
- a. all erosion and sediment control practices and pollution prevention measures to ensure integrity and effectiveness; and
 - b. all SMPs under construction to ensure that they are constructed in conformance with the *SWPPP*; and
 - c. all areas of disturbance that have not achieved *final stabilization*; and
 - d. all points of *discharge to surface waters of the State* located within, or immediately adjacent to, the property boundaries of the *construction site*; and
 - e. all points of *discharge* from the *construction site*.

4. The *qualified inspector* must prepare an inspection report subsequent to each and every inspection. At a minimum, the inspection report must include and/or address all of the following, for all *construction activities* except those listed in Part IV.C.1.:
 - a. Permit identification number; and
 - b. Date and time of inspection; and
 - c. Name and title of person(s) performing inspection; and
 - d. A description of the weather and soil conditions (e.g. dry, wet, saturated) at the time of the inspection, including the temperature at the time of the inspection; and
 - e. A description of the condition of the runoff at all points of *discharge* from the *construction site*. This must include identification of any *discharges* of sediment from the *construction site*. Include *discharges* from conveyance systems (i.e. pipes, culverts, ditches, etc.) and overland flow; and
 - f. A description of the condition of all *surface waters of the State* located within, or immediately adjacent to, the property boundaries of the *construction site* which receive runoff from disturbed areas. This must include identification of any *discharges* of sediment to the *surface waters of the State*; and
 - g. Identification of all erosion and sediment control practices and pollution prevention measures that need repair or maintenance; and
 - h. Identification of all erosion and sediment control practices and pollution prevention measures that were not installed properly or are not functioning as designed and need to be reinstalled or replaced; and
 - i. Description and sketch (map) of areas with active soil disturbance activity, areas that have been disturbed but are inactive at the time of the inspection, and areas that have been stabilized (temporary and/or final) since the last inspection; and
 - j. Estimates, in square feet or acres, of the following areas:

- i. Total area with active soil disturbance (not requiring either *temporary stabilization* or *final stabilization*); and
 - ii. Total area with inactive soil disturbance (requiring either *temporary stabilization* or *final stabilization*); and
 - iii. Total area that has achieved *temporary stabilization*; and
 - iv. Total area that has achieved *final stabilization*; and
- k. Current stage of construction of all SMPs and identification of all *construction activity* on site that is not in conformance with the *SWPPP* and technical standards; and
- l. Corrective action(s) that must be taken to install, repair, replace or maintain erosion and sediment control practices and pollution prevention measures; and to correct deficiencies identified with the construction of the SMP(s); and
- m. Identification and status of all corrective actions that were required by previous inspection; and
- n. Digital photographs, with date stamp, that clearly show the condition of all practices that have been identified as needing corrective actions. The *qualified inspector* must attach color copies of the digital photographs to the inspection report being maintained onsite within seven (7) calendar days of the date of the inspection. The *qualified inspector* must also take digital photographs, with date stamp, that clearly show the condition of the practice(s) after the corrective action has been completed. The *qualified inspector* must attach paper color copies of the digital photographs to the inspection report that documents the completion of the corrective action work within seven (7) calendar days of that inspection.
5. Within one business day of the completion of an inspection, the *qualified inspector* must notify the *owner or operator*, and appropriate contractor or subcontractor identified in Part III.A.7., of any corrective actions that need to be taken. The contractor or subcontractor must:
- a. if the corrective action does not require engineering design:

- i. begin implementing corrective actions within one business day; and
 - ii. complete the corrective actions within five business days; or
 - b. if the corrective action requires engineering design:
 - i. begin the engineering design process within five business days; and
 - ii. complete the corrective action in a reasonable time frame but no later than within 60 calendar days.
6. All inspection reports must be signed by the *qualified inspector*. In accordance with Part I.E.3., the inspection reports must be maintained on site with the *SWPPP*.

Part V. How to Terminate CGP Coverage

A. Electronic Notice of Termination (eNOT) Submittal

The eNOT contains questions to ensure requirements in Part V.A. have been met.

1. An *owner or operator* must terminate coverage when one or more of the following requirements have been met:
 - a. Total project completion:
 - i. all *construction activity* identified in the *SWPPP* has been completed; and
 - ii. all areas of disturbance have achieved *final stabilization*; and
 - iii. all temporary, structural erosion and sediment control measures have been removed; and
 - iv. all SMPs have been constructed in conformance with the *SWPPP* and are operational; and
 - v. an as-built drawing has been prepared; or

- b. Planned shutdown with partial project completion:
 - i. all soil disturbance activities have ceased; and
 - ii. all areas disturbed as of the project shutdown date have achieved *final stabilization*; and
 - iii. all temporary, structural erosion and sediment control measures have been removed; and
 - iv. all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational; and
 - v. an as-built drawing has been prepared; or
 - c. In accordance with Part I.G. Change of Owner or Operator; or
 - d. The *owner or operator* has obtained coverage under an alternative general SPDES permit or an individual SPDES permit.
2. For *construction activities* that require *qualified inspector* inspections in accordance with Part IV.C.1. and have met Part V.A.1.a. or b., the *owner or operator* must have the *qualified inspector* perform a final site inspection prior to submitting the eNOT. The *qualified inspector* must, by signing the “Final Stabilization” and “Post-Construction Stormwater Management Practice(s)” certification statements on the eNOT, certify that all the requirements in Part V.A.1.a. or b. have been achieved.
3. For *construction activities* that are subject to the review authority of *Traditional Land Use Control MS4 Operator(s)* in accordance with Part I.D.2.b.ii.1. and meet Part V.A.1.a. or b., the *owner or operator* must have the *Traditional Land Use Control MS4 Operator(s)* sign the “MS4 Acceptance” statement on the eNOT in accordance with the requirements in Part VII.J. A *Traditional Land Use Control MS4 Operator* official, by signing this statement, determined that it is acceptable for the *owner or operator* to submit the eNOT in accordance with the requirements of this Part. A *Traditional Land Use Control MS4 Operator* can make this determination by performing a final site inspection themselves or by accepting the *qualified inspector’s* final site inspection certification(s) when required in Part V.A.2.

Part V.A.4.

4. For *construction activities* that require SMPs and meet Part V.A.1.a. or b., the *owner or operator* must, prior to submitting the eNOT, ensure one of the following:
 - a. for SMP(s) that were constructed by a private entity, but will be owned, operated, and maintained by a public entity, the SMP(s) and any right-of-way(s) needed to operate and maintain such practice(s) have been deeded to the municipality in which the practice(s) is located; or
 - b. for SMP(s) that are privately owned, but will be operated and maintained by a public entity, an executed operation and maintenance agreement is in place with the municipality that will operate and maintain the SMP(s); or
 - c. for SMP(s) that are privately owned, the *owner or operator* has a mechanism in place that requires operation and maintenance of the practice(s) in accordance with the operation and maintenance plan, such as a deed covenant in the *owner or operator's* deed of record; or
 - d. for SMP(s) that are owned by a public or private institution (e.g. school, university, hospital), government agency or authority, or public utility, the *owner or operator* has policies and procedures in place that ensure operation and maintenance of the practices in accordance with the operation and maintenance plan.
5. An *owner or operator* that has met the requirements of Part V.A.1., 2., 3., and 4. must request termination of coverage under this permit by submitting a complete Notice of Termination form electronically using a NYSDEC approved form.⁵
 - a. The owner's or operator's coverage is terminated as of the termination date indicated in the Letter of Termination (LOT), which is sent by NYSDEC after a complete eNOT is submitted.

⁵ Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

Part VI. Record Retention and Reporting

A. Record Retention

The *owner or operator* must retain a copy of the documents listed in Part I.E.3. and a copy of the LOT for a period of at least five years from the date that NYSDEC accepts a complete NOT submitted in accordance with Part V.

B. Reporting

Except for the eNOI, the signature forms associated with the eNOI, and the eNOT, all other written correspondence requested by NYSDEC, including individual permit applications, must be sent to the address of the appropriate DOW (SPDES) Program contact at the Regional Office listed in Appendix E.

Part VII. Standard Permit Requirements

For the purposes of this permit, examples of contractors and subcontractors include: third-party maintenance and construction contractors.

A. Duty to Comply

The *owner or operator*, and all contractors or subcontractors, must comply with all requirements of this permit. Any non-compliance with the requirements of this permit constitutes a violation of the New York State Environmental Conservation Law (ECL), and its implementing regulations, and is grounds for enforcement action. Filing of a request for termination of coverage under this permit, or a notification of planned changes or anticipated non-compliance, does not limit, diminish or stay compliance with any requirements of this permit.

B. Need to Halt or Reduce Activity Not a Defense

The necessity to halt or reduce the *construction activity* regulated by this permit, in order to maintain compliance with the requirements of this permit, must not be a defense in an enforcement action.

C. Penalties

There are substantial criminal, civil, and administrative penalties associated with violating the requirements of this permit. Fines of up to \$37,500 per day for each

violation and imprisonment for up to 15 years may be assessed depending upon the nature and degree of the offense.

D. False Statements

Any person who knowingly makes any false material statement, representation, or certification in any application, record, report, or other document filed or required to be maintained under this permit, including monitoring reports or reports of compliance or noncompliance must, upon conviction, be punished in accordance with ECL §71-1933 and or New York State Penal Law Articles 175 and 210.

E. Re-Opener Clause

Upon issuance of this permit, a determination has been made on the basis of a submitted Notice of Intent, plans, or other available information, that compliance with the specified permit requirements will reasonably protect classified water use and assure compliance with applicable *water quality standards*. Satisfaction of the requirements of this permit notwithstanding, if operation pursuant to this permit causes or contributes to a condition in contravention of State *water quality standards* or guidance values, or if NYSDEC determines that a modification is necessary to prevent impairment of the best use of the waters or to assure maintenance of *water quality standards* or compliance with other provisions of ECL Article 17 or the Clean Water Act (CWA), or any regulations adopted pursuant thereto, NYSDEC may require such modification and the Commissioner may require abatement action to be taken by the *owner or operator* and may also prohibit such operation until the modification has been implemented.

F. Duty to Mitigate

The *owner or operator*, and its contractors and subcontractors, must take all reasonable steps to *minimize* or prevent any *discharge* in violation of this permit which has a reasonable likelihood of adversely affecting human health or the environment.

G. Requiring Another General Permit or Individual SPDES Permit

NYSDEC may require any *owner or operator* authorized to *discharge* in accordance with this permit to apply for and obtain an individual SPDES permit or apply for authorization to *discharge* in accordance with another general SPDES permit.

1. Cases where an individual SPDES permit or authorization to discharge in accordance with another general SPDES permit may be required include, but is not limited to the following:

Part VII.G.1.a.

- a. the *owner or operator* is not in compliance with the conditions of this permit or does not meet the requirements for coverage under this permit; and
 - b. a change has occurred in the availability of demonstrated technology or practices for the control or abatement of *pollutants* applicable to the *point source*; and
 - c. new effluent limitation guidelines or new source performance standards are promulgated that are applicable to *point sources* authorized to *discharge* in accordance with this permit; and
 - d. existing effluent limitation guidelines or new source performance standards that are applicable to *point sources* authorized to *discharge* in accordance with this permit are modified; and
 - e. a water quality management plan containing requirements applicable to such *point sources* is approved by NYSDEC; and
 - f. circumstances have changed since the time of the request to be covered so that the *owner or operator* is no longer appropriately controlled under this permit, or either a temporary or permanent reduction or elimination of the authorized *discharge* is necessary; and
 - g. the *discharge* is in violation of section 17-0501 of the ECL; and
 - h. the *discharge(s)* is a significant contributor of *pollutants*. In making this determination, NYSDEC may consider the following factors:
 - i. the location of the *discharge(s)* with respect to *surface waters of the State*; and
 - ii. the size of the *discharge(s)*; and
 - iii. the quantity and nature of the *pollutants discharged* to *surface waters of the State*; and
 - iv. other relevant factors including compliance with other provisions of ECL Article 17, or the CWA.
2. When NYSDEC requires any *owner or operator* authorized by this permit to apply for an individual SPDES permit as provided for in this subdivision, it must notify the *owner or operator* in writing that a permit application is required. This notice must include a brief statement of the reasons for this decision, an application

form, a statement setting a time for the *owner or operator* to file the application for an individual SPDES permit, and a deadline, not sooner than 180 days from the *owner's or operator's* receipt of the notification letter, whereby the authorization to *discharge* under this permit must be terminated. NYSDEC may grant additional time upon demonstration, to the satisfaction of the RWE,⁶ that additional time to apply for an alternative authorization is necessary or where NYSDEC has not provided a permit determination in accordance with 6 NYCRR Part 621.

3. When an individual SPDES permit is issued to an *owner or operator* authorized to *discharge* under this permit for the same *discharge(s)*, this permit authorization for *construction activities* authorized under the individual SPDES permit is automatically terminated on the effective date of the individual SPDES permit unless termination is earlier in accordance with 6 NYCRR Part 750.

H. Duty to Provide Information

The *owner or operator* must furnish to NYSDEC, within five business days, unless otherwise set forth by NYSDEC, any information that NYSDEC may request to determine whether cause exists to determine compliance with this permit or to determine whether cause exists for requiring an individual SPDES permit in accordance with 6 NYCRR 750-1.21(e) (see Part VII.G. Requiring Another General Permit or Individual Permit).

The *owner or operator* must make available to NYSDEC, for inspection and copying, or furnish to NYSDEC within 25 business days of receipt of a NYSDEC request for such information, any information retained in accordance with this permit.

Except for Part I.D.4. and 5. and Part I.G., the following applies: where the *owner or operator* becomes aware that it failed to submit any relevant facts on the Notice of Intent, or submitted incorrect information in a Notice of Intent or in any report to NYSDEC, the *owner or operator* must submit such facts or corrected information to NYSDEC within five business days.

I. Extension

In the event a new permit is not issued and effective prior to the expiration of this permit, and this permit is extended pursuant to the State Administrative Procedure Act and 6 NYCRR Part 621, then the *owner or operator* with coverage under this permit may continue to operate and *discharge* in accordance with the requirements of this permit until a new permit is issued and effective.

⁶ The Regional Water Manager where a DEC Region does not have a RWE.

J. Signatories and Certification

The Notice of Intent, Notice of Termination, and reports required by this permit must be signed as provided in 40 CFR §122.22.

1. All Notices of Intent and Notices of Termination must be signed as follows:

a. For a corporation. By a responsible corporate officer. For the purpose of this section, a responsible corporate officer means:

- (i) a president, secretary, treasurer, or vice-president of the corporation in charge of a principal business function, or any other person who performs similar policy- or decision-making functions for the corporation; or
- (ii) the manager of one or more manufacturing, production or operating facilities, provided, the manager is authorized to make management decisions which govern the operation of the regulated facility including having the explicit or implicit duty of making major capital investment recommendations, and initiating and directing other comprehensive measures to assure long term environmental compliance with environmental laws and regulations; the manager can ensure that the necessary systems are established or actions taken to gather complete and accurate information for Notice of Intent or Notice of Termination requirements; and where authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures.

Note: NYSDEC does not require specific assignments or delegations of authority to responsible corporate officers identified in 40 CFR §122.22(a)(1)(i). NYSDEC will presume that these responsible corporate officers have the requisite authority to sign the Notice of Intent or Notice of Termination unless the corporation has notified NYSDEC to the contrary. Corporate procedures governing authority to sign a Notice of Intent or Notice of Termination may provide for assignment or delegation to applicable corporate positions under 40 CFR §122.22(a)(1)(ii) rather than to specific individuals.

b. For a partnership or sole proprietorship. By a general partner or the proprietor, respectively.

Part VII.J.1.c.

- c. For a municipality, State, Federal, or other public agency. By either a principal executive officer or ranking elected official. For purposes of this section, a principal executive officer of a Federal agency includes:
 - 1. the chief executive officer of the agency; or
 - 2. a senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency (e.g., Regional Administrators of EPA).
- 2. All reports required by this permit, and other information requested by NYSDEC, must be signed by a person described in Part VII.J.1., or by a duly authorized representative of that person. A person is a duly authorized representative only if:
 - a. The authorization is made in writing by a person described in Part VII.J.1. or using the Duly Authorized Form, found on the DEC website; and
 - b. The authorization specifies either an individual or a position having responsibility for the overall operation of the regulated facility or activity, position of equivalent responsibility, or an individual or position having overall responsibility for environmental matters for the company. (A duly authorized representative may thus be either a named individual or any individual occupying a named position); and
 - c. The written authorization is submitted to NYSDEC.
- 3. Changes to authorization. If an authorization under Part VII.J.2. is no longer accurate because a different individual or position has responsibility for the overall operation of the *construction activity*, a new authorization satisfying the requirements of Part VII.J.2. must be submitted to NYSDEC prior to or together with any reports, information, or applications to be signed by an authorized representative.
- 4. Certification. Any person signing a document under Part VII.J.1. or 2. must make the following certification:

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who

manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

5. Electronic reporting. If documents described in Part VII.J.1. or 2. are submitted electronically by or on behalf of the *construction activity* with coverage under this permit, any person providing the electronic signature for such documents must meet all relevant requirements of this section, and must ensure that all of the relevant requirements of 40 CFR Part 3 (including, in all cases, subpart D to Part 3) (Cross-Media Electronic Reporting) and 40 CFR Part 127 (NPDES Electronic Reporting Requirements) are met for that submission.

K. Inspection and Entry

The *owner or operator* must allow NYSDEC, the USEPA Regional Administrator, the applicable county health department, or any authorized representatives of those entities, or, in the case of a *construction site* which *discharges* through an *MS4*, an authorized representative of the *MS4* receiving the *discharge*, upon the presentation of credentials and other documents as may be required by law, to:

1. enter upon the *owner's or operator's* premises where a regulated facility or activity is located or conducted or where records must be kept under the requirements of this permit; and
2. have access to and copy at reasonable times, any records that must be kept under the requirements of this permit, including records required to be maintained for purposes of operation and maintenance; and
3. inspect at reasonable times any facilities, equipment (including monitoring and control equipment), practices or operations regulated or required under this permit; and
4. sample or monitor at reasonable times, for the purposes of assuring general SPDES permit compliance or as otherwise authorized by the CWA or ECL, any substances or parameters at any location; and
5. enter upon the property of any contributor to the regulated facility or activity under authority of the *owner or operator*.

L. Confidentiality of Information

The following must not be held confidential: this permit, the fact sheet for this permit, the name and address of any *owner or operator*, effluent data, the Notice of Intent, and information regarding the need to obtain an individual permit or an alternative general SPDES permit. This includes information submitted on forms themselves and any attachments used to supply information required by the forms (except information submitted on usage of substances). Upon the request of the *owner or operator*, NYSDEC must make determinations of confidentiality in accordance with 6 NYCRR Part 616, except as set forth in the previous sentence. Any information accorded confidential status must be disclosed to the Regional Administrator upon his or her written request. Prior to disclosing such information to the Regional Administrator, NYSDEC will notify the Regional Administrator of the confidential status of such information.

M. Other Permits May Be Required

Nothing in this permit relieves the *owner or operator* from a requirement to obtain any other permits required by law.

N. NYSDEC Orders or Civil Decrees/Judgments

The issuance of this permit by the NYSDEC, and the coverage under this permit by the *owner or operator*, does not supersede, revoke, or rescind any existing order on consent or civil Decree/Judgment, or modification to any such documents or to any order issued by the Commissioner, or any of the terms, conditions, or requirements contained in such order or modification therefore, unless expressly noted.

O. Property Rights

Coverage under this permit does not convey any property rights in either real or personal property, or any exclusive privileges, nor does it authorize any injury to private property or any invasion of personal rights, nor any infringement of Federal, State, or local laws or regulations, nor does it obviate the necessity of obtaining the assent of any other jurisdiction as required by law for the *discharge* authorized.

P. Compliance with Interstate Standards

If the *construction activity* covered by this permit originates within the jurisdiction of an interstate water pollution control agency, then the *construction activity* must also comply with any applicable effluent standards or *water quality standards* promulgated by that interstate agency and as set forth in this permit for such *construction activities*.

Q. Oil and Hazardous Substance Liability

Coverage under this permit does not affect the imposition of responsibilities upon, or the institution of any legal action against, the *owner or operator* under section 311 of the CWA, which must be in conformance with regulations promulgated pursuant to section 311 governing the applicability of section 311 of the CWA to *discharges* from facilities with *NPDES* permits, nor must such issuance preclude the institution of any legal action or relieve the *owner or operator* from any responsibilities, liabilities, or penalties to which the *owner or operator* is or may be subject pursuant to the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. section 9601 et seq. (CERCLA).

R. Severability

The provisions of this permit are severable, and if any provision of this permit, or the application of any provision of this permit to any circumstance, is held invalid, the application of such provision to other circumstances, and the remainder of this permit, must not be affected thereby.

S. NYSDEC Approved Forms

The *owner or operator* must provide all relevant information that is requested by NYSDEC, and required by this permit, on all NYSDEC approved forms.

APPENDIX A – Abbreviations and Definitions

Abbreviations

APO – Agency Preservation Officer
BB – New York State Standards and Specifications for Erosion and Sediment Control (Blue Book), dated November 2016
BMP – Best Management Practice
CPESC – Certified Professional in Erosion and Sediment Control
CPv – Channel Protection Volume
CWA – Clean Water Act (or the Federal Water Pollution Control Act, 33 U.S.C. §1251 et seq)
DM – New York State Stormwater Management Design Manual (Design Manual), dated July 31, 2024
DOW – Division of Water
EAF – Environmental Assessment Form
ECL – chapter 43-B of the Consolidated Laws of the State of New York, entitled the Environmental Conservation Law
EPA – U.S. Environmental Protection Agency
HSG – Hydrologic Soil Group
MS4 – Municipal Separate Storm Sewer System
NOI – Notice of Intent
NOT – Notice of Termination
NPDES – National Pollutant Discharge Elimination System
NYC – The City of New York
NYCDEP – The City of New York Department of Environmental Protection
NYSDEC – The New York State Department of Environmental Conservation
OPRHP – Office of Parks, Recreation and Historic Places
Qf – Extreme Flood
Qp – Overbank Flood
RR – Runoff Reduction
RRv – Runoff Reduction Volume
RWE – Regional Water Engineer
SEQR – State Environmental Quality Review Act
SHPA – State Historic Preservation Act
SMP – Post-Construction Stormwater Management Practice
SPDES – State Pollutant Discharge Elimination System
SWPPP – Stormwater Pollution Prevention Plan
TMDL – Total Maximum Daily Load
UPA – Uniform Procedures Act
USDA – United States Department of Agriculture
WQv – Water Quality Volume

Definitions

All definitions in this section are solely for the purposes of this permit. If a word is not italicized in the permit, use its common definition.

Agricultural Building – a structure designed and constructed to house farm implements, hay, grain, poultry, livestock or other horticultural products; excluding any structure designed, constructed or used, in whole or in part, for human habitation, as a place of employment where agricultural products are processed, treated or packaged, or as a place used by the public.

Agricultural Property – the land for construction of a barn, *agricultural building*, silo, stockyard, pen or other structural practices identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023).

Alter Hydrology from Pre- to Post-Development Conditions – the post-development peak flow rate(s) has increased by more than 5% of the pre-developed condition for the design storm of interest (e.g. 10 yr and 100 yr).

Combined Sewer System – a sewer system which conveys sewage and *stormwater* through a single pipe system to a publicly owned treatment works.

Commence (Commencement of) Construction Activities – the initial disturbance of soils associated with clearing, grading or excavation activities; or other construction related activities that disturb or expose soils such as demolition, stockpiling of fill material, and the initial installation of erosion and sediment control practices required in the *SWPPP*. See definition for “*Construction Activity(ies)*” also.

Common Plan of Development or Sale – a contiguous area where multiple separate and distinct *construction activities* are occurring, or may occur, under one plan. The “common plan” of development or sale is broadly defined as any announcement or piece of documentation (including a sign, public notice or hearing, marketing plan, advertisement, drawing, permit application, State Environmental Quality Review Act (SEQR) environmental assessment form or other documents, zoning request, computer design, etc.) or physical demarcation (including boundary signs, lot stakes, surveyor markings, etc.) indicating *construction activities* may occur on a specific plot. A *common plan of development or sale* is comprised of two or more *phases*.

Common plan of development or sale does not include separate and distinct *construction activities* that are occurring, or may occur, under one plan that are at least 1/4 mile apart provided any interconnecting road, pipeline or utility project that is part of the same “common plan” is not concurrently being disturbed.

Construction Activity(ies) – identified within 40 CFR 122.26(b)(14)(x), 122.26(b)(15)(i), and 122.26(b)(15)(ii), any clearing, grading, excavation, filling, demolition or stockpiling activities that result in soil disturbance. Clearing activities can include, but are not limited to, mechanized logging equipment operation, the cutting and skidding of trees, stump removal and/or brush root removal.

Construction activity does not include routine maintenance that is performed to maintain the original line and grade, hydraulic capacity, or original purpose of a facility, which is excluded from the calculation of the soil disturbance for a project. Routine maintenance includes, but is not limited to:

- Re-grading of gravel roads or parking lots; and
- Cleaning and shaping of existing roadside ditches and culverts that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity of the ditch; and
- Replacement of existing culverts that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity of a ditch; and
- Replacement of existing bridges that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity beneath the bridges; and
- Cleaning and shaping of existing roadside ditches that does not maintain the approximate original grade, hydraulic capacity and purpose of the ditch if the changes to the line and grade, hydraulic capacity or purpose of the ditch are installed to improve water quality and quantity controls (e.g. installing grass lined ditch); and
- Placement of aggregate shoulder backing that stabilizes the transition between the road shoulder and the ditch or *embankment*; and
- Full depth milling and filling of existing asphalt pavements, replacement of concrete pavement slabs, and similar work that does not expose soil or disturb the bottom six (6) inches of subbase material; and
- Long-term use of equipment storage areas at or near highway maintenance facilities; and
- Removal of sediment from the edge of the highway to restore a previously existing sheet-flow drainage connection from the highway surface to the highway ditch or *embankment*; and
- Existing use of Canal Corp owned upland disposal sites for the canal, and
- Replacement of curbs, gutters, sidewalks and guide rail posts; and
- Maintenance of ski trails including brush hog use and mowing; and
- Above ground snowmaking pipe replacement; and
- Replacement of existing utility poles; etc.

Construction Site – the land area where *construction activity(ies)* will occur. See also the definitions for “*Commence (Commencement of) Construction Activities*” and “*Common Plan of Development or Sale.*”

Dewatering – the act of draining rainwater and/or groundwater from building foundations, vaults or excavations/trenches.

Directly Discharge(s)(ing) (to a specific surface waterbody) – runoff flows from a *construction site* by overland flow and the first point of *discharge* is the specific surface waterbody, or runoff flows from a *construction site* to a separate storm sewer system and the first point of *discharge* from the separate storm sewer system is the specific surface waterbody.

Discharge(s)(d) – any addition of any *pollutant* to waters of the State through an outlet or *point source*.

Embankment – an earthen or rock slope that supports a road/highway.

Equivalent (Equivalence) – the practice or measure meets all the performance, longevity, maintenance, and safety objectives of the technical standard and will provide an equal or greater degree of water quality protection.

Final Stabilization – all soil disturbance activities have ceased and a uniform, perennial vegetative cover with a density of eighty (80) percent over the entire pervious surface has been established; or other *equivalent* stabilization measures, such as permanent landscape mulches, rock rip-rap or washed/crushed stone have been applied on all disturbed areas that are not covered by permanent structures, concrete or pavement.

Historic Property – any building, structure, site, object or district that is listed on the State or National Registers of Historic Places or is determined to be eligible for listing on the State or National Registers of Historic Places.

Impervious Area (Cover) – all impermeable surfaces that cannot effectively infiltrate rainfall. This includes paved, concrete and compacted gravel surfaces (i.e. parking lots, driveways, roads, runways and sidewalks); building rooftops and miscellaneous impermeable structures such as patios, pools, and sheds.

Infeasible – not technologically possible, or not economically practicable and achievable considering best industry practices.

Minimize(ing)(ation) – reduce and/or eliminate to the extent achievable using control measures (including best management practices) that are technologically available and economically practicable and achievable in light of best industry practices.

Municipal Separate Storm Sewer System (MS4) - a conveyance or system of conveyances (including roads with drainage systems, municipal streets, catch basins, curbs, gutters, ditches, man-made channels, or storm drains):

1. owned or operated by a State, city, town, village, borough, county, parish, district, association, or other public body (created by or pursuant to State law) having jurisdiction over disposal of sewage, industrial wastes, *stormwater*, or other wastes, including special districts under State law such as a sewer district, flood control district or drainage district, or similar entity, or an Indian tribe or an authorized Indian tribal organization, or a designated and approved management agency under section 208 of the CWA, that *discharges to surface waters of the State*; and
2. designed or used for collecting or conveying *stormwater*; and
3. which is not a *combined sewer system*; and
4. which is not part of a Publicly Owned Treatment Works (POTW) as defined at 40 CFR 122.2.

Natural Buffer(s) – an undisturbed area with natural cover running along a surface water (e.g. wetland, stream, river, lake, etc.).

New Development – any land disturbance that does not meet the definition of *Redevelopment Activity* included in this appendix.

New York State Erosion and Sediment Control Certificate Program – a certificate program that establishes and maintains a process to identify and recognize individuals who are capable of developing, designing, inspecting and maintaining erosion and sediment control plans on projects that disturb soils in New York State. The certificate program is administered by the New York State Conservation District Employees Association.

Nonpoint Source(s) – any source of water pollution or *pollutants* which is not a discrete conveyance or *point source* permitted pursuant to Title 7 or 8 of Article 17 of the Environmental Conservation Law (see ECL Section 17-1403).

Overbank – flow events that exceed the capacity of the stream channel and spill out into the adjacent floodplain.

Owner or Operator – the person, persons, or legal entity which owns or leases the property on which the *construction activity* is occurring; an entity that has operational control over the construction plans and specifications, including the ability to make modifications to the plans and specifications; and/or an entity that has day-to-day operational control of those activities at a project that are necessary to ensure compliance with the permit requirements.

Performance Criteria – the six performance criteria for each group of SMPs in Chapters 5 and 6 of the technical standard, New York State Stormwater Management Design Manual (DM), dated July 31, 2024. These include feasibility, conveyance, pretreatment, treatment, landscaping, and maintenance. It does not include the *Sizing Criteria* (i.e. WQv, RRV, CPv, Qp and Qf) in Part I.C.2. of the permit.

Phase – a defined area in which *construction activities* are occurring or will occur separate from other defined area(s).

Point Source – any discernible, confined, and discrete conveyance, including but not limited to any pipe, ditch, channel, tunnel, conduit, well, discrete fissure, container, rolling stock, concentrated animal feeding operation, vessel or other floating craft, or landfill leachate collection system from which *pollutants* are or may be *discharged*.

Pollutant(s) – dredged spoil, filter backwash, solid waste, incinerator residue, sewage, garbage, sewage sludge, munitions, chemical wastes, biological materials, radioactive materials, heat, wrecked or discarded equipment, rock, sand and industrial, municipal, agricultural waste and ballast *discharged* into water; which may cause or might reasonably be expected to cause pollution of the waters of the state in contravention of the standards or guidance values adopted as provided in 6 NYCRR Parts 700 et seq.

Qualified Inspector – a person that is knowledgeable in the principles and practices of erosion and sediment control, such as a licensed Professional Engineer, Certified Professional in Erosion and Sediment Control (CPESC), Registered Landscape Architect, *New York State Erosion and Sediment Control Certificate Program* holder or other NYSDEC endorsed individual(s).

It can also mean someone working under the direct supervision of, and at the same company as, the licensed Professional Engineer or Registered Landscape Architect, provided that person has training in the principles and practices of erosion and sediment control. Training in the principles and practices of erosion and sediment control means that the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect has received four (4) hours of NYSDEC endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity. After receiving the initial training, the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect shall receive four (4) hours of training every three (3) years.

It can also mean a person that meets the *Qualified Professional* qualifications in addition to the *Qualified Inspector* qualifications.

Note: Inspections of any SMPs that include structural components, such as a dam for an impoundment, shall be performed by a licensed Professional Engineer.

Qualified Professional – a person that is knowledgeable in the principles and practices of *stormwater* management and treatment, such as a licensed Professional Engineer, Registered Landscape Architect or other NYSDEC endorsed individual(s). Individuals preparing *SWPPPs* that require the SMP component must have an understanding of the principles of hydrology, water quality management practice design, water quantity control design, and, in many cases, the principles of hydraulics. All components of the *SWPPP* that involve the practice of engineering, as defined by the NYS Education Law (see Article 145), shall be prepared by, or under the direct supervision of, a professional engineer licensed to practice in the State of New York.

Redevelopment Activity(ies) – the disturbance and reconstruction of existing *impervious area*, including *impervious areas* that were removed from a project site within five (5) years of preliminary project plan submission to the local government (i.e. site plan, subdivision, etc.).

Renewable Energy – electricity or thermal energy generated by renewable energy systems through use of the following technologies: solar thermal, photovoltaics, on land and offshore wind, hydroelectric, geothermal electric, geothermal ground source heat, tidal energy, wave energy, ocean thermal, and fuel cells which do not utilize a fossil fuel resource in the process of generating electricity.

Site Limitations – site conditions that prevent the use of an infiltration technique and or infiltration of the total WQv. Typical *site limitations* include: seasonal high groundwater, shallow depth to bedrock, and soils with an infiltration rate less than 0.5 inches/hour. The existence of *site limitations* shall be confirmed and documented using actual field testing (i.e. test pits, soil borings, and infiltration test) or using information from the most current United States Department of Agriculture (USDA) Soil Survey for the County where the project is located.

Sizing Criteria – the criteria included in Part I.C.2 of the permit that are used to size SMPs. The criteria include; Water Quality Volume (WQv), Runoff Reduction Volume (RRv), Channel Protection Volume (Cpv), *Overbank Flood* (Qp), and Extreme Flood (Qf).

Steep Slope – land area designated on the current United States Department of Agriculture (USDA) Soil Survey as Soil Slope Phase D, (provided the map unit name or description is inclusive of slopes greater than 25%), or Soil Slope Phase E or F, (regardless of the map unit name), or a combination of the three designations.

Stormwater – that portion of precipitation that, once having fallen to the ground, is in excess of the evaporative or infiltrative capacity of soils, or the retentive capacity of surface features, which flows or will flow off the land by surface runoff to waters of the State.

Streambank – the terrain alongside the bed of a creek or stream. The bank consists of the sides of the channel, between which the flow is confined.

Stormwater Pollution Prevention Plan (SWPPP) – a project specific report, including construction drawings, that among other things: describes the *construction activity(ies)*, identifies the potential sources of pollution at the *construction site*; describes and shows the *stormwater* controls that will be used to control the *pollutants* (i.e. erosion and sediment controls; for many projects, includes SMPs); and identifies procedures the *owner or operator* will implement to comply with the requirements of the permit. See Part III of the permit for a complete description of the information that must be included in the *SWPPP*.

Surface Waters of the State – shall be construed to include lakes, bays, sounds, ponds, impounding reservoirs, springs, rivers, streams, creeks, estuaries, marshes, inlets, canals, the Atlantic ocean within the territorial seas of the state of New York and all other bodies of surface water, natural or artificial, inland or coastal, fresh or salt, public or private (except those private waters that do not combine or effect a junction with natural surface waters), which are wholly or partially within or bordering the state or within its jurisdiction. Waters of the state are further defined in 6 NYCRR Parts 800 to 941.

Temporarily Ceased – an existing disturbed area will not be disturbed again within 14 calendar days of the previous soil disturbance.

Temporary Stabilization – exposed soil has been covered with material(s) as set forth in the technical standard, New York Standards and Specifications for Erosion and Sediment Control, to prevent the exposed soil from eroding. The materials can include, but are not limited to, mulch, seed and mulch, and erosion control mats (e.g. jute twisted yarn, excelsior wood fiber mats).

Total Maximum Daily Load (TMDL) – the sum of the allowable loads of a single *pollutant* from all contributing point and *nonpoint sources*. It is a calculation of the maximum amount of a *pollutant* that a waterbody can receive and still meet *water quality standards*, and an allocation of that amount to the *pollutant's* sources. A TMDL stipulates Waste Load Allocations (WLA) for *point source discharges*, Load Allocations (LA) for *nonpoint sources*, and a margin of safety (MOS).

Traditional Land Use Control MS4 Operator – a city, town, or village with land use control authority that is authorized to *discharge* under New York State DEC's SPDES General Permit For Stormwater Discharges from Municipal Separate Stormwater Sewer Systems (MS4s) or the City of New York's Individual SPDES Permit for their Municipal Separate Storm Sewer Systems (NY-0287890).

Trained Contractor – an employee from the contracting (construction) company, identified in Part III.A.7., that has received four (4) hours of NYSDEC endorsed training

in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity. After receiving the initial training, the *trained contractor* shall receive four (4) hours of training every three (3) years.

It can also mean an employee from the contracting (construction) company, identified in Part III.A.7., that meets the *qualified inspector* qualifications (e.g. licensed Professional Engineer, Certified Professional in Erosion and Sediment Control (CPESC), Registered Landscape Architect, *New York State Erosion and Sediment Control Certificate Program* holder, or someone working under the direct supervision of, and at the same company as, the licensed Professional Engineer or Registered Landscape Architect, provided they have received four (4) hours of NYSDEC endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity).

The *trained contractor* is responsible for the day-to-day implementation of the *SWPPP*.

Tree Clearing – *construction activities* limited to felling and removal of trees.

Tree clearing does not include hand felling and leaving the trees in place with no support from mechanized equipment, which is not considered *construction activity* requiring coverage under this permit.

Water Quality Standard – such measures of purity or quality for any waters in relation to their reasonable and necessary use as promulgated in 6 NYCRR Part 700 et seq.

APPENDIX B – Required SWPPP Components by Project Type

Table 1
CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A SWPPP
THAT ONLY INCLUDES EROSION AND SEDIMENT CONTROLS

The following *construction activities* that involve soil disturbances of one (1) or more acres of land, but less than five (5) acres:

- Single-family home not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D
- Single-family residential subdivisions with 25% or less *impervious cover* at total site build-out and not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D
- Construction of a barn or other *agricultural building*, silo, stock yard or pen.
- Structural agricultural conservation practices as identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023) that include construction or reconstruction of *impervious area* or *alter hydrology from pre- to post-development* conditions.

The following *construction activities* that involve soil disturbances between five thousand (5000) square feet and one (1) acre of land:

- All construction activities located in the New York City Watershed located east of the Hudson River, see Appendix C Figure 1, that involve soil disturbances between five thousand (5,000) square feet and one (1) acre of land.

Within the municipal boundaries of NYC:

- Stand-alone road reconstruction, where the total soil disturbance from only that road construction, is less than one (1) acre of land.

The following *construction activities*:

- Installation of underground linear utilities; such as gas lines, fiber-optic cable, cable TV, electric, telephone, sewer mains, and water mains
- Environmental enhancement projects, such as wetland mitigation, *stormwater* retrofits, stream restoration, and resiliency projects that reconstruct shoreline areas to address sea level rise
- Pond construction
- Linear bike paths running through areas with vegetative cover, including bike paths surfaced with an *impervious cover*
- Cross-country ski trails, walking/hiking trails, and mountain biking trails, including a de minimis parking lot (maximum 10 spaces total, sized for passenger cars) with 35 feet minimum preservation of undisturbed area downgradient from the parking lot
- Dam rehabilitation (the structure of the dam itself)
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are not part of residential, commercial, or institutional development;
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that include incidental shoulder or curb work along an existing highway to support construction of the sidewalk, bike path, or walking path.

Table 1 (Continued)
CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A SWPPP
THAT ONLY INCLUDES EROSION AND SEDIMENT CONTROLS

The following *construction activities*:

- Slope stabilization
- Slope flattening that changes the grade of the site, but does not significantly change the runoff characteristics
- Spoil areas that will be covered with vegetation
- Vegetated open space (i.e. recreational parks, lawns, meadows, fields, downhill ski trails) that do not *alter hydrology from pre- to post-development* conditions
- Athletic fields (natural grass) that do not include the construction or reconstruction of *impervious area* and do not *alter hydrology from pre- to post-development* conditions
- Demolition where vegetation will be established, and no *redevelopment activity* is planned¹
- Installation or replacement of either an overhead electric transmission line or a ski lift tower that does not include the construction of permanent access roads or parking areas surfaced with *impervious cover*.
- Solar array field areas that have tables elevated off the ground, spaced one table width apart, do not *alter hydrology from pre- to post-development conditions*, and address water quality volume and runoff reduction volume by maintaining sheet flow on slopes less than 8%.
- Structural agricultural conservation practices as identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023) that do not include construction or reconstruction of *impervious area* and do not *alter hydrology from pre- to post-development* conditions.
- Temporary access roads, median crossovers, detour roads, lanes, or other temporary *impervious areas* that will be restored to pre-construction conditions once the *construction activity* is complete (in this context, “temporary” means the *impervious area* will be in place for two years or less)
- Other *construction activities* that do not include the construction or reconstruction of *impervious area*, and do not *alter hydrology from pre- to post-development* conditions, and are not listed in Table 2.

1. If the site is redeveloped in the future, a new eNOI must be submitted.

Table 2

CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A *SWPPP* THAT INCLUDES POST-CONSTRUCTION STORMWATER MANAGEMENT PRACTICES (SMPs)

The following *construction activities*:

- Single-family home located in one of the watersheds listed in Appendix C or *directly discharging* to one of the 303(d) segments listed in Appendix D
- Single-family home that disturbs five (5) or more acres of land
- Single-family residential subdivisions located in one of the watersheds listed in Appendix C or *directly discharging* to one of the 303(d) segments listed in Appendix D
- Single-family residential subdivisions that involve soil disturbances of between one (1) and five (5) acres of land with greater than 25% *impervious cover* at total site build-out
- Single-family residential subdivisions that involve soil disturbances of between 20,000 square feet and one (1) acre of land within the municipal boundaries of NYC with greater than 25% *impervious cover* at total site build-out
- Single-family residential subdivisions that involve soil disturbances of five (5) or more acres of land, and single-family residential subdivisions that involve soil disturbances of less than five (5) acres that are part of a *common plan of development or sale* that will ultimately disturb five (5) or more acres of land
- Multi-family residential developments; includes duplexes, townhomes, condominiums, senior housing complexes, apartment complexes, and mobile home parks
- Creation of 5,000 square feet or more of *impervious area* in the municipal boundaries of NYC
- Airports
- Amusement parks
- Breweries, cideries, and wineries, including establishments constructed on agricultural land
- Campgrounds
- Cemeteries that include the construction or reconstruction of *impervious area* (>5% of disturbed area) or *alter the hydrology from pre- to post-development* conditions
- Commercial developments
- Churches and other places of worship
- Construction of a barn or other *agricultural building* (e.g. silo) that involves soil disturbance greater than five acres.
- Structural agricultural conservation practices as identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023) that involves soil disturbance greater than five acres and include the construction or reconstruction of *impervious area* or *alter hydrology from pre- to post-development* conditions.
- Facility buildings, including ski lodges, restroom buildings, pumphouses, ski lift terminals, and maintenance and groomer garages
- Institutional development; includes hospitals, prisons, schools and colleges
- Industrial facilities; includes industrial parks
- Landfills; including creation of landfills or capping landfills.
- Municipal facilities; includes highway garages, transfer stations, office buildings, POTWs, water treatment plants, and water storage tanks
- Golf courses
- Office complexes

Table 2 (Continued)

CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A *SWPPP* THAT INCLUDES POST-CONSTRUCTION STORMWATER MANAGEMENT PRACTICES (SMPs)

The following *construction activities*:

- Permanent laydown yards and equipment storage lots
- Playgrounds that include the construction or reconstruction of *impervious area*
- Sports complexes
- Racetracks; includes racetracks with earthen (dirt) surfaces
- Road construction or reconstruction, outside the municipal boundaries of NYC
- Road construction within the municipal boundaries of NYC
- Stand-alone road reconstruction, within the municipal boundaries of NYC where the total soil disturbance from that road reconstruction involves soil disturbance of one (1) acre or more of land
- Parking lot construction or reconstruction (as with all Table 2 bullets, this includes parking lots constructed as part of the *construction activities* listed in Table 1, unless a Table 1 bullet specifies otherwise)
- Athletic fields (natural grass) that include the construction or reconstruction of *impervious area* (>5% of disturbed area) or *alter the hydrology from pre- to post-development* conditions
- Athletic fields with artificial turf
- Permanent access roads, parking areas, substations, compressor stations, and well drilling pads, surfaced with *impervious cover*, and constructed as part of an overhead electric transmission line, wind-power, cell tower, oil or gas well drilling, sewer or water main, ski lift, or other linear utility project
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are part of a residential, commercial or institutional development
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are part of highway construction or reconstruction
- Solar array field areas on slopes greater than 8% that cannot maintain sheet flow using management practices identified in the BB or the DM
- Solar array field areas on slopes less than 8% that will *alter the hydrology from pre- to post-development* conditions
- Solar array field areas with tables that are not elevated high enough to achieve *final stabilization* beneath the tables
- Traditional *impervious areas* associated with solar development (e.g. roads, buildings, transformers)
- Utility pads surfaced with *impervious cover*, including electric vehicle charging stations
- All other *construction activities* that include the construction or reconstruction of *impervious area* or *alter the hydrology from pre- to post-development* conditions, and are not listed in Table 1

APPENDIX C – Watersheds Requiring Enhanced Phosphorus Removal

Watersheds where *owners or operators of construction activities* identified in Table 2 of Appendix B must prepare a *SWPPP* that includes SMPs designed in conformance with the Enhanced Phosphorus Removal Standards included in the DM technical standard.

- Entire New York City Watershed located east of the Hudson River – Figure 1
- Onondaga Lake Watershed – Figure 2
- Greenwood Lake Watershed – Figure 3
- Oscawana Lake Watershed – Figure 4
- Kinderhook Lake Watershed – Figure 5

Figure 1 - New York City Watershed East of the Hudson

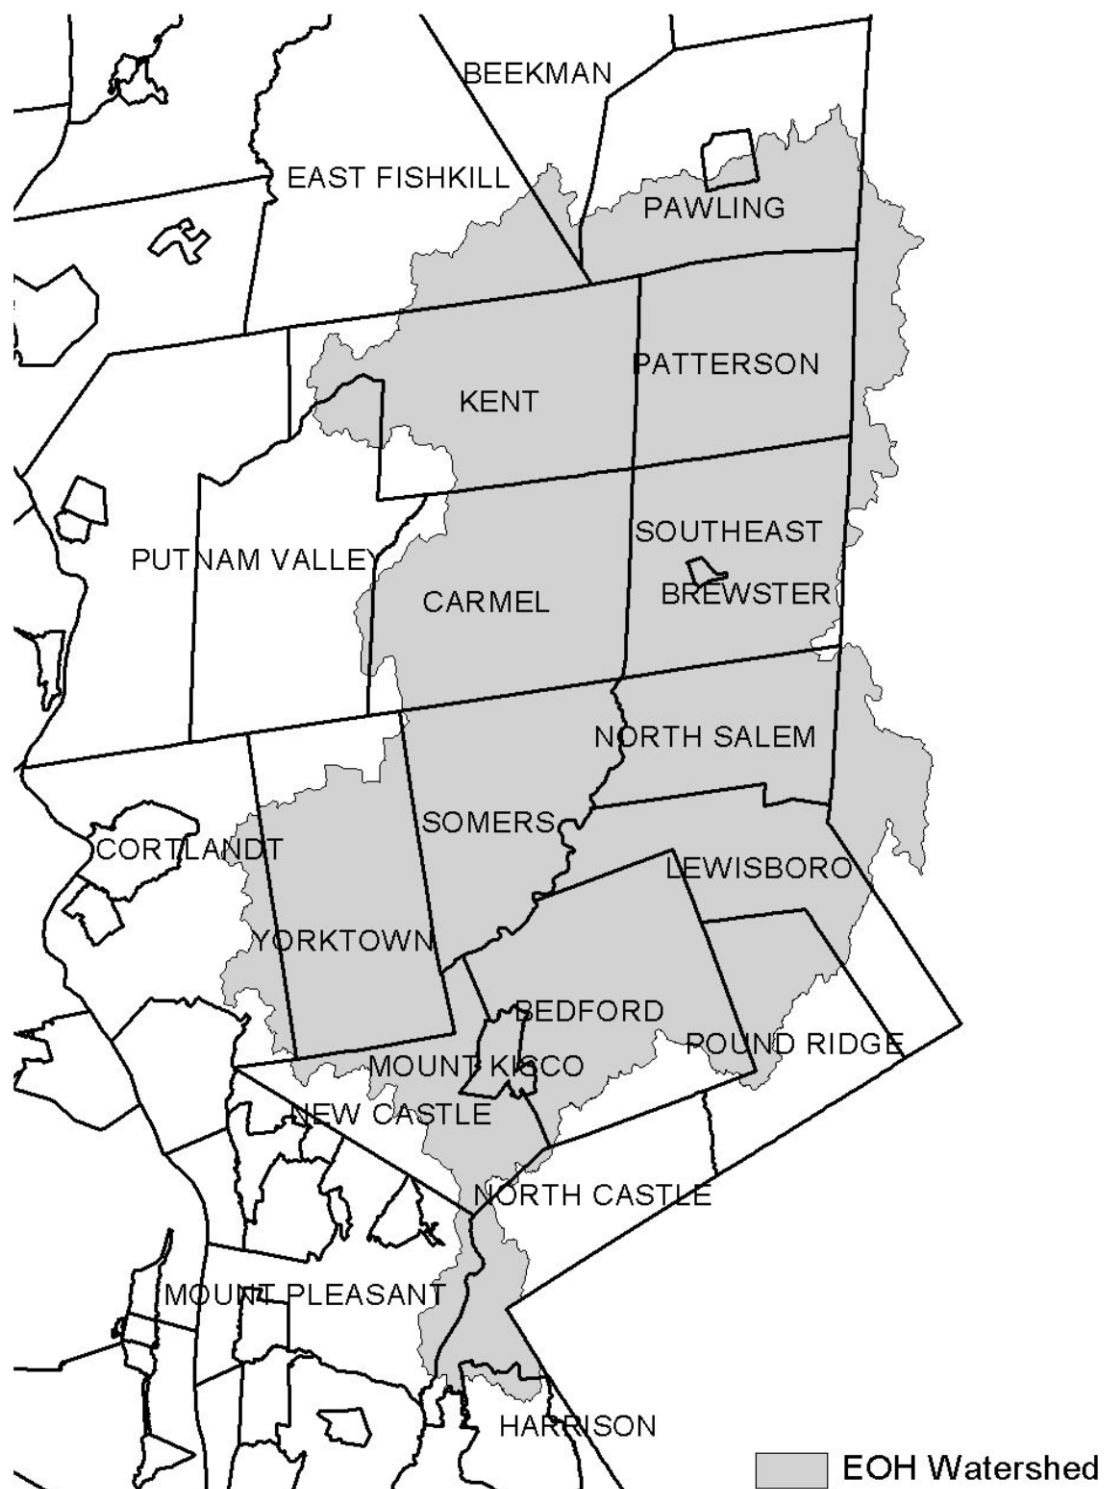


Figure 2 - Onondaga Lake Watershed



Figure 3 - Greenwood Lake Watershed



Figure 4 - Oscawana Lake Watershed


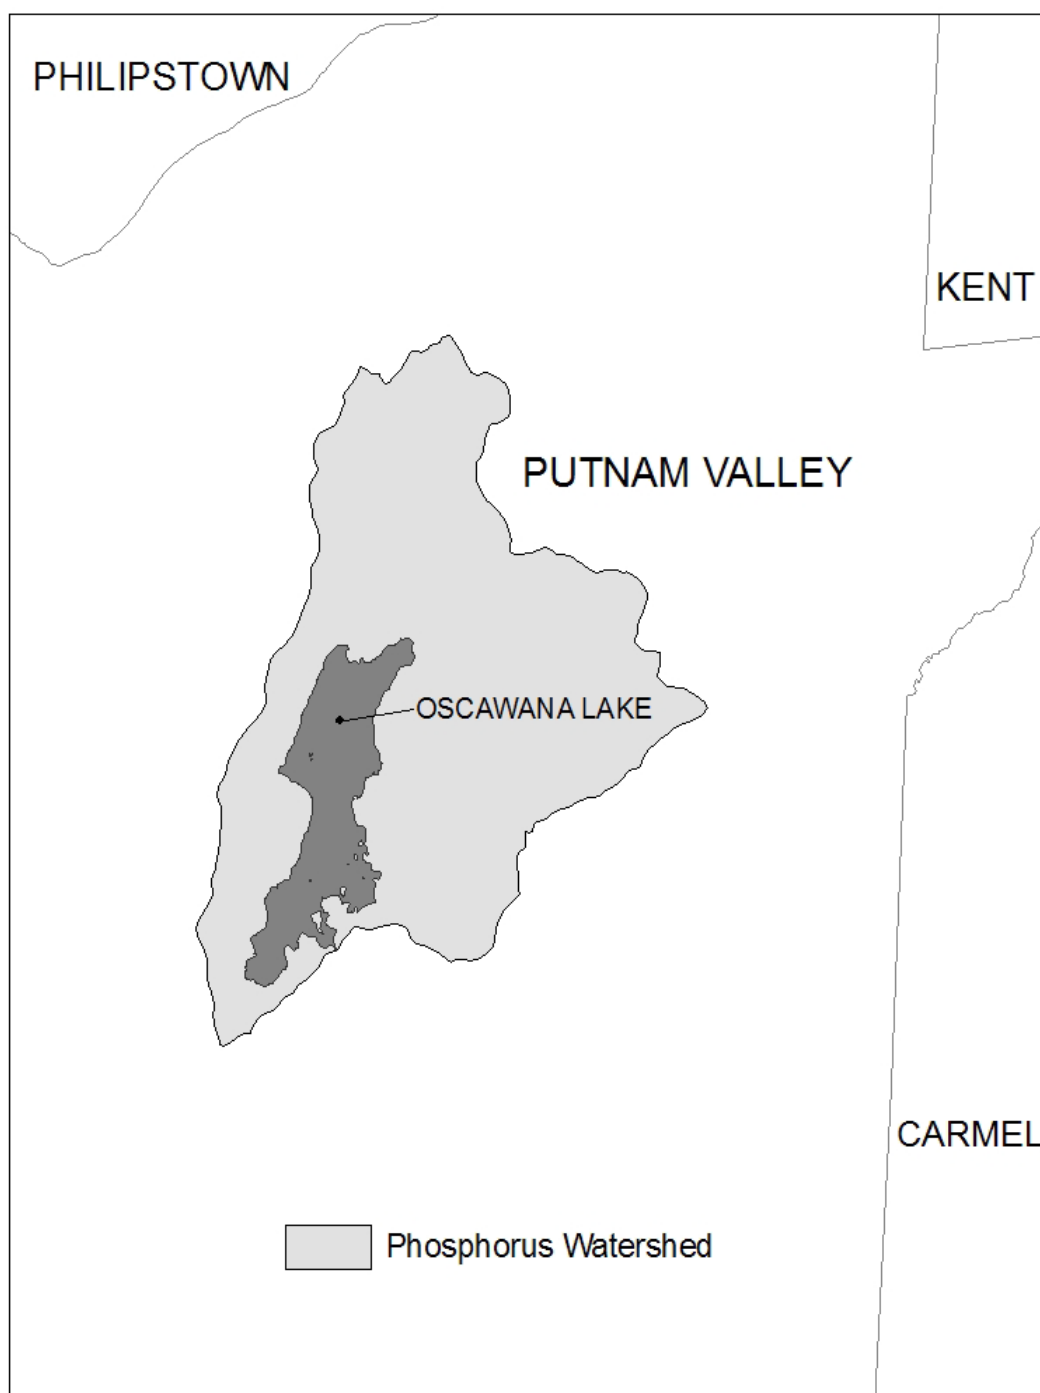


Figure 5 - Kinderhook Lake Watershed

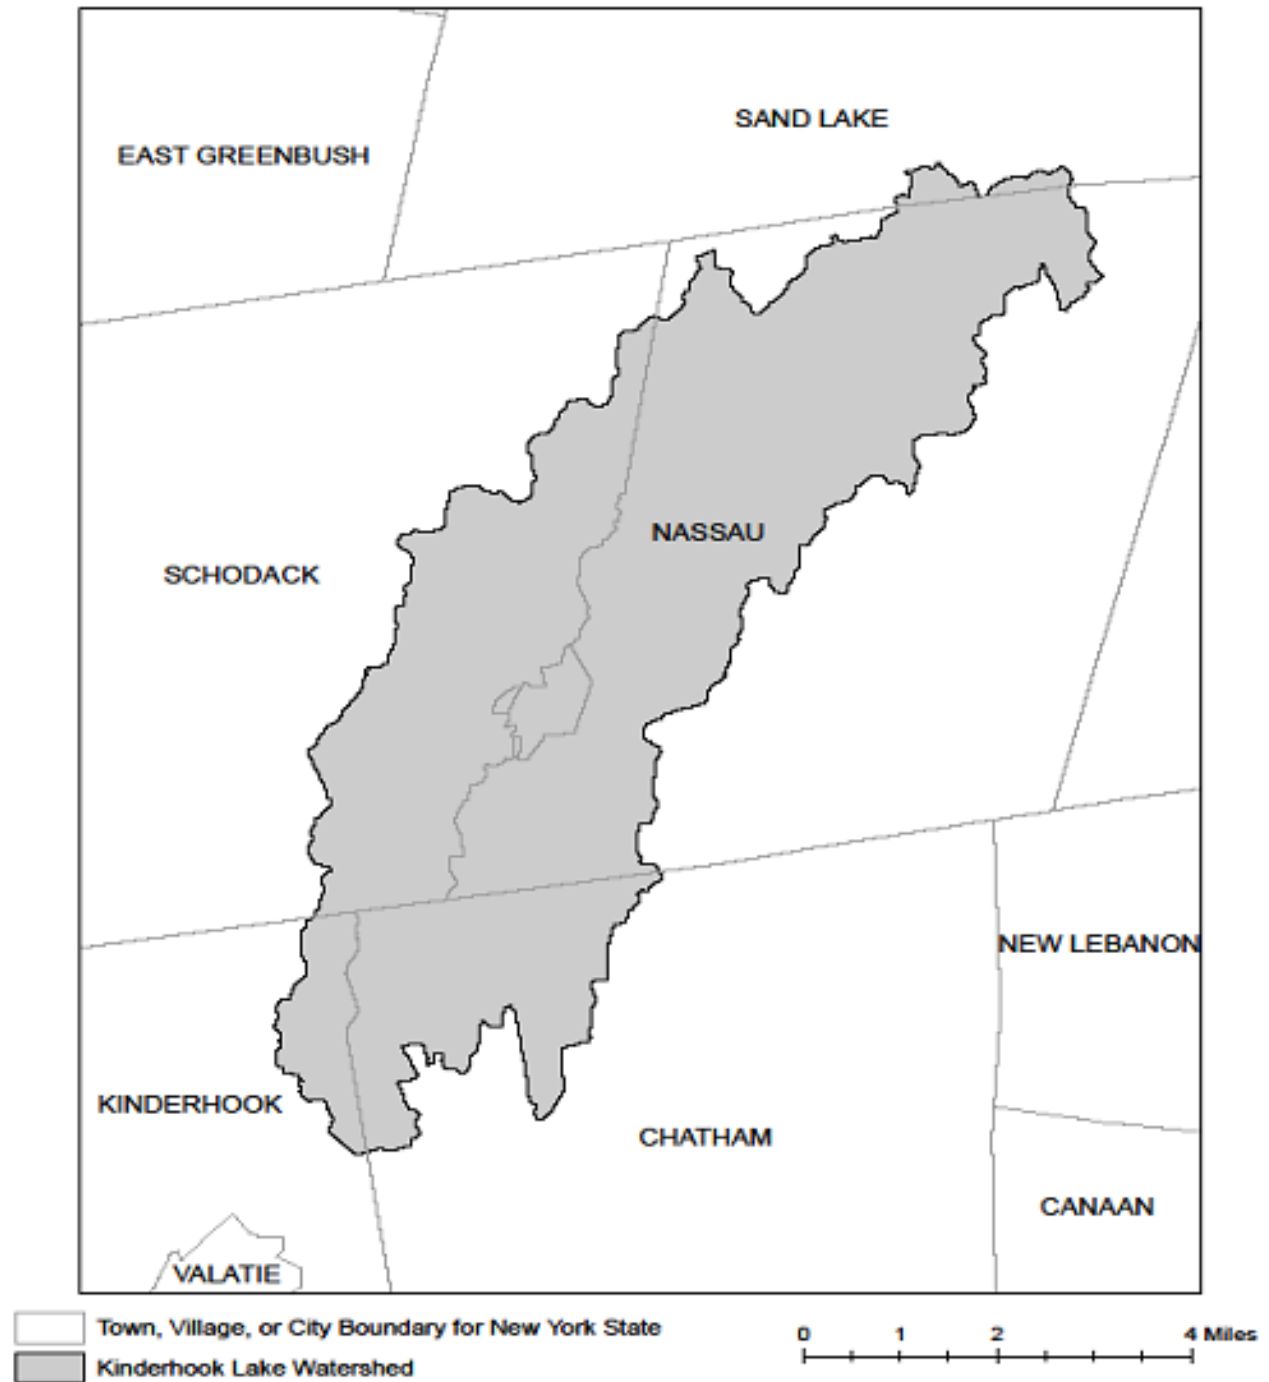

APPENDIX D – Impaired Waterbodies (by Construction Related Pollutants)

List of waterbodies impaired by *pollutants* related to *construction activity*, including turbidity, silt/sediment, and nutrients (e.g. nitrogen, phosphorus). This list is a subset of “The Final New York State 2018 Section 303(d) List of Impaired Waters Requiring a TMDL” dated June 2020.

County	Waterbody	Pollutant
Albany	Ann Lee (Shakers) Pond, Stump Pond (1201-0096)	Phosphorus
Albany	Lawsons Lake (1301-0235)	Phosphorus
Allegany	Amity Lake, Saunders Pond (0403-0054)	Phosphorus
Allegany	Andover Pond (0403-0056)	Phosphorus
Bronx	Reservoir No.1/Lake Isle (1702-0075)	Phosphorus
Bronx	Van Cortlandt Lake (1702-0008)	Phosphorus
Broome	Blueberry, Laurel Lakes (1404-0033)	Phosphorus
Broome	Fly Pond, Deer Lake (1404-0038)	Phosphorus
Broome	Minor Tribs to Lower Susquehanna (0603-0044)	Phosphorus
Broome	Whitney Point Lake/Reservoir (0602-0004)	Phosphorus
Cattaraugus	Allegheny River/Reservoir (0201-0023)	Phosphorus
Cattaraugus	Beaver Lake/Alma Pond (0201-0073)	Phosphorus
Cattaraugus	Case Lake (0201-0020)	Phosphorus
Cattaraugus	Linlyco/Club Pond (0201-0035)	Phosphorus
Cayuga	Duck Lake (0704-0025)	Phosphorus
Cayuga	Owasco Inlet, Upper, and tribs (0706-0014)	Nutrients
Chautauqua	Chadakoin River and tribs (0202-0018)	Phosphorus
Chautauqua	Hulburt/Clymer Pond (0202-0079)	Phosphorus
Chautauqua	Middle Cassadaga Lake (0202-0002)	Phosphorus
Clinton	Great Chazy River, Lower, Main Stem (1002-0001)	Silt/Sediment
Columbia	Robinson Pond (1308-0003)	Phosphorus
Cortland	Dean Pond (0602-0077)	Phosphorus
Dutchess	Fallkill Creek (1301-0087)	Phosphorus
Dutchess	Hillside Lake (1304-0001)	Phosphorus
Dutchess	Wappingers Lake (1305-0001)	Phosphorus
Dutchess	Wappingers Lake (1305-0001)	Silt/Sediment
Erie	Beeman Creek and tribs (0102-0030)	Phosphorus
Erie	Delaware Park Pond (0101-0026)	Phosphorus
Erie	Ellicott Creek, Lower, and tribs (0102-0018)	Phosphorus
Erie	Ellicott Creek, Lower, and tribs (0102-0018)	Silt/Sediment
Erie	Green Lake (0101-0038)	Phosphorus
Erie	Little Sister Creek, Lower, and tribs (0104-0045)	Phosphorus
Erie	Murder Creek, Lower, and tribs (0102-0031)	Phosphorus

Erie	Rush Creek and tribs (0104-0018)	Phosphorus
Erie	Scajaquada Creek, Lower, and tribs (0101-0023)	Phosphorus
Erie	Scajaquada Creek, Middle, and tribs (0101-0033)	Phosphorus
Erie	Scajaquada Creek, Upper, and tribs (0101-0034)	Phosphorus
Erie	South Branch Smoke Cr, Lower, and tribs (0101-0036)	Phosphorus
Erie	South Branch Smoke Cr, Lower, and tribs (0101-0036)	Silt/Sediment
Genesee	Bigelow Creek and tribs (0402-0016)	Phosphorus
Genesee	Black Creek, Middle, and minor tribs (0402-0028)	Phosphorus
Genesee	Black Creek, Upper, and minor tribs (0402-0048)	Phosphorus
Genesee	Bowen Brook and tribs (0102-0036)	Phosphorus
Genesee	LeRoy Reservoir (0402-0003)	Phosphorus
Genesee	Mill Pond (0402-0050)	Phosphorus
Genesee	Oak Orchard Cr, Upper, and tribs (0301-0014)	Phosphorus
Genesee	Oatka Creek, Middle, and minor tribs (0402-0031)	Phosphorus
Genesee	Tonawanda Cr, Middle, Main Stem (0102-0002)	Phosphorus
Greene	Schoharie Reservoir (1202-0012)	Silt/Sediment
Greene	Sleepy Hollow Lake (1301-0059)	Silt/Sediment
Herkimer	Steele Creek tribs (1201-0197)	Phosphorus
Herkimer	Steele Creek tribs (1201-0197)	Silt/Sediment
Kings	Hendrix Creek (1701-0006) 18	Nitrogen
Kings	Prospect Park Lake (1701-0196)	Phosphorus
Lewis	Mill Creek/South Branch, and tribs (0801-0200)	Nutrients
Livingston	Christie Creek and tribs (0402-0060)	Phosphorus
Livingston	Conesus Lake (0402-0004)	Phosphorus
Livingston	Mill Creek and minor tribs (0404-0011)	Silt/Sediment
Monroe	Black Creek, Lower, and minor tribs (0402-0033)	Phosphorus
Monroe	Buck Pond (0301-0017)	Phosphorus
Monroe	Cranberry Pond (0301-0016)	Phosphorus
Monroe	Durand, Eastman Lakes (0302-0037)	Phosphorus
Monroe	Lake Ontario Shoreline, Western (0301-0069) 9	Phosphorus
Monroe	Long Pond (0301-0015)	Phosphorus
Monroe	Mill Creek and tribs (0302-0025)	Phosphorus 2
Monroe	Mill Creek/Blue Pond Outlet and tribs (0402-0049)	Phosphorus
Monroe	Minor Tribs to Irondequoit Bay (0302-0038)	Phosphorus
Monroe	Rochester Embayment - East (0302-0002) [9]	Phosphorus
Monroe	Rochester Embayment - West (0301-0068) 9	Phosphorus
Monroe	Shipbuilders Creek and tribs (0302-0026)	Phosphorus 2
Monroe	Thomas Creek/White Brook and tribs (0302-0023)	Phosphorus

Nassau	Bannister Creek/Bay (1701-0380)	Nitrogen
Nassau	Beaver Lake (1702-0152)	Phosphorus
Nassau	Browswere Bay (1701-0383)	Nitrogen
Nassau	Camaans Pond (1701-0052)	Phosphorus
Nassau	East Meadow Brook, Upper, and tribs (1701-0211)	Silt/Sediment
Nassau	East Rockaway Channel (1701-0381)	Nitrogen
Nassau	Glen Cove Creek, Lower, and tribs (1702-0146)	Silt/Sediment
Nassau	Grant Park Pond (1701-0054)	Phosphorus
Nassau	Hempstead Bay, Broad Channel (1701-0032)	Nitrogen
Nassau	Hempstead Lake (1701-0015)	Phosphorus
Nassau	Hewlett Bay (1701-0382)	Nitrogen
Nassau	Hog Island Channel (1701-0220)	Nitrogen
Nassau	Massapequa Creek, Upper, and tribs (1701-0174)	Phosphorus
Nassau	Milburn/Parsonage Creeks, Upp, and tribs (1701-0212)	Phosphorus
Nassau	Reynolds Channel, East (1701-0215) [12]	Nitrogen
Nassau	Reynolds Channel, West (1701-0216) 12	Nitrogen
Nassau	Tidal Tribs to Hempstead Bay (1701-0218)	Nitrogen
Nassau	Tribs (fresh) to East Bay (1701-0204)	Silt/Sediment
Nassau	Tribs (fresh) to East Bay (1701-0204)	Phosphorus
Nassau	Tribs to Smith Pond/Halls Pond (1701-0221)	Phosphorus
Nassau	Woodmere Channel (1701-0219)	Nitrogen
New York	Harlem Meer (1702-0103)	Phosphorus
New York	The Lake in Central Park (1702-0105)	Phosphorus
Niagara	Bergholtz Creek and tribs (0101-0004)	Phosphorus
Niagara	Hyde Park Lake (0101-0030)	Phosphorus
Niagara	Lake Ontario Shoreline, Western (0301-0053) 9	Phosphorus
Niagara	Lake Ontario Shoreline, Western (0301-0072) 9	Phosphorus
Oneida	Ballou, Nail Creeks (1201-0203)	Phosphorus
Onondaga	Ley Creek and tribs (0702-0001) 10	Nutrients (phosphorus)
Onondaga	Minor Tribs to Onondaga Lake (0702-0022) 10	Nutrients (phosphorus)
Onondaga	Minor Tribs to Onondaga Lake (0702-0022) 10	Nitrogen (NH ₃ , NO ₂)
Onondaga	Onondaga Creek, Lower (0702-0023) 10	Nutrients (phosphorus)
Onondaga	Onondaga Creek, Lower, and tribs (0702-0023)	Turbidity
Onondaga	Onondaga Creek, Middle, and tribs (0702-0004)	Turbidity
Onondaga	Onondaga Creek, Upper, and tribs (0702-0024)	Turbidity
Ontario	Great Brook and minor tribs (0704-0034)	Phosphorus 2
Ontario	Great Brook and minor tribs (0704-0034)	Silt/Sediment

Ontario	Hemlock Lake Outlet and minor tribs (0402-0013)	Phosphorus
Ontario	Honeoye Lake (0402-0032)	Phosphorus
Orange	Brown Pond Reservoir (1303-0013)	Phosphorus
Orange	Lake Washington (1303-0012)	Phosphorus
Orange	Minor Tribs to Middle Wallkill (1306-0061)	Phosphorus
Orange	Monhagen Brook and tribs (1306-0074)	Phosphorus
Orange	Orange Lake (1301-0008) [16]	Phosphorus
Orange	Quaker Creek and tribs (1306-0025)	Phosphorus
Orange	Wallkill River, Middle, Main Stem (1306-0038)	Phosphorus
Orange	Wallkill River, Upper, and Minor tribs (1306-0017)	Phosphorus
Orleans	Glenwood Lake (0301-0041)	Phosphorus
Orleans	Lake Ontario Shoreline, Western (0301-0070) 9	Phosphorus
Orleans	Lake Ontario Shoreline, Western (0301-0071) 9	Phosphorus
Oswego	Lake Neatahwanta (0701-0018)	Nutrients (phosphorus)
Oswego	Pleasant Lake (0703-0047)	Phosphorus
Putnam	Lost Lake, Putnam Lake (1302-0053)	Phosphorus
Putnam	Minor Tribs to Croton Falls Reservoir (1302-0001)	Phosphorus
Queens	Bergen Basin (1701-0009) 18	Nitrogen
Queens	Jamaica Bay, Eastern, and tribs, Queens (1701-0005) 18	Nitrogen
Queens	Kissena Lake (1702-0258)	Phosphorus
Queens	Meadow Lake (1702-0030)	Phosphorus
Queens	Shellbank Basin (1701-0001) 18	Nitrogen
Queens	Willow Lake (1702-0031)	Phosphorus
Rensselaer	Nassau Lake (1310-0001)	Phosphorus
Rensselaer	Snyders Lake (1301-0043)	Phosphorus
Richmond	Grassmere Lake/Bradys Pond (1701-0357)	Phosphorus
Rockland	Congers Lake, Swartout Lake (1501-0019)	Phosphorus
Rockland	Rockland Lake (1501-0021)	Phosphorus
Saratoga	Ballston Lake (1101-0036)	Phosphorus
Saratoga	Dwaas Kill and tribs (1101-0007)	Phosphorus
Saratoga	Dwaas Kill and tribs (1101-0007)	Silt/Sediment
Saratoga	Lake Lonely (1101-0034)	Phosphorus
Saratoga	Round Lake (1101-0060)	Phosphorus
Saratoga	Tribs to Lake Lonely (1101-0001)	Phosphorus
Schenectady	Collins Lake (1201-0077)	Phosphorus
Schenectady	Duane Lake (1311-0006)	Phosphorus
Schenectady Lake	Mariaville Lake (1201-0113)	Phosphorus
Schuyler	Cayuta Lake (0603-0005)	Phosphorus

Seneca	Reeder Creek and tribs (0705-0074)	Phosphorus
St.Lawrence	Black Lake Outlet, Black Lake (0906-0001)	Phosphorus
St.Lawrence	Fish Creek and minor tribs (0906-0026)	Phosphorus
Steuben	Smith Pond (0502-0012)	Phosphorus
Suffolk	Agawam Lake (1701-0117)	Phosphorus
Suffolk	Big/Little Fresh Ponds (1701-0125)	Phosphorus
Suffolk	Canaan Lake (1701-0018)	Phosphorus
Suffolk	Canaan Lake (1701-0018)	Silt/Sediment
Suffolk	Fresh Pond (1701-0241)	Phosphorus
Suffolk	Great South Bay, East (1701-0039)	Nitrogen
Suffolk	Great South Bay, Middle (1701-0040)	Nitrogen
Suffolk	Great South Bay, West (1701-0173)	Nitrogen
Suffolk	Lake Ronkonkoma (1701-0020)	Phosphorus
Suffolk	Mattituck/Marratooka Pond (1701-0129)	Phosphorus
Suffolk	Mill and Seven Ponds (1701-0113)	Phosphorus
Suffolk	Millers Pond (1702-0013)	Phosphorus
Suffolk	Moriches Bay, East (1701-0305)	Nitrogen
Suffolk	Moriches Bay, West (1701-0038)	Nitrogen
Suffolk	Quantuck Bay (1701-0042)	Nitrogen
Suffolk	Shinnecock Bay and Inlet (1701-0033)	Nitrogen
Suffolk	Tidal Tribs to West Moriches Bay (1701-0312)	Nitrogen
Sullivan	Bodine, Montgomery Lakes (1401-0091)	Phosphorus
Sullivan	Davies Lake (1402-0047)	Phosphorus
Sullivan	Evens Lake (1402-0004)	Phosphorus
Sullivan	Pleasure Lake (1402-0055)	Phosphorus
Sullivan	Swan Lake (1401-0063)	Phosphorus
Tompkins	Cayuga Lake, Southern End (0705-0040)	Phosphorus
Tompkins	Cayuga Lake, Southern End (0705-0040)	Silt/Sediment
Ulster	Ashokan Reservoir (1307-0004)	Silt/Sediment
Ulster	Esopus Creek, Lower, Main Stem (1307-0010) [17]	Turbidity
Ulster	Esopus Creek, Middle, Main Stem (1307-0003) 17	Turbidity
Ulster	Esopus Creek, Upper, and minor tribs (1307-0007)[3]	Silt/Sediment
Ulster	Wallkill River, Lower, Main Stem (1306-0027)	Phosphorus
Warren	Hague Brook and tribs (1006-0006)	Silt/Sediment
Warren	Huddle/Finkle Brooks and tribs (1006-0003)	Silt/Sediment
Warren	Indian Brook and tribs (1006-0002)	Silt/Sediment
Warren	Lake George (1006-0016) and tribs	Silt/Sediment
Warren	Tribs to Lake George, East Shore (1006-0020)	Silt/Sediment
Warren	Tribs to Lake George, Lk.George Village (1006-0008)	Silt/Sediment

Washington	Wood Cr/Champlain Canal and tribs (1005-0036)	Phosphorus
Westchester	Lake Katonah (1302-0136)	Phosphorus
Westchester	Lake Lincolndale (1302-0089)	Phosphorus
Westchester	Lake Meahagh (1301-0053)	Phosphorus
Westchester	Lake Mohegan (1301-0149)	Phosphorus
Westchester	Lake Shenorock (1302-0083)	Phosphorus
Westchester	Mamaroneck River, Lower (1702-0071)	Silt/Sediment
Westchester	Mamaroneck River, Upp, & minor tribs (1702-0123)	Silt/Sediment
Westchester	Saw Mill River (1301-0007)	Phosphorus
Westchester	Saw Mill River, Middle, and tribs (1301-0100)	Phosphorus
Westchester	Sheldrake River (1702-0069)	Phosphorus
Westchester	Sheldrake River (1702-0069)	Silt/Sediment
Westchester	Silver Lake (1702-0040)	Phosphorus
Westchester	Teatown Lake (1302-0150)	Phosphorus
Westchester	Truesdale Lake (1302-0054)	Phosphorus
Westchester	Wallace Pond (1301-0140)	Phosphorus

APPENDIX E – List of NYSDEC Regional Offices

<u>Region</u>	<u>COVERING THE FOLLOWING COUNTIES:</u>	<u>DIVISION OF ENVIRONMENTAL PERMITS (DEP) PERMIT ADMINISTRATORS</u>	<u>DIVISION OF WATER (DOW) WATER (SPDES) PROGRAM</u>
1	NASSAU AND SUFFOLK	50 CIRCLE ROAD STONY BROOK, NY 11790 TEL. (631) 444-0365	50 CIRCLE ROAD STONY BROOK, NY 11790-3409 TEL. (631) 444-0405
2	BRONX, KINGS, NEW YORK, QUEENS AND RICHMOND	1 HUNTERS POINT PLAZA, 47-40 21ST ST. LONG ISLAND CITY, NY 11101-5407 TEL. (718) 482-4997	1 HUNTERS POINT PLAZA, 47-40 21ST ST. LONG ISLAND CITY, NY 11101-5407 TEL. (718) 482-4933
3	DUTCHESS, ORANGE, PUTNAM, ROCKLAND, SULLIVAN, ULSTER AND WESTCHESTER	21 SOUTH PUTT CORNERS ROAD NEW PALTZ, NY 12561-1696 TEL. (845) 256-3059	220 WHITE PLAINS ROAD, SUITE 110 TEL. (914) 428 - 2505
4	ALBANY, COLUMBIA, DELAWARE, GREENE, MONTGOMERY, OTSEGO, RENSSELAER, SCHENECTADY AND SCHOHARIE	1130 NORTH WESTCOTT ROAD SCHENECTADY, NY 12306-2014 TEL. (518) 357-2069	1130 NORTH WESTCOTT ROAD SCHENECTADY, NY 12306-2014 TEL. (518) 357-2045
5	CLINTON, ESSEX, FRANKLIN, FULTON, HAMILTON, SARATOGA, WARREN AND WASHINGTON	1115 STATE ROUTE 86, Po Box 296 RAY BROOK, NY 12977-0296 TEL. (518) 897-1234	232 GOLF COURSE ROAD WARRENSBURG, NY 12885-1172 TEL. (518) 623-1200
6	HERKIMER, JEFFERSON, LEWIS, ONEIDA AND ST. LAWRENCE	STATE OFFICE BUILDING 317 WASHINGTON STREET WATERTOWN, NY 13601-3787 TEL. (315) 785-2245	STATE OFFICE BUILDING 207 GENESEE STREET UTICA, NY 13501-2885 TEL. (315) 793-2554
7	BROOME, CAYUGA, CHENANGO, CORTLAND, MADISON, ONONDAGA, OSWEGO, TIOGA AND TOMPKINS	5786 WIDEWATERS PARKWAY SYRACUSE, NY 13214-1867 TEL. (315) 426-7438	5786 WIDEWATERS PARKWAY SYRACUSE, NY 13214-1867 TEL. (315) 426-7500
8	CHEMUNG, GENESEE, LIVINGSTON, MONROE, ONTARIO, ORLEANS, SCHUYLER, SENECA, STEUBEN, WAYNE AND YATES	6274 EAST AVON-LIMA ROADAVON, NY 14414-9519 TEL. (585) 226-2466	6274 EAST AVON-LIMA RD. AVON, NY 14414-9519 TEL. (585) 226-2466
9	ALLEGANY, CATTARAUGUS, CHAUTAUQUA, ERIE, NIAGARA AND WYOMING	700 DELAWARE AVENUE BUFFALO, NY 14209-2999 TEL. (716) 851-7165	700 DELAWARE AVENUE BUFFALO, NY 14209-2999 TEL. (716) 851-7070

APPENDIX F – SWPPP Preparer Certification Form

The SWPPP Preparer Certification Form required by this permit begins on the following page.



SWPPP Preparer Certification Form

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b., the completed form must be attached to the eNOI and submitted to NYSDEC electronically.)

Project/Site Name:

eNOI Submission ID:

Owner/Operator Name:

Certification Statement – SWPPP Preparer

I hereby certify that the Stormwater Pollution Prevention Plan (SWPPP) has been prepared in accordance with the requirements of GP-0-25-001. I certify under penalty of law that the SWPPP and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

SWPPP Preparer First Name

MI

SWPPP Preparer Last Name

Signature

Date

APPENDIX G – MS4 SWPPP Acceptance Form

The MS4 SWPPP Acceptance Form required by this permit begins on the following page.



Department of
Environmental
Conservation

MS4 SWPPP Acceptance Form

for construction activities seeking authorization under the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b., the completed form must be attached to the eNOI and submitted to NYSDEC electronically.)

I. Project Owner/Operator Information

1. Owner/Operator Name:

2. Contact Person:

3. Street Address:

4. City/State/Zip:

II. Project Site Information

5. Project/Site Name:

6. Street Address:

7. City/State/Zip:

III. Stormwater Pollution Prevention Plan (SWPPP) Review and Acceptance Information

8. SWPPP Reviewed by:

9. Title/Position:

10. Date Final SWPPP Reviewed and Accepted:

IV. Regulated MS4 Information

11. Name of MS4 Operator:

12. MS4 SPDES Permit Identification Number: NYR20A

13. Street Address:

14. City/State/Zip:

15. Telephone Number:

MS4 SWPPP Acceptance Form - continued

V. Certification Statement - MS4 Official (principal executive officer or ranking elected official) or Duly Authorized Representative

I hereby certify that the final Stormwater Pollution Prevention Plan (SWPPP) for the construction project identified in section II. of this form has been reviewed and meets the substantive requirements in the SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP). Note: The MS4 Operator, through the acceptance of the SWPPP, assumes no responsibility for the accuracy and adequacy of the design included in the SWPPP. In addition, review and acceptance of the SWPPP by the MS4 Operator does not relieve the owner/operator or their SWPPP preparer of responsibility or liability for errors or omissions in the plan.

Printed Name¹:

Title/Position:

Signature:

Date:

VI. Additional Information

¹ Printed name of the principal executive officer or ranking elected official for the MS4 Operator or their duly authorized representative in accordance with CGP Part VII.J.2.

APPENDIX H – NYCDEP SWPPP Acceptance/Approval Form

The City of New York Department of Environmental Protection (NYCDEP) SWPPP Acceptance/Approval form required by this permit begins on the following page.



THE CITY OF NEW YORK
DEPARTMENT OF ENVIRONMENTAL PROTECTION
Bureau of Environmental Planning and Analysis
59-17 Junction Blvd., 9th Floor; Flushing, NY 11373

SWPPP Acceptance/Approval

Application Number:

I. Project Owner/Operator Information

1. Owner/Operator Name:

2. Contact Person:

3. Street Address:

4. City/State/Zip:

II. Project Site Information

5. Project/Site Name:

6. Street Address:

7. City/State/Zip:

III. Stormwater Pollution Prevention Plan (SWPPP) Review and Acceptance/Approval

8. SWPPP Reviewed by:

9. Title/Position: /

10. Date Final SWPPP Reviewed and Accepted:

11. Acceptance/Approval Expiration Date:

IV. Regulated MS4 Information for projects that require coverage under the NY State Pollution Discharge Elimination System General Permit for Stormwater Discharges from Construction Activity

12. Name of MS4: *CITY OF NEW YORK*

13. MS4 SPDES Permit Identification Number: *NY-0287890*

14. Contact Person:

15. Street Address: *59-17 Junction Blvd. 9th Floor*

16. City/State/Zip: *Flushing, NY 11373*

17. Telephone Number:



Projects in the MS4 area must submit a copy of this SWPPP Acceptance with a Notice of Intent for coverage under the NY SPDES General Permit for Stormwater Discharges from Construction Activity to: NYS Department of Environmental Conservation, Division of Water; 625 Broadway, 4th Floor; Albany, New York 12233-3505.



THE CITY OF NEW YORK
DEPARTMENT OF ENVIRONMENTAL PROTECTION
Bureau of Environmental Planning and Analysis
59-17 Junction Blvd., 9th Floor; Flushing, NY 11373

V. Certification Statement - MS4 Official (principal executive officer or ranking elected official) or Duly Authorized Representative

I hereby certify that the final Stormwater Pollution Prevention Plan (SWPPP) for the construction project identified in question 5 has been reviewed and meets the substantive requirements in the SPDES General Permit For Stormwater Discharges from Municipal Separate Storm Sewer Systems (MS4s).

Note: The MS4, through the acceptance of the SWPPP, assumes no responsibility for the accuracy and adequacy of the design included in the SWPPP. In addition, review and acceptance of the SWPPP by the MS4 does not relieve the owner/operator or their SWPPP preparer of responsibility or liability for errors or omissions in the plan.

Printed Name:

Title/Position:

Signature:

Date:

VI. Conditions of Acceptance/Approval and Additional Information



Projects in the MS4 area must submit a copy of this SWPPP Acceptance with a Notice of Intent for coverage under the NY SPDES General Permit for Stormwater Discharges from Construction Activity to: NYS Department of Environmental Conservation, Division of Water; 625 Broadway, 4th Floor; Albany, New York 12233-3505.

APPENDIX I – MS4 No Jurisdiction Form

The MS4 No Jurisdiction Form required by this permit begins on the following page.



Department of
Environmental
Conservation

MS4 No Jurisdiction Form

for construction activities seeking authorization under the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b., the completed form must be attached to the eNOI and submitted to NYSDEC electronically.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. eNOI Submission ID:

III. Traditional Land Use Control MS4 Operator Information

- a. Name of MS4 Operator:
- b. MS4 SPDES Permit ID Number: NYR20A
- c. Street Address:
- d. City/State/Zip:
- e. Telephone Number:

IV. Certification Statement

In accordance with CGP Part I.D.2.b.ii.3., I hereby certify that the Traditional Land Use Control MS4 Operator identified in section III. of this form does not have review authority over the construction project identified in section II. of this form, which is owned/operated by the entity identified in section I. of this form. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the principal executive officer or ranking elected official for the MS4 Operator or their duly authorized representative in accordance with CGP Part VII.J.2.:
- b. Title/Position:
- c. Signature:
- d. Date:

APPENDIX J – Owner/Operator Certification Form

The Owner/Operator Certification Form required by this permit begins on the following page.



Owner/Operator Certification Form

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b. or Part I.F.2. and 3., the completed form must be attached to the eNOI or the Request to Continue Coverage, and submitted to NYSDEC electronically.)

Project/Site Name: _____

eNOI Submission ID: _____

eNOI Submitted by: ☐ Owner/Operator ☐ SWPPP Preparer ☐ Other

Certification Statement - Owner/Operator

I hereby certify that I read, and will comply with, the GP-0-25-001 permit requirements. I understand that authorization to discharge under the permit for the project/site named above is dependent on receipt of a Letter of Authorization (LOA) or a Letter of Continued Coverage (LOCC) from the New York State Department of Environmental Conservation (NYSDEC) in accordance with CGP Part I.D.3.b. or Part I.F.4. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Owner/Operator First Name

MI

Owner/Operator Last Name

Signature

Date

Appendix G

Construction Phase Inspection Report (Sample Form)

LANSING ENGINEERING, PC

WEEKLY SWPPP SITE INSPECTION REPORT

Project:
LE Project Number:
Contractor:
Inspector Name/Title:
NYR#:

Date and Time:
Temperature:
Ambient Conditions:
Soil Conditions:
LE SIMPL:

INSPECTION CHECKLIST

Record Keeping

Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐

- 1) Is the Notice of Intent and NOI Acknowledgement Letter retained at the construction site?
- 2) Is the MS4 Acceptance Form retained at the construction site?
- 3) Is a copy of the General Permit (GP-0-25-001) and SWPPP retained at the construction site?
- 4) Are all necessary contractor certifications signed and retained at the construction site?
- 5) Are SWPPP inspection reports signed and retained at the construction site?

Visual Observations

Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐
Yes	No	N/A
☐	☐	☐

- 6) Are there currently less than 5 acres of disturbed soils at the site?
- 7) Are natural resource areas (i.e. streams, surface waterbodies, wetlands, trees, etc.) protected with barriers or similar erosion and sediment controls?
- 8) Have permanent stormwater controls such as sediment basins and conveyance systems been constructed? (Not applicable during beginning phases of construction)
- 9) Were all stormwater discharges clear or the same as receiving waters on the day of inspection? This includes receiving waters, all conveyance systems (i.e. pipes, culverts, ditches, etc.) and overland flow. Please describe the quality and quantity at all points of discharge from the site and the condition of receiving waters.
- 10) Are catch basins/storm drain inlets properly protected?
- 11) Have vegetative or structural stabilization measures been implemented on all **active** areas where there are exposed soils?
- 12) Have vegetative or structural stabilization measures been implemented on all **inactive** areas where there are exposed soils?
- 13) Have vegetative or structural stabilization methods been implemented on slopes where there are exposed soils?
- 14) Have on-site vehicle tracking sediments and other eroded sediments been cleared?
- 15) Is the construction entrance preventing sediment from being tracked onto the street?
- 16) Are roads and properties adjacent to the construction site free of sediment and/or debris?
- 17) Is dust adequately controlled at the construction site?
- 18) Have all erosion and sediment controls been installed properly and are they functioning as designed?
- 19) Are all erosion and sediment controls being maintained to ensure integrity and effectiveness?
- 20) Have all post-construction erosion and sediment controls been constructed as designed? (Not applicable during beginning phases of construction)

Use this space below to explain each “NO” checked above, to provide additional comments, and to identify the following: all erosion and sediment controls that need installation, maintenance or replacement, any areas with rill or gully erosion on slopes, loss of vegetation, seed or mulch, excessive deposition of sediments or ponding water along diversion or barrier systems, and any areas of erosion near outlet or overflow structures in the sedimentation basin areas.

General Reminders:

- Please remember that all areas of disturbance should be stabilized as soon as possible unless work resumes, but in no case longer than 14 days.
- Please see map to correspond with comments and recommendations below.
- Please sweep Miller Road & Tisdale Lane as needed.
- Please add clean crushed stone to construction entrance as needed to prevent tracking of on-site sediments into adjacent roadways.
- In accordance with the NYSDEC Blue Book, please remember to stabilize all soils throughout site within 3 days from when disturbance activity has temporarily or permanently ceased. If straw mulch is used for temporary stabilization, it should be applied at 4 tons per acre. Rolled erosion control blankets should be used on all slopes 3:1v or steeper. Recommend stabilizing soil stockpiles as per the standard specifications for winter stabilization from the NYS Blue Book which states that soil stockpiles must be protected by the use of established vegetation, anchored straw mulch, rolled stabilization matting, or other durable covering. A barrier must be installed at least 15 feet from the toe of the stockpile to prevent soil migration and to capture loose soil.

Specific Comments:


1. Description
Timestamped Picture

Discharge Locations & Drainage Pathways (areas subject to change)

Location (see map)	Description	Discharge	Comments & Recommendations

Include a site map identifying the following:

- Stormwater discharge locations and drainage pathways
- Disturbed areas at the time of inspection
- Disturbed areas that have not undergone active site work during the previous 14 days
- Areas that are expected to undergo initial disturbance or significant work within the next 14-day period.
- Areas that have undergone temporary or permanent stabilization since last inspection
- Corrective actions that should be taken to install, repair, replace, or maintain erosion and sediment controls; and to correct deficiencies identified with the construction of post-construction management practices.
- The current phase of construction of all post-construction stormwater management practices and identification of all construction that is not in compliance with the SWPPP and/or technical standards.



CERTIFICATION

Lansing Engineering Qualified Inspector Signature: _____

Date: _____

Appendix H

MS4 Acceptance Form



Department of
Environmental
Conservation

MS4 SWPPP Acceptance Form

for construction activities seeking authorization under the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b., the completed form must be attached to the eNOI and submitted to NYSDEC electronically.)

I. Project Owner/Operator Information

1. Owner/Operator Name:

2. Contact Person:

3. Street Address:

4. City/State/Zip:

II. Project Site Information

5. Project/Site Name:

6. Street Address:

7. City/State/Zip:

III. Stormwater Pollution Prevention Plan (SWPPP) Review and Acceptance Information

8. SWPPP Reviewed by:

9. Title/Position:

10. Date Final SWPPP Reviewed and Accepted:

IV. Regulated MS4 Information

11. Name of MS4 Operator:

12. MS4 SPDES Permit Identification Number: NYR20A

13. Street Address:

14. City/State/Zip:

15. Telephone Number:

MS4 SWPPP Acceptance Form - continued

V. Certification Statement - MS4 Official (principal executive officer or ranking elected official) or Duly Authorized Representative

I hereby certify that the final Stormwater Pollution Prevention Plan (SWPPP) for the construction project identified in section II. of this form has been reviewed and meets the substantive requirements in the SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP). Note: The MS4 Operator, through the acceptance of the SWPPP, assumes no responsibility for the accuracy and adequacy of the design included in the SWPPP. In addition, review and acceptance of the SWPPP by the MS4 Operator does not relieve the owner/operator or their SWPPP preparer of responsibility or liability for errors or omissions in the plan.

Printed Name¹:

Title/Position:

Signature:

Date:

VI. Additional Information

¹ Printed name of the principal executive officer or ranking elected official for the MS4 Operator or their duly authorized representative in accordance with CGP Part VII.J.2.

Appendix I
Notice of Intent (NOI)

Appendix J

Notice of Termination (NOT) Documentation



Department of
Environmental
Conservation

eNOT Owner or Operator Certification

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Certification Statement

I certify that I have met the requirements of CGP Part V.A.1., 2., 3., and 4. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the Owner or Operator:
- b. Title/Position:
- c. Signature:
- d. Date:



Department of
Environmental
Conservation

eNOT Qualified Inspector Certification – SMPs

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Certification Statement

I hereby certify that all the requirements in CGP Part V.A.1.a.iv. or CGP Part V.A.1.b.iv. have been achieved. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the Qualified Inspector:
- b. Title/Position:
- c. Signature:
- d. Date:



Department of
Environmental
Conservation

eNOT Qualified Inspector Certification – Final Stabilization

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Certification Statement

I hereby certify that all the requirements in CGP Part V.A.1.a.i., ii., and iii. or CGP Part V.A.1.b.i., ii., and iii. have been achieved. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the Qualified Inspector:
- b. Title/Position:
- c. Signature:
- d. Date:



Department of
Environmental
Conservation

eNOT MS4 Acceptance

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Traditional Land Use Control MS4 Operator Information

- a. Name of MS4 Operator:
- b. MS4 SPDES Permit ID Number: NYR20A
- c. Street Address:
- d. City/State/Zip:
- e. Telephone Number:

IV. Certification Statement

I have determined that it is acceptable for the owner or operator of the construction project identified above to submit the electronic Notice of Termination in accordance with CGP Part V. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the principal executive officer or ranking elected official for the MS4 Operator or their duly authorized representative in accordance with CGP Part VII.J.2.:
- b. Title/Position:
- c. Signature:
- d. Date:



Appendix K

Deep Ripping and Decompaction



**New York State
DEPARTMENT OF ENVIRONMENTAL CONSERVATION**

Division of Water

Deep-Ripping and Decompaction

April 2008

**New York State
Department of Environmental Conservation**

Document Prepared by:

John E. Lacey,
Land Resource Consultant and Environmental Compliance Monitor
(Formerly with the Division of Agricultural Protection and Development Services,
NYS Dept. of Agriculture & Markets)

Alternative Stormwater Management Deep-Ripping and Decompaction

Description

The two-phase practice of 1) “Deep Ripping;” and 2) “Decompaction” (deep subsoiling), of the soil material as a step in the cleanup and restoration/landscaping of a construction site, helps mitigate the physically induced impacts of soil compression; i.e.: soil compaction or the substantial increase in the bulk density of the soil material.

Deep Ripping and Decompaction are key factors which help in restoring soil pore space and permeability for water infiltration. Conversely, the physical actions of cut-and-fill work, land grading, the ongoing movement of construction equipment and the transport of building materials throughout a site alter the architecture and structure of the soil, resulting in: the mixing of layers (horizons) of soil materials, compression of those materials and diminished soil porosity which, if left unchecked, severely impairs the soil’s water holding capacity and vertical drainage (rainfall infiltration), from the surface downward.

In a humid climate region, compaction damage on a site is virtually guaranteed over the duration of a project. Soil in very moist to wet condition when compacted, will have severely reduced permeability. Figure 1 displays the early stage of the deep-ripping phase (Note that all topsoil was stripped prior to construction access, and it remains stockpiled until the next phase – decompaction – is complete). A heavy-duty tractor is pulling a three-shank ripper on the first of several series of incrementally deepening passes through the construction access corridor's densely compressed subsoil material. Figure 2 illustrates the approximate volumetric composition of a loam surface soil when conditions are good for plant growth, with adequate natural pore space for fluctuating moisture conditions.



Fig. 1. A typical deep ripping phase of this practice, during the first in a series of progressively deeper “rips” through severely compressed subsoil.

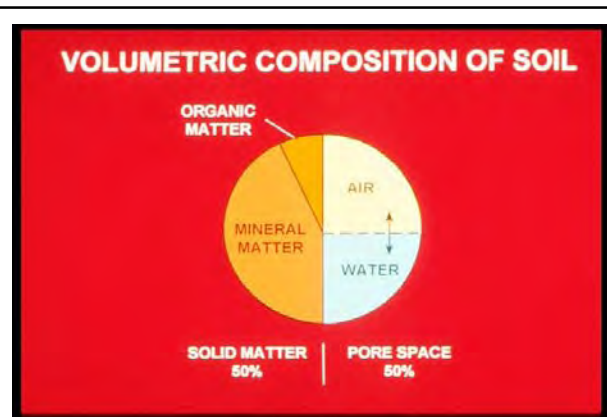


Fig. 2. About 50% of the volume of undisturbed loam surface soil is pore space, when soil is in good condition for plant growth. Brady, 2002.

Recommended Application of Practice

The objective of Deep Ripping and Decompaction is to effectively fracture (vertically and laterally) through the thickness of the physically compressed subsoil material (see Figure 3), restoring soil porosity and permeability and aiding infiltration to help reduce runoff. Together with topsoil stripping, the “two-phase” practice of Deep Ripping and Decompaction first became established as a “best management practice” through ongoing success on commercial farmlands affected by heavy utility construction right-of-way projects (transmission pipelines and large power lines).

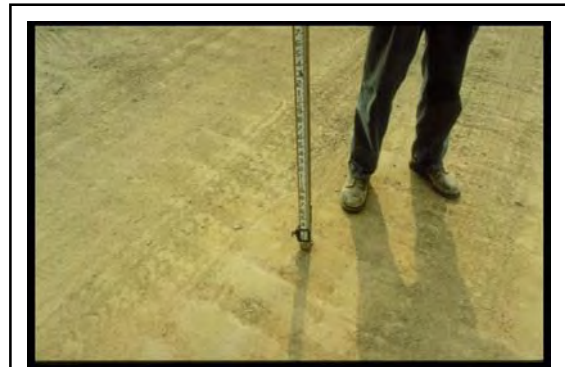


Fig. 3. Construction site with significant compaction of the deep basal till subsoil extends 24 inches below this exposed cut-and-fill work surface.

Soil permeability, soil drainage and cropland productivity were restored. For broader construction application, the two-phase practice of Deep Ripping and Decompaction is best adapted to areas impacted with significant soil compaction, on contiguous open portions of large construction sites and inside long, open construction corridors used as temporary access over the duration of construction. Each mitigation area should have minimal above-and-below-ground obstructions for the easy avoidance and maneuvering of a large tractor and ripping/decompacting implements. Conversely, the complete two-phase practice is not recommended in congested or obstructed areas due to the limitations on tractor and implement movement.

Benefits

Aggressive “deep ripping” through the compressed thickness of exposed subsoil before the replacement/respreading of the topsoil layer, followed by “decompaction,” i.e.: “sub-soiling,” through the restored topsoil layer down into the subsoil, offers the following benefits:

- Increases the project (larger size) area’s direct surface infiltration of rainfall by providing the open site’s mitigated soil condition and lowers the demand on concentrated runoff control structures
- Enhances direct groundwater recharge through greater dispersion across and through a broader surface than afforded by some runoff-control structural measures
- Decreases runoff volume generated and provides hydrologic source control
- May be planned for application in feasible open locations either alone or in

conjunction with plans for structural practices (e.g., subsurface drain line or infiltration basin) serving the same or contiguous areas

- Promotes successful long-term revegetation by restoring soil permeability, drainage and water holding capacity for healthy (rather than restricted) root-system development of trees, shrubs and deep rooted ground cover, minimizing plant drowning during wet periods and burnout during dry periods.

Feasibility / Limitations

The effectiveness of Deep Ripping and Decompaction is governed mostly by site factors such as: the original (undisturbed) soil's hydrologic characteristics; the general slope; local weather/timing (soil moisture) for implementation; the space-related freedom of equipment/implement maneuverability (noted above in **Recommended Application of Practice**), and by the proper selection and operation of tractor and implements (explained below in **Design Guidance**). The more notable site-related factors include:

Soil

In the undisturbed condition, each identified soil type comprising a site is grouped into one of four categories of soil hydrology, Hydrologic Soil Group A, B, C or D, determined primarily by a range of characteristics including soil texture, drainage capability when thoroughly wet, and depth to water table. The natural rates of infiltration and transmission of soil-water through the undisturbed soil layers for Group A is "high" with a low runoff potential while soils in Group B are moderate in infiltration and the transmission of soil-water with a moderate runoff potential, depending somewhat on slope. Soils in Group C have slow rates of infiltration and transmission of soil-water and a moderately high runoff potential influenced by soil texture and slope; while soils in Group D have exceptionally slow rates of infiltration and transmission of soil-water, and high runoff potential.

In Figure 4, the profile displays the undisturbed horizons of a soil in Hydrologic Soil Group C and the naturally slow rate of infiltration through the subsoil. The slow rate of infiltration begins immediately below the topsoil horizon (30 cm), due to the limited amount of macro pores, e.g.: natural subsoil fractures, worm holes and root channels. Infiltration after the construction-induced mixing and compression of such subsoil material is virtually absent; but can be restored back to this natural level with the two-phase practice of deep ripping and decompaction, followed by the permanent establishment of an appropriate, deep taproot

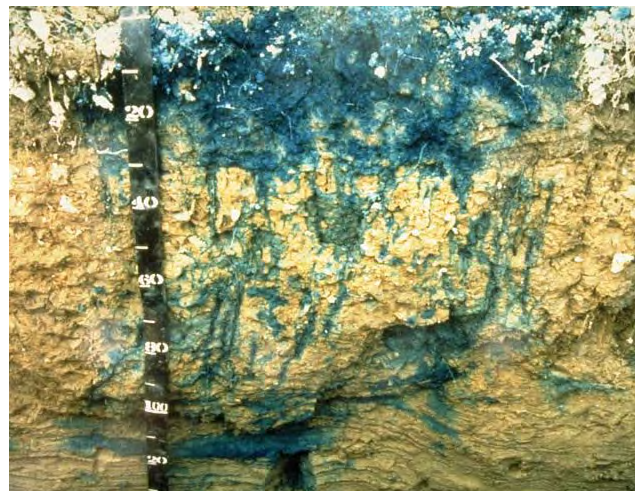


Fig. 4. Profile (in centimeters) displaying the infiltration test result of the natural undisturbed horizons of a soil in Hydrologic Soil Group C.

lawn/ground cover to help maintain the restored subsoil structure. Infiltration after construction-induced mixing and compression of such subsoil material can be notably rehabilitated with the Deep Ripping and Decompaction practice, which prepares the site for the appropriate long-term lawn/ground cover mix including deep taproot plants such as clover, fescue or trefoil, etc. needed for all rehabilitated soils.

Generally, soils in Hydrologic Soil Groups A and B, which respectively may include deep, well-drained, sandy-gravelly materials or deep, moderately well-drained basal till materials, are among the easier ones to restore permeability and infiltration, by deep ripping and decompaction. Among the many different soils in Hydrologic Soil Group C are those unique glacial tills having a natural fragipan zone, beginning about 12 to 18 inches (30 – 45cm), below surface. Although soils in Hydrologic Soil Group C do require a somewhat more carefully applied level of the Deep Ripping and Decompaction practice, it can greatly benefit such affected areas by reducing the runoff and fostering infiltration to a level equal to that of pre-disturbance.

Soils in Hydrologic Soil Group D typically have a permanent high water table close to the surface, influenced by a clay or other highly impervious layer of material. In many locations with clay subsoil material, the bulk density is so naturally high that heavy trafficking has little or no added impact on infiltration; and structural runoff control practices rather than Deep Ripping and Decompaction should be considered.

The information about Hydrologic Soil Groups is merely a general guideline. Site-specific data such as limited depths of cut-and-fill grading with minimal removal or translocation of the inherent subsoil materials (as analyzed in the county soil survey) or, conversely, the excavation and translocation of deeper, unconsolidated substratum or consolidated bedrock materials (unlike the analyzed subsoil horizons' materials referred to in the county soil survey) should always be taken into account.

Sites made up with significant quantities of large rocks, or having a very shallow depth to bedrock, are not conducive to deep ripping and decompaction (subsoiling); and other measures may be more practical.

Slope

The two-phase application of 1) deep ripping and 2) decompaction (deep subsoiling), is most practical on flat, gentle and moderate slopes. In some situations, such as but not limited to temporary construction access corridors, inclusion areas that are moderately steep along a project's otherwise gentle or moderate slope may also be deep ripped and decompacted. For limited instances of moderate steepness on other projects, however, the post-construction land use and the relative alignment of the potential ripping and decompaction work in relation to the lay of the slope should be reviewed for safety and practicality. In broad construction areas predominated by moderately steep or steep slopes, the practice is generally not used.

Local Weather/Timing/Soil Moisture

Effective fracturing of compressed subsoil material from the exposed work surface, laterally and vertically down through the affected zone is achieved only when the soil material is moderately dry to moderately moist. Neither one of the two-phases, deep ripping nor decompaction (deep

subsoiling), can be effectively conducted when the soil material (subsoil or replaced topsoil) is in either a “plastic” or “liquid” state of soil consistency. Pulling the respective implements legs through the soil when it is overly moist only results in the “slicing and smearing” of the material or added “squeezing and compression” instead of the necessary fracturing. Ample drying time is needed for a “rippable” soil condition not merely in the material close to the surface, but throughout the material located down to the bottom of the physically compressed zone of the subsoil.

The “poor man’s Atterberg field test” for soil plasticity is a simple “hand-roll” method used for quick, on-site determination of whether or not the moisture level of the affected soil material is low enough for: effective deep ripping of subsoil; respreading of topsoil in a friable state; and final decompaction (deep subsoiling). Using a sample of soil material obtained from the planned bottom depth of ripping, e.g.: 20 - 24 inches below exposed subsoil surface, the sample is hand rolled between the palms down to a 1/8-inch diameter thread. (Use the same test for stored topsoil material before respreading on the site.) If the respective soil sample crumbles apart in segments no greater than 3/8 of an inch long, by the time it is rolled down to 1/8 inch diameter, it is low enough in moisture for deep ripping (or topsoil replacement), and decompaction. Conversely, as shown in Figure 5, if the rolled sample stretches out in increments greater than 3/8 of an inch long before crumbling, it is in a “plastic” state of soil consistency and is too wet for subsoil ripping (as well as topsoil replacement) and final decompaction.

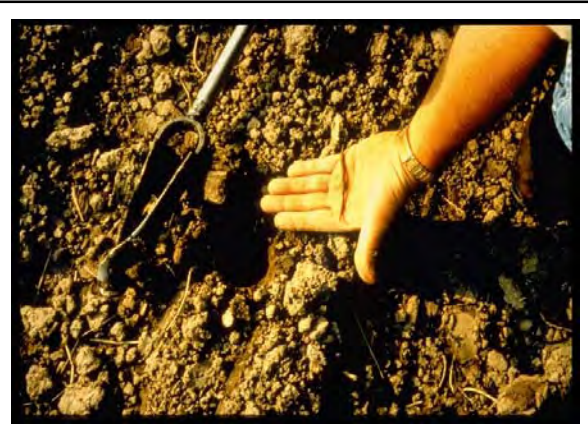


Fig. 5. Augered from a depth of 19 inches below the surface of the replaced topsoil, this subsoil sample was hand rolled to a 1/8-inch diameter. The test shows the soil at this site stretches out too far without crumbling; it indicates the material is in a plastic state of consistence, too wet for final decompaction (deep subsoiling) at this time.

Design Guidance

Beyond the above-noted site factors, a vital requirement for the effective Deep Ripping and Decompaction (deep subsoiling), is implementing the practice in its distinct, two-phase process:

- 1) Deep rip the affected thickness of exposed subsoil material (see Figure 10 and 11), aggressively fracturing it before the protected topsoil is reapplied on the site (see Figure 12); and
- 2) Decompact (deep subsoil), simultaneously through the restored topsoil layer and the upper half of the affected subsoil (Figure 13). The second phase, “decompaction,” mitigates the partial recompaction which occurs during the heavy process of topsoil spreading/grading. Prior to deep ripping and decompacting the site, all construction activity, including construction equipment and material storage, site cleanup and trafficking (Figure 14), should be finished; and the site closed off to further disturbance. Likewise, once the practice is underway and the area’s soil permeability and

rainfall infiltration are being restored, a policy limiting all further traffic to permanent travel lanes is maintained.

The other critical elements, outlined below, are: using the proper implements (deep, heavy-duty rippers and subsoilers), and ample pulling-power equipment (tractors); and conducting the practice at the appropriate speed, depth and pattern(s) of movement.

Note that an appropriate plan for the separate practice of establishing a healthy perennial ground cover, with deep rooting to help maintain the restored soil structure, should be developed in advance. This may require the assistance of an agronomist or landscape horticulturist.

Implements

Avoid the use of all undersize implements. The small-to-medium, light-duty tool will, at best, only “scarify” the uppermost surface portion of the mass of compacted subsoil material. The term “chisel plow” is commonly but incorrectly applied to a broad range of implements. While a few may be adapted for the moderate subsoiling of non-impacted soils, the majority are less durable and used for only lighter land-fitting (see Figure 6).



Fig. 6. A light duty chisel implement, not adequate for either the deep ripping or decompaction (deep subsoiling) phase.



Fig. 7. One of several variations of an agricultural ripper. This unit has long, rugged shanks mounted on a steel V-frame for deep, aggressive fracturing through Phase 1.

Use a “heavy duty” agricultural-grade, deep ripper (see Figures 7,9,10 and 11) for the first phase: the lateral and vertical fracturing of the mass of exposed and compressed subsoil, down and through, to the bottom of impact, prior to the replacement of the topsoil layer. (Any oversize rocks which are uplifted to the subsoil surface during the deep ripping phase are picked and removed.) Like the heavy-duty class of implement for the first phase, the decompaction (deep subsoiling) of Phase 2 is conducted with the heavy-duty version of the deep subsoiler. More preferable is the angled-leg variety of deep subsoiler (shown in Figures 8 and 13). It minimizes the inversion of the subsoil and topsoil layers while laterally and vertically fracturing the upper half of the previously ripped subsoil layer and all of the topsoil layer by delivering a momentary, wave-like “lifting and shattering” action up through the soil layers as it is pulled.

Pulling-Power of Equipment

Use the following rule of thumb for tractor horsepower (hp) whenever deep ripping and decompacting a significantly impacted site: For both types of implement, have at least 40 hp of tractor pull available for each mounted shank/ leg.

Using the examples of a 3-shank and a 5-shank implement, the respective tractors should have 120 and 200 hp available for fracturing down to the final depth of 20-to-24 inches per phase. Final depth for the deep ripping in Phase 1 is achieved incrementally by a progressive series of passes (see Depth and Patterns of Movement, below); while for Phase 2, the full operating depth of the deep subsoiler is applied from the beginning.

The operating speed for pulling both types of implement should not exceed 2 to 3 mph. At this slow and managed rate of operating speed, maximum functional performance is sustained by the tractor and the implement performing the soil fracturing. Referring to Figure 8, the implement is the 6-leg version of the deep angled-leg subsoiler. Its two outside legs are “chained up” so that only four legs will be engaged (at the maximum depth), requiring no less than 160 hp, (rather than 240 hp) of pull. The 4-wheel drive, articulated-frame tractor in Figure 8 is 174 hp. It will be decompacting this unobstructed, former construction access area simultaneously through 11 inches of replaced topsoil and the upper 12 inches of the previously deep-ripped subsoil. In constricted areas of Phase 1) Deep Ripping, a medium-size tractor with adequate hp, such as the one in Figure 9 pulling a 3-shank deep ripper, may be more maneuverable.

Some industrial-grade variations of ripping implements are attached to power graders and bulldozers. Although highly durable, they are generally not recommended. Typically, the shanks or “teeth” of these rippers are too short and stout; and they are mounted too far apart to achieve the well-distributed type of lateral and vertical fracturing of the soil materials necessary to restore soil permeability and infiltration. In addition, the power graders and bulldozers, as pullers, are far less maneuverable for turns and patterns than the tractor.



Fig. 8. A deep, angled-leg subsoiler, ideal for Phase 2 decompaction of after the topsoil layer is graded on top of the ripped subsoil.



Fig. 9. This medium tractor is pulling a 3-shank deep ripper. The severely compacted construction access corridor is narrow, and the 120 hp tractor is more maneuverable for Phase 1 deep ripping (subsoil fracturing), here.

Depth and Patterns of Movement

As previously noted both Phase 1 Deep Ripping through significantly compressed, exposed subsoil and Phase 2 Decomposition (deep subsoiling) through the replaced topsoil and upper subsoil need to be performed at maximum capable depth of each implement. With an implement's guide wheels attached, some have a "normal" maximum operating depth of 18 inches, while others may go deeper. In many situations, however, the tractor/implement operator must first remove the guide wheels and other non essential elements from the implement. This adapts the ripper or the deep subsoiler for skillful pulling with its frame only a few inches above surface, while the shanks or legs, fracture the soil material 20-to-24 inches deep.

There may be construction sites where the depth of the exposed subsoil's compression is moderate, e.g.: 12 inches, rather than deep. This can be verified by using a $\frac{3}{4}$ inch cone penetrometer and a shovel to test the subsoil for its level of compaction, incrementally, every three inches of increasing depth. Once the full thickness of the subsoil's compacted zone is finally "pieced" and there is a significant drop in the psi measurements of the soil penetrometer, the depth/thickness of compaction is determined. This is repeated at several representative locations of the construction site. If the thickness of the site's subsoil compaction is verified as, for example, ten inches, then the Phase 1 Deep Ripping can be correspondingly reduced to the implement's minimum operable depth of 12 inches. However, the Phase 2 simultaneous Decomposition (subsoiling) of an 11 inch thick layer of replaced topsoil and the upper subsoil should run at the subsoiling implements full operating depth.



Fig. 10. An early pass with a 3-shank deep ripper penetrating only 8 inches into this worksite's severely compressed subsoil.



Fig. 11. A repeat run of the 3-shank ripper along the same patterned pass area as Fig. 9; here, incrementally reaching 18 of the needed 22 inches of subsoil fracture.

Typically, three separate series (patterns) are used for both the Phase 1 Deep Ripping and the Phase 2 Decomposition on significantly compacted sites. For Phase 1, each series begins with a moderate depth of rip and, by repeat-pass, continues until full depth is reached. Phase 2 applies the full depth of Decomposition (subsoiling), from the beginning.

Every separate series (pattern) consists of parallel, forward-and-return runs, with each progressive

pass of the implement's legs or shanks evenly staggered between those from the previous pass. This compensates for the shank or leg-spacing on the implement, e.g., with 24-to-30 inches between each shank or leg. The staggered return pass ensures lateral and vertical fracturing actuated every 12 to 15 inches across the densely compressed soil mass.

Large, Unobstructed Areas

For larger easy areas, use the standard patterns of movement:

- The first series (pattern) of passes is applied lengthwise, parallel with the longest spread of the site; gradually progressing across the site's width, with each successive pass.
- The second series runs obliquely, crossing the first series at an angle of about 45 degrees.
- The third series runs at right angle (or 90 degrees), to the first series to complete the fracturing and shattering on severely compacted sites, and avoid leaving large unbroken blocks of compressed soil material. (In certain instances, the third series may be optional, depending on how thoroughly the first two series loosen the material and eliminate large chunks/blocks of material as verified by tests with a $\frac{3}{4}$ -inch cone penetrometer.)



Fig. 12. Moderately dry topsoil is being replaced on the affected site now that Phase 1 deep ripping of the compressed subsoil is complete.



Fig. 13. The same deep, angled-leg subsoiler shown in Fig. 7 is engaged at maximum depth for Phase 2, decompaction (deep soiling), of the replaced topsoil and the upper subsoil materials.

Corridors

In long corridors of limited width and less maneuverability than larger sites, e.g.: along compacted areas used as temporary construction access, a modified series of pattern passes are used.

- First, apply the same initial lengthwise, parallel series of passes described above.

- A second series of passes makes a broad “S” shaped pattern of rips, continually and gradually alternating the “S” curves between opposite edges inside the compacted corridor.
- The third and final series again uses the broad, alternating S pattern, but it is “flip-flopped” to continually cross the previous S pattern along the corridor’s centerline. This final series of the S pattern curves back along the edge areas skipped by the second series.

Maintenance and Cost

Once the two-phase practice of Deep Ripping and Decomposition is completed, two items are essential for maintaining a site’s soil porosity and permeability for infiltration. They are: planting and maintaining the appropriate ground cover with deep roots to maintain the soil structure (see Figure 15); and keeping the site free of traffic or other weight loads.

Note that site-specific choice of an appropriate vegetative ground-cover seed mix, including the proper seeding ratio of one or more perennial species with a deep taproot system and the proper amount of lime and soil nutrients (fertilizer mix) adapted to the soil-needs, are basic to the final practice of landscaping, i.e: surface tillage, seeding/planting/fertilizing and culti-packing or mulching is applied. The "maintenance" of an effectively deep-ripped and decompacted area is generally limited to the successful perennial (long-term) landscape ground cover; as long as no weight-bearing force of soil compaction is applied.



Fig. 14. The severely compacted soil of a temporary construction yard used daily by heavy equipment for four months; shown before deep ripping, topsoil replacement, and decompaction.



Fig. 15. The same site as Fig. 14 after deep ripping of the exposed subsoil, topsoil replacement, decompaction through the topsoil and upper subsoil and final surface tillage and revegetation to maintain soil permeability and infiltration.

The Deep Ripping and Decompaction practice is, by necessity, more extensive than periodic subsoiling of farmland. The cost of deep ripping and decompacting (deep subsoiling), will vary according to the depth and severity of soil-material compression and the relative amount of tractor and implement time that is required. In some instances, depending on open maneuverability, two-to-three acres of compacted project area may be deep-ripped in one day. In other situations of more severe compaction and - or less maneuverability, as little as one acre may be fully ripped in a day. Generally, if the Phase 1) Deep Ripping is fully effective, the Phase 2) Decompaction should be completed in $\frac{2}{3}$ to $\frac{3}{4}$ of the time required for Phase 1.

Using the example of two acres of Phase 1) Deep Ripping in one day, at \$1800 per day, the net cost is \$900 per acre. If the Phase 2) Decompacting or deep subsoiling takes $\frac{3}{4}$ the time as Phase 1, it costs \$675 per acre for a combined total of \$1575 per acre to complete the practice (these figures do not include the cost of the separate practice of topsoil stripping and replacement). Due to the many variables, it must be recognized that cost will be determined by the specific conditions or constraints of the site and the availability of proper equipment.

Resources

Publications:


- American Society of Agricultural Engineers. 1971. *Compaction of Agricultural Soils*. ASAE.
- Brady, N.C., and R.R. Weil. 2002. *The Nature and Properties of Soils*. 13th ed. Pearson Education, Inc.
- Baver, L.D. 1948. *Soil Physics*. John Wiley & Sons.
- Carpachi, N. 1987 (1995 fifth printing). *Excavation and Grading Handbook, Revised*. 2nd ed. Craftsman Book Company
- Ellis, B. (Editor). 1997. *Safe & Easy Lawn Care: The Complete Guide to Organic Low Maintenance Lawn*. Houghton Mifflin.
- Harpstead, M.I., T.J. Sauer, and W.F. Bennett. 2001. *Soil Science Simplified*. 4th ed. Iowa State University Press.
- Magdoff, F., and H. van Es. 2000. *Building Soils for Better Crops*. 2nd ed. Sustainable Agricultural Networks
- McCarthy, D.F. 1993. *Essentials of Soil Mechanics and Foundations, Basic Geotechnics* 4th ed. Regents/Prentice Hall.
- Plaster, E.J. 1992. *Soil Science & Management*. 3rd ed. Delmar Publishers.
- Union Gas Limited, Ontario, Canada. 1984. *Rehabilitation of Agricultural Lands, Dawn-Kerwood Loop Pipeline; Technical Report*. Ecological Services for Planning, Ltd.; Robinson, Merritt & Devries, Ltd. and Smith, Hoffman Associates, Ltd.
- US Department of Agriculture in cooperation with Cornell University Agricultural Experiment Station. Various years. *Soil Survey of (various names) County, New York*. USDA.

Internet Access:

- Examples of implements:
V-Rippers. Access by internet search of *John Deere Ag -New Equipment for 915* (larger-frame model) *V-Ripper*; and, *for 913* (smaller-frame model) *V-Ripper*. Deep, angled-leg subsoiler. Access by internet search of: *Bigham Brothers Shear Bolt Paratill-Subsoiler*.
http://salesmanual.deere.com/sales/salesmanual/en_NA/primary_tillage/2008/feature/rippers/915v_pattern_frame.html?sbu=ag&link=prodcut Last visited March 08.
- Soils data of USDA Natural Resources Conservation Service. NRCS Web Soil Survey. <http://websoilsurvey.nrcs.usda.gov/app/> and *USDA-NRCS Official Soil Series Descriptions; View by Name*. <http://ortho.ftw.nrcs.usda.gov/cgi-bin/osd/osdname.cgi> . Last visited Jan. 08.
- Soil penetrometer information. Access by internet searches of: *Diagnosing Soil Compaction using a Penetrometer (soil compaction tester)*, PSU Extension; as well as *Dickey-john Soil Compaction Tester*.
<http://www.dickey-johnproducts.com/pdf/SoilCompactionTest.pdf> and <http://cropsoil.psu.edu/Extension/Facts/uc178pdf> Last visited Sept. 07

Appendix L

Permit Eligibility

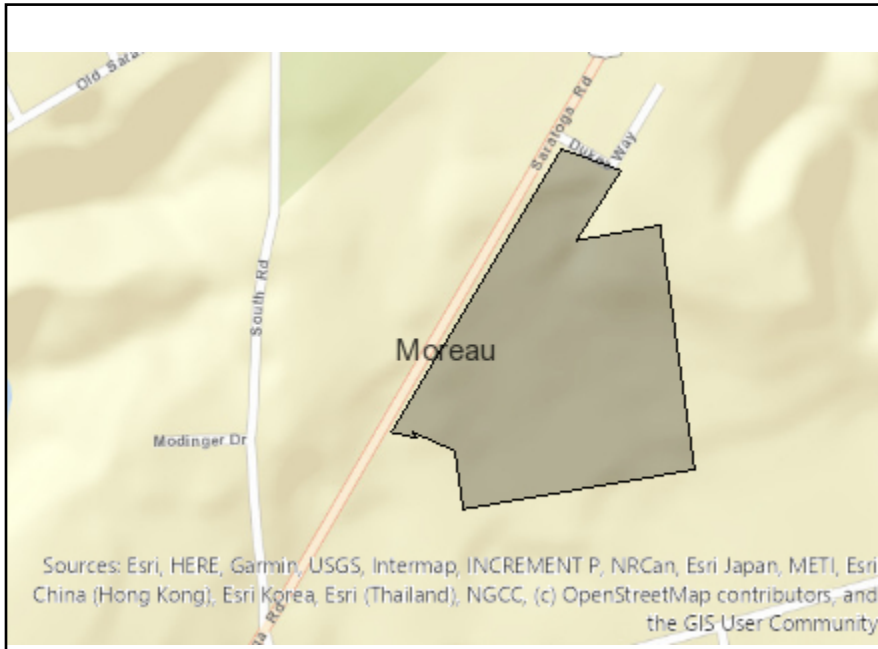

Disclaimer: The EAF Mapper is a screening tool intended to assist project sponsors and reviewing agencies in preparing an environmental assessment form (EAF). Not all questions asked in the EAF are answered by the EAF Mapper. Additional information on any EAF question can be obtained by consulting the EAF Workbooks. Although the EAF Mapper provides the most up-to-date digital data available to DEC, you may also need to contact local or other data sources to confirm data provided by the Mapper or to obtain data not provided by the Mapper.



B.i.i [Coastal or Waterfront Area]	No
B.i.ii [Local Waterfront Revitalization Area]	No
C.2.b. [Special Planning District]	Yes - Digital mapping data are not available for all Special Planning Districts. Refer to EAF Workbook.
C.2.b. [Special Planning District - Name]	NYS Heritage Areas: Mohawk Valley Heritage Corridor
E.1.h [DEC Spills or Remediation Site - Potential Contamination History]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.1.h.i [DEC Spills or Remediation Site - Listed]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.1.h.i [DEC Spills or Remediation Site - Environmental Site Remediation Database]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.1.h.iii [Within 2,000' of DEC Remediation Site]	No
E.2.g [Unique Geologic Features]	No
E.2.h.i [Surface Water Features]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.h.ii [Surface Water Features]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.h.iii [Surface Water Features]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.h.v [Impaired Water Bodies]	No
E.2.i. [Floodway]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.j. [100 Year Floodplain]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.k. [500 Year Floodplain]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.l. [Aquifers]	No

E.2.n. [Natural Communities]	No
E.2.o. [Endangered or Threatened Species]	No
E.2.p. [Rare Plants or Animals]	No
E.3.a. [Agricultural District]	No
E.3.c. [National Natural Landmark]	No
E.3.d [Critical Environmental Area]	No
E.3.e. [National or State Register of Historic Places or State Eligible Sites]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.3.f. [Archeological Sites]	Yes
E.3.i. [Designated River Corridor]	No
E.4.a [Disadvantaged Community]	No
